



NORTH

CONSTRUCTION SEQUENCING:

1. INSTALL CONCRETE WASHOUTS AS NEEDED. IF NECESSARY CALCIUM CHLORIDE CAN ALSO BE UTILIZED.
2. CONSTRUCT FOUNDATION FOOTING/PILE CAP CONSTRUCTION. BACKFILL AS COMPLETED.
3. CONSTRUCT INTERIOR FOUNDATIONS.
4. CONSTRUCT INTERIOR UNDER-SLAB PLUMBING.
5. BRING BUILDING PAD TO SLAB SUBGRADE.

GENERAL NOTES:

1. DUST SHALL BE KEPT TO A MINIMUM. THE SITE SUBCONTRACTOR SHALL SPRAY WATER FOR DUST CONTROL. IF NECESSARY CALCIUM CHLORIDE CAN ALSO BE UTILIZED.
2. VIBRATION MONITORING SHALL BE IMPLEMENTED FOR ADJACENT STRUCTURES BY SEISMOGRAPHS RECORDINGS DURING ANY PILE DRIVING. A POST-MONITORING REPORT SHALL BE GENERATED.
3. NOISES CREATED BY CONSTRUCTION AND MAINTENANCE ACTIVITIES BETWEEN 7:30 AM AND 10:00 PM ARE EXEMPT FROM THE MAXIMUM PERMISSIBLE SOUND LEVELS SET FORTH IN SUBSECTION (b)(3) OF PERFORMANCE STANDARDS SECTION 14-230.5.
4. THE HOURS OF CONSTRUCTION ARE 7:00 A.M. TO 7:00 P.M. HOWEVER, IF IT IS NECESSARY TO PERFORM CONSTRUCTION ACTIVITIES OUTSIDE THE AFORESAID HOURS, THE GENERAL CONTRACTOR SHALL REQUEST PERMISSION FROM THE DEPARTMENT OF PUBLIC SERVICES AND ANY NOISE BETWEEN THE HOURS OF 10:00 PM OF ONE (1) DAY AND 7:00 AM OF THE FOLLOWING DAY SHALL NOT EXCEED (55) dBA.
5. THE GENERAL CONTRACTOR SHALL CONTACT IN ADVANCE THE ADJACENT LAND OWNERS BY EMAIL, TELEPHONE, OR IN PERSON TO NOTIFY OF ANY ACTIVITIES THAT MAY HAVE ADVERSE IMPACTS ON THEM.
6. KNOX LOCKS SHALL BE INSTALLED ON ALL GATES TO ALLOW THE FIRE DEPARTMENT ACCESS TO THE SITE.
7. SITEWORK CONSTRUCTION VEHICLES SHALL EXIT THE STABILIZED CONSTRUCTION ENTRANCE ON FORE STREET.
8. SIDEWALK SNOW REMOVAL SHALL BE THE RESPONSIBILITY OF THE PROPERTY OWNER ALONG THEIR STREET FRONTAGE.
9. PROJECT DELIVERIES SHALL NOT BE SCHEDULED DURING PEAK TRAFFIC TIMES: MON THROUGH FRIDAY, 7-9AM AND 4-6PM.



MUTCD M4-9b

TEMPORARY PEDESTRIAN SIGN
(MUTCD M4-9b, POINTING LEFT)

TEMPORARY PEDESTRIAN SIGN
(MUTCD M4-9b, POINTING RIGHT)

FOUNDATIONS TO START
AT THIS END OF BUILDING


TEMPORARY STABILIZED
CONSTRUCTION ENTRANCE

CONSTRUCTION PARKING

CONCRETE WASHOUT
TO BE WITHIN THE
BUILDING FOOT PRINT

TEMPORARY FENCING
ALONG CURB LINE

JOB SITE
TRAILER

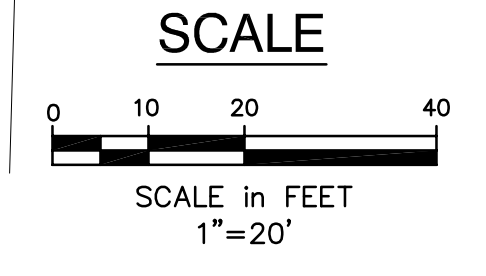

**PROPOSED AC HOTEL
PORTLAND**

FORE STREET /
HANCOCK STREET /
THAMES STREET
PORTLAND, MAINE

PORTLAND NORWICH GROUP, LLC.
2330 PALM RIDGE ROAD #305
SANIBEL, FLORIDA 33957



11 CORPORATE DRIVE ■ BELMONT ■ NH 03220
PHONE (603) 527-9090 ■ WWW.OPECHEE.COM

**CONSTRUCTION
MANAGEMENT
FOUNDATIONS**

No.	Revision/Issue	Date

150.06094 09/09/16

CM2
