### 1.3.5 EROSION CONTROL MEASURES AND SITE STABILIZATION

- THE PRIMARY EMPHASIS OF THE EROSION/SEDIMENTATION CONTROL PLAN, WHICH WILL BE IMPLEMENTED FOR THIS PROJECT, IS AS FOLLOWS
- DEVELOPMENT OF A CAREFUL CONSTRUCTION SEQUENCE. \* RAPID REVEGETATION OF DENUDED AREAS TO MINIMIZE THE PERIOD OF SOIL EXPOSURE.
- RAPID STABILIZATION OF DRAINAGE PATHS TO AVOID RILL AND GULLY EROSION.
- THE USE OF ON-SITE MEASURES TO CAPTURE SEDIMENT (HAY BALES/ STONE CHECK DAMS/SILT FENCE, ETC.)
- THE FOLLOWING TEMPORARY AND PERMANENT EROSION AND SEDIMENT CONTROL DEVICES WILL BE IMPLEMENTED AS PART OF THE SITE DEVELOPMENT. THESE DEVICES SHALL BE INSTALLED AS INDICATED ON THE PLANS OR AS DESCRIBED WITHIN THIS REPORT. FOR FURTHER REFERENCE, SEE THE LATEST EDITION OF THE MAINE EROSION AND SEDIMENT CONTROL BMPS.
- A. DEWATERING AND TEMPORARY STREAM DIVERSION
- STRUCTURE (E.G. HAY BALE LINED POOL) PRIOR TO DISCHARGE. THE DISCHARGE SITE SHALL BE SELECTED TO AVOID FLOODING, ICING, AND SEDIMENT DISCHARGES TO A PROTECTED RESOURCE. IN NO CASE SHALL THE FILTER BAG OR CONTAINMENT STRUCTURE BE LOCATED WITHIN 50 FEET OF A PROTECTED NATURAL

WATER FROM CONSTRUCTION TRENCH DEWATERING OR TEMPORARY STREAM DIVERSION SHALL PASS FIRST THROUGH A FILTER BAG OR SECONDARY CONTAINMENT

#### B. INSPECTION AND MONITORING

MAINTENANCE MEASURES SHALL BE APPLIED AS NEEDED DURING THE ENTIRE CONSTRUCTION SEASON. AFTER EACH RAINFALL, SNOW STORM OR PERIOD OF THAWING AND RUNOFF, THE SITE CONTRACTOR SHALL PERFORM A VISUAL INSPECTION OF ALL INSTALLED EROSION CONTROL MEASURES AND PERFORM REPAIRS AS NEEDED TO INSURE THEIR CONTINUOUS FUNCTION. FOLLOWING THE TEMPORARY AND/OR FINAL SEEDING AND MULCHING, THE CONTRACTOR SHALL IN THE SPRING INSPECT AND REPAIR ANY DAMAGES AND/OR UNESTABLISHED SPOTS. ESTABLISHED VEGETATIVE COVER MEANS A MINIMUM OF 90% OF AREAS VEGETATED WITH VIGOROUS GROWTH

- THE FOLLOWING MEASURES ARE PLANNED AS TEMPORARY EROSION/SEDIMENTATION CONTROL MEASURES DURING CONSTRUCTION:
- 1. CRUSHED STONE-STABILIZED CONSTRUCTION ENTRANCE SHALL BE PLACED AT THE ACCESS DRIVE TO THE PROJECT SITE ALONG ALLEN AVENUE. INSTALL CONSTRUCTION ENTRANCE ONLY AS NECESSARY WHEN PAVEMENT IS REMOVED.
- 2. SILTATION FENCE OR WOOD WASTE COMPOST BERMS SHALL BE INSTALLED DOWNSTREAM OF ANY DISTURBED AREAS TO TRAP RUNOFF BORNE SEDIMENTS UNTIL GRASS AREAS ARE REVEGETATED. THE SILT FENCE AND/OR WOOD WASTE COMPOST BERMS SHALL BE INSTALLED PER THE DETAILS PROVIDED IN THIS PACKAGE AND INSPECTED AT LEAST ONCE A WEEK AND BEFORE AND IMMEDIATELY AFTER A STORM EVENT OF 0.5 INCHES OR GREATER, AND AT LEAST DAILY DURING PROLONGED RAINFALL. REPAIRS SHALL BE MADE IF THERE ARE ANY SIGNS OF EROSION OR SEDIMENTATION BELOW THE FENCE OR BERM LINE. IF THERE ARE SIGNS OF UNDERCUTTING AT THE CENTER OR THE EDGES, OR IMPOUNDING OF LARGE VOLUMES OF WATER BEHIND THE FENCE OR BERM, THE BARRIER SHALL BE REPLACED WITH A STONE CHECK DAM. WOOD WASTE COMPOST BERMS ARE NOT TO BE USED ADJACENT TO WETLAND AREAS THAT ARE NOT TO BE DISTURBED.
- 3. STRAW OR HAY MULCH INCLUDING HYDROSEEDING IS INTENDED TO PROVIDE COVER FOR DENUDED OR SEEDED AREAS UNTIL REVEGETATION IS ESTABLISHED.
  MULCH PLACED BETWEEN APRIL 15TH AND OCTOBER 15TH ON SLOPES OF LESS THEN 15 PERCENT SHALL BE ANCHORED BY APPLYING WATER; MULCH PLACED ON SLOPES OF EQUAL TO OR STEEPER THAN 15 PERCENT SHALL BE COVERED BY A FABRIC NETTING AND ANCHORED WITH STAPLES IN ACCORDANCE WITH MANUFACTURER'S RECOMMENDATION. FABRIC NETTING AND STAPLES SHALL BE USED ON DISTURBED AREAS WITHIN 50' OF LAKES, STREAMS, AND WETLANDS RE COVERED WITH A FARRIC NETTING AND ANCHORED WITH STAPLES IN ACCORDANCE WITH THE MANUFACTURER'S RECOMMENDATIONS. SLOPES STEEPER THAN 1 AND EQUAL TO OR FLATTER THAN 2:1, WHICH ARE TO BE REVEGETATED, SHALL RECEIVE CURLEX BLANKETS BY AMERICAN EXCELSIOR OR EQUAL. SLOPES STEEPER THAN 2:1 SHALL RECEIVE RIPRAP AS NOTED ON THE PLANS. THE MULCH APPLICATION RATE FOR BOTH TEMPORARY AND PERMANENT SEEDING IS 75 LBS PER 1000 SF AS IDENTIFIED IN ATTACHMENT A OF THIS SECTION. MULCH SHALL NOT BE PLACED OVER SNOW.
- 4. TEMPORARY STOCKPILES OF STUMPS, GRUBBINGS, OR COMMON EXCAVATION WILL BE PROTECTED AS FOLLOWS:
- d) TEMPORARY STOCKPILES SHALL NOT BE LOCATED WITHIN 100 FEET OF ANY WETLANDS WHICH WILL NOT BE DISTURBED AND LOCATED AWAY FROM DRAINAGE
- b) STOCKPILES SHALL BE STABILIZED WITHIN 7 DAYS BY FITHER TEMPORARILY SEEDING THE STOCKPILE BY A HYDROSEED METHOD CONTAINING AN EMULSIFIED c) STOCKPILES SHALL BE SURROUNDED BY SEDIMENTATION BARRIER AT THE TIME OF FORMATION
- 5. ALL DENUDED AREAS THAT ARE WITHIN 100 FEET OF AN UNDISTURBED WETLAND, WHICH HAVE BEEN ROUGH GRADED AND ARE NOT LOCATED WITHIN A BUILDING PAD, PARKING AREA, OR ACCESS DRIVE SUBBASE AREA, SHALL RECEIVE MULCH OR EROSION CONTROL MESH FABRIC WITHIN 48 HOURS OF INITIAL DISTURBANCE OF SOIL. ALL AREAS WITHIN 100 FEET OF AN UNDISTURBED WETLAND SHALL BE MULCHED PRIOR TO ANY PREDICTED RAIN EVENT REGARDLESS OF THE 48 HOUR WINDOW. IN OTHER AREAS, THE TIME PERIOD MAY BE EXTENDED TO 7 DAYS.
- 6. FOR WORK, WHICH IS CONDUCTED BETWEEN OCTOBER 15TH AND APRIL 15TH OF ANY CALENDAR YEAR, ALL DENUDED AREAS, SHALL BE COVERED WITH HAY MULCH OR EROSION CONTROL MIX, APPLIED AT TMICE THE NORMAL APPLICATION RATE AND ANCHORED WITH A FABRIC NETTING. THE TIME PERIOD FOR APPLYING MULCH SHALL BE LIMITED TO 2 DAYS FOR ALL AREAS.
- 7. WASHINGTON AND ALLEN AVENUE SHALL BE SWEPT TO CONTROL MUD AND DUST AS NECESSARY. ADDITIONAL STONE SHALL BE ADDED TO THE STABILIZED CONSTRUCTION ENTRANCE TO MINIMIZE THE TRACKING OF MATERIAL OFF THE SITE AND ONTO THE SURROUNDING ROADWAYS.
- 8. DURING GRUBBING OPERATIONS STONE CHECK DAMS SHALL BE INSTALLED AT ANY EVIDENT CONCENTRATED FLOW DISCHARGE POINTS AND AS DIRECTED ON THE 9. SILT FENCING WITH A MINIMUM STAKE SPACING OF 6 FEET SHOULD BE USED, UNLESS THE FENCE IS SUPPORTED BY WIRE FENCE REINFORCEMENT OF MINIMUM 14
- GAUGE AND WITH A MAXIMUM MESH SPACING OF 6 INCHES, IN WHICH CASE STAKES MAY BE SPACED A MAXIMUM OF 10 FEET APART. THE BOTTOM OF THE
- 10. WOOD WASTE COMPOST/BARK BERMS MAY BE USED IN LIEU OF SILTATION FENCING. BERMS SHALL BE REMOVED AND SPREAD IN A LAYER NOT TO EXCEED 3" THICK ONCE UPSTREAM AREAS ARE COMPLETED AND A 90% CATCH OF VEGETATION IS ATTAINED.
- 11. STORM DRAIN CATCH BASIN INLET PROTECTION SHALL BE PROVIDED THROUGH THE USE OF STONE SEDIMENT BARRIERS OR APPROVED SEDIMENT BAGS (SUCH AS SILT SACK). INSTALLATION DETAILS ARE PROVIDED IN THE PLAN SET. THE BARRIERS SHALL BE INSPECTED AFTER EACH RAINFALL AND REPAIRS MADE AS NFCFSSARY. SFDIMENT SHALL BE REMOVED AND THE BARRIER RESTORED TO ITS ORIGINAL DIMENSIONS WHEN THE SEDIMENT HAS ACCUMULATED TO ½ THE DESIGN DEPTH OF THE BARRIER, THE BARRIER SHALL BE REMOVED WHEN THE TRIBUTARY DRAINAGE AREA HAS BEEN STABILIZED 12. WATER AND/OR CALCIUM CHLORIDE SHALL BE FURNISHED AND APPLIED IN ACCORDANCE WITH MDOT SPECIFICATIONS - SECTION 637 - DUST CONTROL
- 13. LOAM AND SEED IS INTENDED TO SERVE. AS THE PRIMARY PERMANENT REVEGETATIVE MEASURE FOR ALL DENUDED AREAS NOT PROVIDED WITH OTHER EROSION CONTROL MEASURES, SUCH AS RIPRAP. APPLICATION RATES ARE PROVIDED IN ATTACHMENT A OF THIS SECTION. SEEDING SHALL NOT OCCUR OVER SNOW.
- PERMANENT EROSION CONTROL MEASURES THE FOLLOWING PERMANENT EROSION CONTROL MEASURES HAVE BEEN DESIGNED AS PART OF THE EROSION/SEDIMENTATION CONTROL PLAN:
- 1. ALL AREAS DISTURBED DURING CONSTRUCTION, BUT NOT SUBJECT TO OTHER RESTORATION (PAVING, RIPRAP, ETC.) WILL BE LOAMED, LIMED, FERTILIZED, MULCHED, AND SEEDED. FABRIC NETTING, ANCHORED WITH STAPLES, SHALL BE PLACED OVER THE MULCH IN AREAS AS NOTED IN TEMPORARY EROSION CONTROL MEASURES PARAGRAPH 3 OF THIS REPORT. ALL AREAS WITHIN 100 FEET OF AN UNDISTURBED WETLAND SHALL BE MULCHED PRIOR TO ANY PREDICTED RAIN EVENT REGARDLESS OF THE 48 HOUR WINDOW. NATIVE TOPSOIL SHALL BE STOCKPILED AND REUSED FOR FINAL RESTORATION WHEN IT IS OF
- 2. ALL STORM DRAIN PIPE OUTLETS SHALL HAVE RIPRAP APRONS AT THEIR OUTLET TO PROTECT THE OUTLET AND RECEIVING CHANNEL FROM SCOUR AND DETERIORATION. INSTALLATION DETAILS ARE PROVIDED IN THE PLAN SET. THE APRONS SHALL BE INSTALLED AND STABILIZED TO THE EXTENT PRACTICABLE PRIOR TO DIRECTING RUNOFF TO THE TRIBUTARY PIPE OR CULVERT.
- 3. CATCH BASINS SHALL BE PROVIDED WITH SEDIMENT SUMPS AND INLET HOODS (THE SNOUT) FOR ALL OUTLET PIPES THAT ARE 18" IN DIAMETER OR LESS. 4 IMPLEMENTATION SCHEDULE

THE FOLLOWING CONSTRUCTION SEQUENCE SHALL BE REQUIRED TO INSURE THE EFFECTIVENESS OF THE EROSION AND SEDIMENTATION CONTROL MEASURES ARE OPTIMIZED: IT IS ANTICIPATED THAT CONSTRUCTION OF THE WALGREENS AND RELATED INFRASTRUCTURE WILL COMMENCE IN SPRING OF 2009 AND BE COMPLETED BY WINTER OF 2009

NOTE: FOR ALL GRADING ACTIVITIES, THE CONTRACTOR SHALL EXERCISE EXTREME CAUTION NOT TO OVEREXPOSE THE SITE BY LIMITING THE DISTURBED AREA.

1. INSTALL STABILIZED CONSTRUCTION ENTRANCE AT THE ACCESS DRIVE TO THE PROJECT SITE. INSTALL CONSTRUCTION ENTRANCE ONLY AS NECESSARY WHEN

- 2. INSTALL PERIMETER SILT FENCE, WOOD WASTE BERMS, AND/OR NON-WOVEN GEOTEXTILE FILLED WITH WOOD WASTE (SILT SOCKS) PRIOR TO GRUBBING RESPECTIVE
- 3. CLEAR AND GRUB SITE. INSTALL STONE CHECK DAMS AT ANY EVIDENT CONCENTRATED FLOW DISCHARGE POINTS.
- 4. FOUNDATION PREPARATION AREA SHALL BE EXCAVATED FOR INSTALLATION OF THE BUILDING FOOTINGS. BUILDING WORK WILL BE ON GOING THROUGH THE REMAINDER OF THE PROJECT.
- 5. COMMENCE INSTALLATION OF DRAINAGE APPURTENANCES.
- 6. COMMENCE EARTHWORK AND GRADING TO SUBGRADE. 7. COMMENCE INSTALLATION OF ELECTRICAL SERVICE.
- 8. COMMENCE INSTALLATION OF WATERLINE AND SEWER LINE
- COMMENCE INSTALLATION OF GAS SERVICE.
- 10. CONTINUE EARTHWORK AND GRADING TO SUBGRADE AS NECESSARY FOR CONSTRUCTION.
- 11. COMPLETE INSTALLATION OF UNDERGROUND UTILITIES TO WITHIN 5' OF THE BUILDINGS. 12. INSTALL LIGHT POLE FOUNDATIONS AND UTILITY POLES.
- 13. COMPLETE REMAINING EARTHWORK OPERATIONS.
- 14. COMPLETE INSTALLATION OF CATCH BASINS AND APPURTENANCES.
- 15. INSTALL SUB-BASE AND BASE GRAVEL WITHIN PARKING FIELDS, WALKWAYS, AND ALL DRIVEWAYS.
- 16. INSTALL CURBING IN PARKING FIELDS, DRIVEWAYS, AND ALONG THE STREETS AS NEEDED.
- 17. INSTALL BASE COURSE PAVING FOR ACCESS DRIVE AND PARKING AREA AS WELL AS CONCRETE SURFACES. 18. LOAM, LIME, FERTILIZE, SEED AND MULCH DISTURBED AREAS AND COMPLETE ALL LANDSCAPING.
- 19. INSTALL SURFACE COURSE PAVING FOR ACCESS DRIVE AND PARKING AREAS. STRIPE PER PLAN
- 20. ONCE THE SITE IS STABILIZED AND A 90% CATCH OF VEGETATION HAS BEEN OBTAINED, REMOVE ALL TEMPORARY EROSION CONTROL MEASURES.
- 21. TOUCH UP LOAM AND SEED NOTE: ALL DENUDED AREAS NOT SUBJECT TO FINAL PAVING, RIPRAP, OR GRAVEL SHALL BE REVEGETATED
- PRIOR TO CONSTRUCTION OF THE PROJECT, THE CONTRACTOR SHALL SUBMIT TO THE OWNER A SCHEDULE FOR THE COMPLETION OF THE WORK, WHICH WILL SATISFY THE
- 1. THE ABOVE CONSTRUCTION SEQUENCE SHOULD GENERALLY BE COMPLETED IN THE SPECIFIED ORDER; HOWEVER, SEVERAL SEPARATE ITEMS MAY BE CONSTRUCTED SIMULTANEOUSLY. WORK MUST ALSO BE SCHEDULED OR PHASED TO REDUCE THE EXTENT OF THE EXPOSED AREAS AS SPECIFIED BELOW. THE INTENT OF THIS SEQUENCE IS TO PROVIDE FOR EROSION CONTROL AND TO HAVE STRUCTURAL MEASURES SUCH AS SILT FENCE AND CONSTRUCTION ENTRANCES IN PLACE
- BEFORE LARGE AREAS OF LAND ARE DENUDED. 2. THE WORK SHALL BE CONDUCTED IN SECTIONS WHICH SHALL:
- d) LIMIT THE AMOUNT OF EXPOSED AREA TO THOSE AREAS IN WHICH WORK IS EXPECTED TO BE UNDERTAKEN DURING THE PROCEEDING 30 DAYS. b) REVEGETATE DISTURBED AREAS AS RAPIDLY AS POSSIBLE. ALL AREAS SHALL BE PERMANENTLY STABILIZED WITHIN 7 DAYS OF FINAL GRADING OR BEFORE A STORM EVENT; OR TEMPORARILY STABILIZED WITHIN 48 HOURS OF INITIAL DISTURBANCE OF SOIL FOR AREAS WITHIN 100 FEET OF AN UNDISTURBED WETLAND
- c) INCORPORATE PLANNED INLETS AND DRAINAGE SYSTEM AS EARLY AS POSSIBLE INTO THE CONSTRUCTION PHASE. THE DITCHES SHALL BE IMMEDIATELY LINED OR REVEGETATED AS SOON AS THEIR INSTALLATION IS COMPLETE.

15 Shaker Road

Gray, ME 04039

AND 7 DAYS FOR ALL OTHER AREAS. AREAS WITHIN 100 FEET OF AN UNDISTURBED WETLAND SHALL BE MULCHED PRIOR TO ANY PREDICTED RAIN EVENT

- 5 EROSION, SEDIMENTATION AND STABILIZATION CONTROL PLAN
- THE EROSION CONTROL PLAN IS INCLUDED IN THE PLAN SET. .6 DETAILS AND SPECIFICATIONS
- THE EROSION CONTROL DETAILS AND SPECIFICATIONS ARE INCLUDED IN THE PLAN SET

# THE RICHMOND COMPANY, INC.

Gorrill-Palmer Consulting Engineers, Inc. PO Box 1237 Engineering Excellence since 1998 207-657-6910

1.7 WINTER STABILIZATION PLAN THE WINTER CONSTRUCTION PERIOD IS FROM NOVEMBER 1 THROUGH APRIL 15. IF THE CONSTRUCTION SITE IS NOT STABILIZED WITH PAVEMENT, A ROAD GRAVEL BASE, 75% MATURE VEGETATION COVER OR RIPRAP BY NOVEMBER 15 THEN THE SITE NEEDS TO BE PROTECTED WITH OVER-WINTER STABILIZATION. AN AREA CONSIDERED OPEN IS ANY AREA NOT STABILIZED WITH PAVEMENT, VEGETATION, MULCHING, EROSION CONTROL MATS, RIPRAP OR GRAVEL BASE ON A ROAD.

WINTER EXCAVATION AND EARTHWORK SHALL BE COMPLETED SUCH THAT ANY AREA LEFT EXPOSED CAN BE CONTROLLED BY THE CONTRACTOR. LIMIT THE EXPOSED AREA TO THOSE AREAS IN WHICH WORK IS EXPECTED TO BE UNDER TAKEN DURING THE PROCEEDING 15 DAYS AND THAT CAN BE MULCHED IN ONE DAY PRIOR TO ANY SNOW EVENT ALL AREAS SHALL BE CONSIDERED TO BE DENUDED UNTIL THE SUBBASE GRAVEL IS INSTALLED IN ROADWAY/PARKING AREAS OR THE AREAS OF FUTURE LOAM AND SEED HAVE BEEN LOAMED, SEEDED AND MULCHED. HAY AND STRAW MULCH RATE SHALL BE A MINIMUM OF 150 LBS./1,000 S.F. (3 TONS/ACRE) AND SHALL BE PROPERLY ANCHORED. THE CONTRACTOR SHALL INSTALL ANY ADDED MEASURES WHICH MAY BE NECESSARY TO CONTROL EROSION/SEDIMENTATION FROM THE SITE DEPENDENT UPON THE ACTUAL SITE AND WEATHER CONDITIONS, CONTINUATION OF EARTHWORK OPERATIONS ON ADDITIONAL AREAS SHALL NOT BEGIN UNTIL THE EXPOSED SOIL SURFACE ON THE AREA BEING WORKED HAS BEEN STABILIZED, IN ORDER TO MINIMIZE AREAS WITHOUT EROSION CONTROL PROTECTION.

STOCKPILES OF SOIL OR SUBSOIL SHALL BE MULCHED FOR OVER WINTER PROTECTION WITH HAY OR STRAW AT TWICE THE NORMAL RATE OR AT 150 LBS/1,000 S.F. (3 TONS PER ACRE) OR WITH A FOUR-INCH LAYER OF WOODWASTE EROSION CONTROL MIX. THIS SHALL BE DONE WITHIN 24 HOURS OF STOCKING AND RE-ESTABLISHED PRIOR TO ANY RAINFALL OR SNOWFALL. ANY SOIL STOCKPILE SHALL NOT BE PLACED (EVEN COVERED WITH HAY OR STRAW) WITHIN 100 FEET FROM ANY NATURAL RESOURCES.

ANY AREAS WITHIN 100 FFFT FROM ANY NATURAL RESOURCES. IF NOT STABILIZED WITH A MINIMUM OF 75% MATURE VEGETATION CATCH, SHALL BE MULCHED BY DECEMBER 1 ANT AREAS WITHIN TOU FEEL FROM ANT NATURAL RESOURCES, IF NOT STABILIZED WITH A MINIMUM OF 75% MATURE VEGETATION CATCH, SHALL BE MULCHED BY DECEMBER 1 AND ANCHORED WITH PLASTIC NETTING OR PROTECTED WITH EROSION CONTROL MATS. DURING WINTER CONSTRUCTION, A DOUBLE LINE OF SEDIMENT BARRIERS (I.E. SILT FENCE BACKED WITH HAY BALES OR EROSION CONTROL MIX) SHALL BE PLACED BETWEEN ANY NATURAL RESOURCE AND THE DISTURBED AREA. PROJECTS CROSSING THE NATURAL RESOURCE SHALL BE PROTECTED A MINIMUM DISTANCE OF 100 FEET ON EITHER SIDE FROM THE RESOURCE. EXISTING PROJECTS NOT STABILIZED BY DECEMBER 1 SHALL BE PROTECTED WITH THE SECOND LINE OF SEDIMENT BARRIER TO ENSURE FUNCTIONALITY DURING THE SPRING THAW AND RAINS.

3. SEDIMENT BARRIERS DURING FROZEN CONDITIONS, SEDIMENT BARRIERS SHALL CONSIST OF WOODWASTE FILTER BERMS AS FROZEN SOIL PREVENTS THE PROPER INSTALLATION OF HAY BALES AND

AN AREA SHALL BE CONSIDERED DENUDED UNTIL AREAS OF FUTURE LOAM AND SEED HAVE BEEN LOAMED, SEEDED AND MULCHED. HAY AND STRAW MULCH SHALL BE APPLIED AT A RATE OF 150 LB. PER 1,000 SQUARE FEET OR 3 TONS/ACRE (TWICE THE NORMAL ACCEPTED RATE OF 75-LBS./1,000 S.F. OR 1.5 TONS/ACRE) AND SHALL BE PROPERLY ANCHORED. MULCH SHALL NOT BE SPREAD ON TOP OF SNOW. THE SNOW SHALL BE REMOVED DOWN TO A ONE-INCH DEPTH OR LESS PRIOR TO APPLICATION. AFTER EACH DAY OF FINAL GRADING, THE AREA SHALL BE PROPERLY STABILIZED WITH ANCHORED HAY OR STRAW OR EROSION CONTROL MATTING. AN AREA SHALL BE ONSIDERED TO HAVE BEEN STABILIZED WHEN EXPOSED SURFACES HAVE BEEN EITHER MULCHED WITH STRAW OR HAY AT A RATE OF 150 LB. PER 1,000 SQUARE FEET (3 FONS/ACRE) AND ADEQUATELY ANCHORED THAT GROUND SURFACE IS NOT VISIBLE THOUGH THE MULCH.

BETWEEN THE DATES OF NOVEMBER 1 AND APRIL 15. ALL MULCH SHALL BE ANCHORED BY PEG LINE, MULCH NETTING, ASPHALT EMULSION CHEMICAL, OR WOOD CELLULOSE FIBER. WHEN GROUND SURFACE IS NOT VISIBLE THROUGH THE MULCH THEN COVER IS SUFFICIENT. AFTER NOVEMBER 1ST, MULCH AND ANCHORING OF ALL BARE SOIL SHALL OCCUR AT THE END OF EACH FINAL GRADING WORKDAY 5. MULCHING ON SLOPES AND DITCHES

SLOPES SHALL NOT BE LEFT EXPOSED FOR ANY EXTENDED TIME OF WORK SUSPENSION UNLESS FULLY MULCHED AND ANCHORED WITH PEG AND NETTING OR WITH EROSION CONTROL BLANKETS. MULCHING SHALL BE APPLIED AT A RATE OF 230 LBS/1,000 S.F. ON ALL SLOPES GREATER THAN 8%. MULCH NETTING SHALL BE USED TO ANCHOR MULCH IN ALL DRAINAGE WAYS WITH A SLOPE GREATER THAT 3% FOR SLOPES EXPOSED TO DIRECT WINDS AND FOR ALL OTHER SLOPES GREATER THAT 8%. EROSION CONTROL BLANKETS SHALL BE USED IN LIEU OF MULCH IN ALL DRAINAGE WAYS WITH SLOPES 8%. EROSION CONTROL MIX CAN BE USED TO SUBSTITUTE EROSION CONTROL BLANKETS ON ALL SLOPES EXCEPT DITCHES.

BETWEEN THE DATES OF OCTOBER 15 AND APRIL 1ST, LOAM OR SEED WILL NOT BE REQUIRED. DURING PERIODS OF ABOVE FREEZING TEMPERATURES FINISHED AREAS SHALL BE FINE GRADED AND EITHER PROTECTED WITH MULCH OR TEMPORARILY SEEDED AND MULCHED UNTIL SUCH TIME AS THE FINAL TREATMENT CAN BE APPLIED. IF THE DATE IS AFTER NOVEMBER 1ST AND IF THE EXPOSED AREA HAS BEEN LOOMED, FINAL GRADED WITH A UNIFORM SURFACE, THEN THE AREA MAY BE DORMANT SEEDED AT A RATE OF 3 TIMES HIGHER THAN SPECIFIED FOR PERMANENT SEED AND THEN MULCHED. DORMANT SEEDING MAY BE SELECTED TO BE PLACED PRIOR TO THE PLACEMENT OF MULCH AND FABRIC NETTING ANCHORED WITH STAPLES. IF DORMANT SEEDING IS USED FOR THE SITE, ALL DISTURBED AREAS SHALL RECEIVE 4" OF LOAM AND SEED AT AN APPLICATION RATE OF 5 LBS/1,000 S.F. ALL AREAS SEEDED DURING THE WINTER SHALL BE INSPECTED IN THE SPRING FOR ADEQUATE CATCH. ALL AREAS INSUFFICIENTLY VEGETATED (LESS THAN 75% CATCH) SHALL BE REVEGETATED BY REPLACING LOAM, SEED AND MULCH. IF DORMANT SEEDING IS NOT USED FOR THE SITE, ALL DISTURBED AREAS SHALL

STANDARD FOR THE TIMELY STABILIZATION OF DITCHES AND CHANNELS -- THE APPLICANT SHALL CONSTRUCT AND STABILIZE ALL STONE-LINED DITCHES AND CHANNELS ON THE SITE BY NOVEMBER 15. THE APPLICANT SHALL CONSTRUCT AND STABILIZE ALL GRASS-LINED DITCHES AND CHANNELS ON THE SITE BY SEPTEMBER 1. IF THE APPLICANT FAILS TO STABILIZE A DITCH OR CHANNEL TO BE GRASS-LINED BY SEPTEMBER 1, THEN THE APPLICANT WILL TAKE ONE OF THE FOLLOWING ACTIONS TO STABILIZE INSTALL A SOD LINING IN THE DITCH -- THE APPLICANT SHALL LINE THE DITCH WITH PROPERLY INSTALLED SOD BY OCTOBER 1. PROPER INSTALLATION INCLUDES THE APPLICANT PINNING THE SOD ONTO THE SOIL WITH WIRE PINS, ROLLING THE SOD TO GUARANTEE CONTACT BETWEEN THE SOD AND UNDERLYING SOIL, WATERING THE SOD TO PROMOTE ROOT GROWTH INTO THE DISTURBED SOIL, AND ANCHORING THE SOD WITH JUTE OR PLASTIC MESH TO PREVENT THE SOD STRIPS FROM SLOUGHING DURING FLOW

STANDARDS FOR TIMELY STABILIZATION OF CONSTRUCTION SITES DURING WINTER

INSTALL A STONE LINING IN THE DITCH ——THE APPLICANT SHALL LINE THE DITCH WITH STONE RIPRAP BY NOVEMBER 15. THE APPLICANT SHALL HIRE A REGISTERED PROFESSIONAL ENGINEER TO DETERMINE THE STONE SIZE AND LINING THICKNESS NEEDED TO WITHSTAND THE ANTICIPATED FLOW VELOCITIES AND FLOW DEPTHS WITHIN THE DITCH. IF NECESSARY, THE APPLICANT SHALL REGRADE THE DITCH PRIOR TO PLACING THE STONE LINING SO TO PREVENT THE STONE LINING FROM REDUCING THE DITCH'S 2. STANDARD FOR THE TIMELY STABILIZATION OF DISTURBED SLOPES -- THE APPLICANT SHALL CONSTRUCT AND STABILIZE STONE-COVERED SLOPES BY NOVEMBER 15. THE APPLICANT SHALL SEED AND MULCH ALL SLOPES TO BE VEGETATED BY SEPTEMBER 1. THE DEPARTMENT SHALL CONSIDER ANY AREA HAVING A GRADE GREATER THAN 15% TO BE A SLOPE. IF THE APPLICANT FAILS TO STABILIZE ANY SLOPE TO BE VEGETATED BY SEPTEMBER 1, THEN THE APPLICANT SHALL TAKE ONE OF THE FOLLOWING ACTIONS STABILIZE THE SOIL WITH TEMPORARY VEGETATION AND EROSION CONTROL MATS -- BY SEPTEMBER 1 THE APPLICANT SHALL SEED THE DISTURBED SLOPE WITH WINTER RYE AT A SEEDING RATE OF 3 POUNDS PER 1,000 SQUARE FEET AND APPLY EROSION CONTROL MATS OVER THE MULCHED SLOPE. THE APPLICANT SHALL MONITOR GROWTH OF THE RYE OVER THE NEXT 30 DAYS. IF THE RYE FAILS TO GROW AT LEAST THREE INCHES OR COVER AT LEAST 75% OF THE DISTURBED SLOPE BY NOVEMBER 1, THEN THE APPLICANT SHALL COVER THE SLOPE WITH A LAYER OF WOODWASTE COMPOST AS DESCRIBED IN ITEM III OF THIS STANDARD OR WITH STONE RIPRAP AS DESCRIBED IN ITEM IV

STABILIZE THE SLOPE WITH SOD — THE APPLICANT SHALL STABILIZE THE DISTURBED SLOPE WITH PROPERLY INSTALLED SOD BY SEPTEMBER 1. PROPER INSTALLATION INCLUDES THE APPLICANT PINNING THE SOD ONTO THE SLOPE WITH WIRE PINS, ROLLING THE SOD TO GUARANTEE CONTACT BETWEEN THE SOD AND UNDERLYING SOIL, AND WATERING THE SOD TO PROMOTE ROOT GROWTH INTO THE DISTURBED SOIL. THE APPLICANT SHALL NOT USE LATE—SEASON SOD INSTALLATION TO STABILIZE SLOPES HAVING A STABILIZE THE SLOPE WITH WOODWASTE COMPOST -- THE APPLICANT SHALL PLACE A SIX-INCH LAYER OF WOODWASTE COMPOST ON THE SLOPE BY NOVEMBER 15. PRIOR TO PLACING THE WOODWASTE COMPOST, THE APPLICANT SHALL REMOVE ANY SNOW ACCUMULATION ON THE DISTURBED SLOPE. THE APPLICANT SHALL NOT USE WOODWASTE COMPOST TO STABILIZE SLOPES HAVING GRADES GREATER THAN 50% (2H: 1V) OR HAVING GROUNDWATER SEEPS ON THE SLOPE FACE.

STABILIZE THE SLOPE WITH STONE RIPRAP -- THE APPLICANT SHALL PLACE A LAYER OF STONE RIPRAP ON THE SLOPE BY NOVEMBER 15. THE APPLICANT SHALL HIRE A REGISTERED PROFESSIONAL ENGINEER TO DETERMINE THE STONE SIZE NEEDED FOR STABILITY AND TO DESIGN A FILTER LAYER FOR UNDERNEATH THE RIPRAP. 3. STANDARD FOR THE TIMELY STABILIZATION OF DISTURBED SOILS -- BY SEPTEMBER 15 THE APPLICANT SHALL SEED AND MULCH ALL DISTURBED SOILS ON AREAS HAVING A SLOPE LESS THAN 15% IF THE APPLICANT FAILS TO STABILIZE THESE SOILS BY THIS DATE, THEN THE APPLICANT SHALL TAKE ONE OF THE FOLLOWING ACTIONS TO STABILIZE THE SOIL WITH TEMPORARY VEGETATION -- BY SEPTEMBER 1 THE APPLICANT SHALL SEED THE DISTURBED SOIL WITH WINTER RYE AT A SEEDING RATE OF 3 POUNDS PER 1000 SQUARE FEET, LIGHTLY MULCH THE SEEDED SOIL WITH HAY OR STRAW AT 75 POUNDS PER 1000 SQUARE FEET, AND ANCHOR THE MULCH WITH PLASTIC NETTING.

THE APPLICANT SHALL MONITOR GROWTH OF THE RYE OVER THE NEXT 30 DAYS. IF THE RYE FAILS TO GROW AT LEAST THREE INCHES OR COVER AT LEAST 75% OF THE STABILIZE THE SOIL WITH SOD -- THE APPLICANT SHALL STABILIZE THE DISTURBED SOIL WITH PROPERLY INSTALLED SOD BY SEPTEMBER 15. PROPER INSTALLATION INCLUDES HE APPLICANT PINNING THE SOD ONTO THE SOIL WITH WIRE PINS, ROLLING THE SOD TO GUARANTEE CONTACT BETWEEN THE SOD AND UNDERLYING SOIL, AND WATERING THE SOD TO PROMOTE ROOT GROWTH INTO THE DISTURBED SOIL. STABILIZE THE SOIL WITH MULCH -- BY NOVEMBER 15 THE APPLICANT SHALL MULCH THE DISTURBED SOIL BY SPREADING HAY OR STRAW AT A RATE OF AT LEAST 150 POUNDS PER 1000 SQUARE FEET ON THE AREA SO THAT NO SOIL IS VISIBLE THROUGH THE MULCH. PRIOR TO APPLYING THE MULCH, THE APPLICANT SHALL REMOVE ANY SNOW ACCUMULATION ON THE DISTURBED AREA. IMMEDIATELY AFTER APPLYING THE MULCH, THE APPLICANT WILL ANCHOR THE MULCH WITH PLASTIC NETTING TO PREVENT WIND FROM MOVING THE MULCH OFF THE DISTURBED SOIL.

1.8 MAINTENANCE OF FACILITIES THE STORMWATER FACILITIES WILL BE MAINTAINED BY THE APPLICANT OR THEIR ASSIGNED HEIRS. THE CONTRACT DOCUMENTS WILL REQUIRE THE CONTRACTOR TO DESIGNATE A PERSON RESPONSIBLE FOR MAINTENANCE OF THE SEDIMENTATION CONTROL FEATURES DURING CONSTRUCTION AS REQUIRED BY THE EROSION CONTROL REPORT. LONG-TERM OPERATION/MAINTENANCE RECOMMENDED FOR THE STORMWATER FACILITIES IS PRESENTED BELOW. THE RESPONSIBLE PARTY MAY CONTRACT WITH SUCH PROFESSIONALS, AS MAY BE NECESSARY IN ORDER TO COMPLY WITH THIS PROVISION AND MAY RELY ON THE ADVICE OF

PROFESSIONALS IN CARRYING OUT ITS DUTY HEREUNDER, PROVIDED, THAT THE FOLLOWING OPERATION AND MAINTENANCE PROCEDURES ARE HEREBY ESTABLISHED AS A

INSPECTION AND MAINTENANCE FREQUENCY AND CORRECTIVE MEASURES: HE FOLLOWING AREAS, FACILITIES, AND MEASURES WILL BE INSPECTED AND THE IDENTIFIED DEFICIENCIES WILL BE CORRECTED. CLEAN-OUT MUST INCLUDE THE REMOVAL AND LEGAL DISPOSAL OF ANY ACCUMULATED SEDIMENTS AND DEBRIS.

INSPECT CATCH BASINS 2 TIMES PER YEAR (PREFERABLY IN SPRING AND FALL) TO ENSURE THAT THE CATCH BASINS ARE WORKING IN THEIR INTENDED FASHION AND THAT THEY ARE FREE OF DEBRIS. CLEAN STRUCTURES WHEN SEDIMENT DEPTHS REACH 12" FROM INVERT OF OUTLET. IF THE BASIN OUTLET IS DESIGNED WITH A HOOD TO TRAP FLOATABLE MATERIALS (I.E. SNOUT), CHECK TO ENSURE WATERTIGHT SEAL IS WORKING. AT A MINIMUM, REMOVE FLOATING DEBRIS AND HYDROCARBONS AT THE TIME OF THE INSPECTION. HYDROCARBON SOCKS INSTALLED WITHIN CATCH BASINS SHALL BE PROPERLY DISPOSED OF BY AN APPROVED CONTRACTOR WITHIN 14 DAYS AFTER THE FIRST 1" RAINFALL EVENT AFTER FINAL PAVEMENT. HYDROCARBON SOCKS SHALL BE MAINTAINED WITHIN ALL CATCH BASINS DURING THE FIRST YEAR OF OPERATION. ALL SOCKS SHOULD BE REMOVED AND DISPOSED OF ONE YEAR AFTER THE INITIAL REPLACEMENT. NEW HYDROCARBON SOCKS SHALL BE INSTALLED WITHIN AREAS THAT RECEIVE NEW

INSPECT SLOPES AND EMBANKMENTS EARLY IN THE GROWING SEASON TO IDENTIFY ACTIVE OR POTENTIAL EROSION PROBLEMS. REPLANT BARE AREAS OR AREAS WITH SPARSE GROWTH. WHERE RILL EROSION IS EVIDENT, ARMOR THE AREA WITH AN APPROPRIATE LINING OR DIVERT THE EROSIVE FLOWS TO ON—SITE AREAS ABLE TO WITHSTAND THE CONCENTRATED FLOWS. THE FACILITIES WILL BE INSPECTED AFTER MAJOR STORMS AND ANY IDENTIFIED DEFICIENCIES WILL BE CORRECTED. ROADWAYS AND PARKING SURFACES: CLEAR ACCUMULATIONS OF WINTER SAND IN PARKING LOTS AND ALONG ROADWAYS AT LEAST ONCE A YEAR, PREFERABLY IN THE

SPRING. ACCUMULATIONS ON PAVEMENT MAY BE REMOVED BY PAVEMENT SWEEPING. ACCUMULATIONS OF SAND ALONG ROAD SHOULDERS MAY BE REMOVED BY GRADING EXCESS SAND TO THE PAVEMENT EDGE AND REMOVING IT MANUALLY OR BY A FRONT-END LOADER. REPAIR POTHOLES AND OTHER ROADWAY OBSTRUCTIONS AND HAZARDS. PLOWING AND SANDING OF PAVED AREAS SHALL BE PERFORMED AS NECESSARY TO MAINTAIN VEHICULAR TRAFFIC SAFETY. DOWNSTREAM DEFENDER® ADVANCED VORTEX SEPARATOR MAINTENANCE FOR THE DOWNSTREAM DEFENDER SHALL CONFORM TO MANUFACTURERS SPECIFICATIONS. DURING THE FIRST YEAR OF OPERATION, THE UNIT SHOULD BE INSPECTED EVERY SIX MONTHS TO DETERMINE THE RATE OF SEDIMENT AND FLOATABLES ACCUMULATION. SUBSEQUENT MAINTENANCE WILL INCLUDE THE INSPECTION OF UNIT; REMOVAL OF SEDIMENT AND FLOATABLES; AND DOCUMENTATION OF MAINTENANCE PERFORMED. IT IS EXPECTED THAT THE MAINTENANCE SCHEDULE OF THIS UNIT WILL FOLLOW THE SEMI-ANNUAL SCHEDULE PROPOSED FOR THE OTHER STORMWATER FACILITIES.

RECERTIFICATION AS PART OF THE STORMWATER PERMIT, THE APPLICANT IS REQUIRED TO MEET THE STANDARDS IN APPENDIX B OF THE CHAPTER 500 RULES. APPENDIX B STATES THAT A PROJECT MUST SUBMIT A CERTIFICATION OF THE FOLLOWING TO THE DEPARTMENT WITHIN THREE MONTHS OF THE EXPIRATION OF EACH FIVE—YEAR INTERVAL FROM THE DATE G. IDENTIFICATION AND REPAIR OF EROSION PROBLEMS. ALL AREAS OF THE PROJECT SITE HAVE BEEN INSPECTED FOR AREAS OF EROSION, AND APPROPRIATE STEPS HAVE BEEN TAKEN TO PERMANENTLY STABILIZE THESE AREAS.

b. INSPECTION AND REPAIR OF STORMWATER CONTROL SYSTEM. ALL ASPECTS OF THE STORMWATER CONTROL SYSTEM HAVE BEEN INSPECTED FOR DAMAGE, WEAR, AND MALFUNCTION, AND APPROPRIATE STEPS HAVE BEEN TAKEN TO REPAIR OR REPLACE THE SYSTEM, OR PORTIONS OF THE SYSTEM.

MAINTENANCE. THE EROSION AND STORMWATER MAINTENANCE PLAN FOR THE SITE IS BEING IMPLEMENTED AS WRITTEN, OR MODIFICATIONS TO THE PLAN HAVE BEEN SUBMITTED TO AND APPROVED BY THE DEPARTMENT, AND THE MAINTENANCE LOG IS BEING MAINTAINED.

AS PART OF THE STORMWATER PERMIT, THE APPLICANT IS REQUIRED TO MEET THE STANDARDS IN APPENDIX C OF THE CHAPTER 500 RULES. THE FOLLOWING PROCEDURES ARE HEREBY ESTABLISHED AS A MINIMUM FOR COMPLIANCE WITH THIS SECTION. FOR FURTHER INFORMATION ON THE PROCEDURES LISTED BELOW, REFER TO CHAPTER 500 RULES -

APPROPRIATE SPILL PREVENTION, CONTAINMENT, AND RESPONSE PLANNING/IMPLEMENTATION SHALL BE USED TO PREVENT POLLUTANTS FROM BEING DISCHARGED FROM DURING CONSTRUCTION, HAZARDOUS MATERIALS WITH THE POTENTIAL TO CONTAMINATE GROUNDWATER SHALL NOT BE STORED OR HANDLED IN AREAS OF THE SITE WHICH


APPROPRIATE MEASURES SHALL BE TAKEN TO ENSURE THAT ACTIVITIES DO NOT RESULT IN NOTICEABLE EROSION OF THE SOILS AND WATER AND/OR CALCIUM CHLORIDE SHALL BE USED TO ENSURE THAT ACTIVITIES DO NOT RESULT IN FUGITIVE DUST EMISSIONS DURING OR AFTER CONSTRUCTION. DEBRIS AND OTHER MATERIALS:
LITTER, CONSTRUCTION DEBRIS, AND CHEMICALS EXPOSED TO STORMWATER MUST BE PREVENTED FROM BECOMING A POLLUTANT SOURCE.

FAX: 207-657-6912

WATER COLLECTED THROUGH THE PROCESS OF TRENCHING AND/OR DE-WATERING MUST BE REMOVED FROM THE PONDED AREA, AND MUST BE SPREAD THROUGH NATURAL WOODED BUFFERS OR OTHER AREAS THAT ARE SPECIFICALLY DESIGNED TO COLLECT THE MAXIMUM AMOUNT OF SEDIMENT POSSIBLE.


E-Mail: mailbox@gorrillpalmer.com

IDENTIFY AND PREVENT CONTAMINATION BY NON-STORMWATER DISCHARGES.

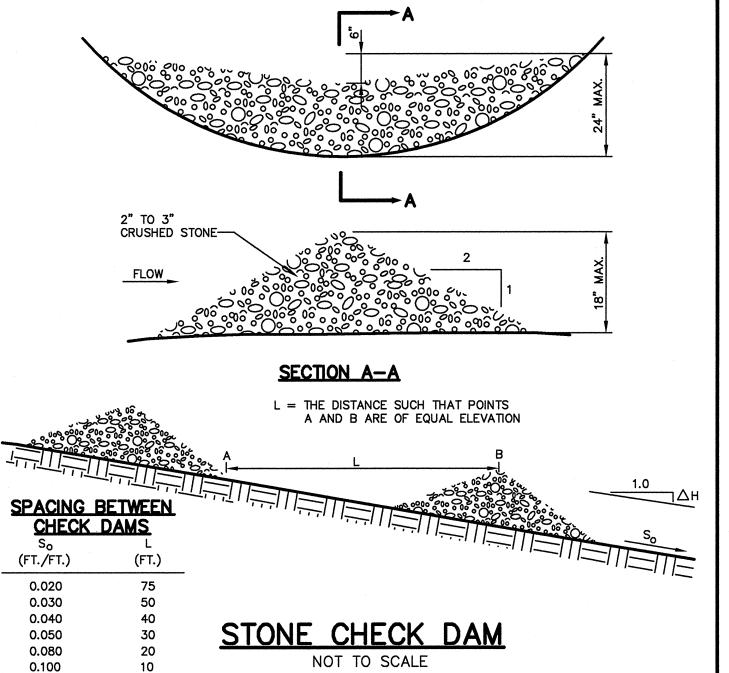

NOTES:


- 1. CONTRACTOR SHALL ADD STONE TO ENTRANCE AS MUD/SILT MATERIAL ACCUMULATES,
- 2. INSTALL CONSTRUCTION ENTRANCE ONLY AS NECESSARY WHEN PAVEMENT IS REMOVED.

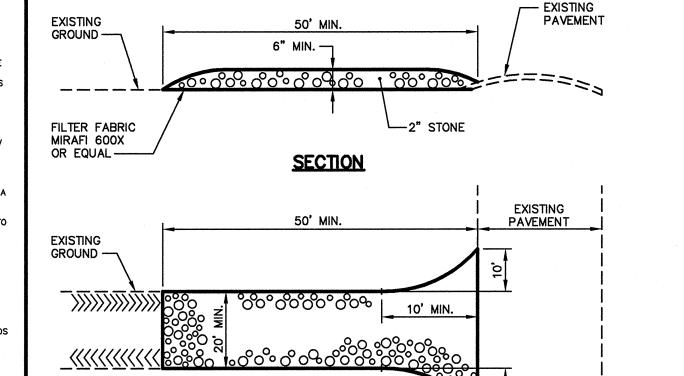

## STABILIZED CONSTRUCTION ENTRANCE


NOT TO SCALE


PLAN VIEW

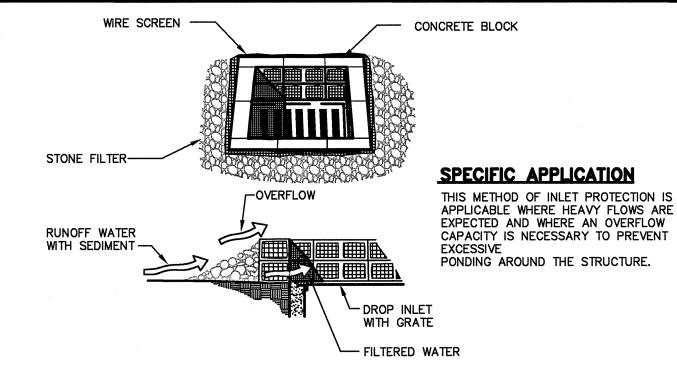


- PLACE CONCRETE BLOCKS LENGTHWISE ON THEIR SIDES IN A SINGLE ROW AROUND THE PERIMETER OF THE INLET, WITH THE ENDS OF ADJACENT BLOCKS ABUTTING. THE HEIGHT OF THE BARRIER CAN BE VARIED, DEPENDING ON DESIGN NEEDS, BY STACKING COMBINATIONS OF 4", 8" AND 12" WIDE BLOCKS. THE BARRIER OF BLOCKS SHALL BE AT LEAST 12 INCHES HIGH, AND NO GREATER
- WIRE MESH SHALL BE PLACED OVER THE OUTSIDE VERTICAL FACE (WEBBING) OF THE CONCRETE BLOCKS TO PREVENT STONE FROM BEING WASHED THROUGH THE HOLES IN THE BLOCKS. HARDWARE CLOTH OR COMPARABLE WIRE MESH WITH 1/2" OPENINGS SHALL BE USED.
- 3. STONE SHALL BE PILED AGAINST THE WIRE TO THE TOP OF THE BLOCK BARRIER, AS SHOWN IN DETAIL. THE STONE FILTER SHALL BE 3/4" CRUSHED STONE.
- 4. IF THE STONE FILTER BECOMES CLOGGED WITH SEDIMENT, SO THAT IT NO LONGER ADEQUATELY PERFORMS ITS FUNCTION, THE STONE MUST BE PULLED AWAY FROM THE BLOCKS, CLEANED AND REPLACED.

STONE SEDIMENT BARRIER

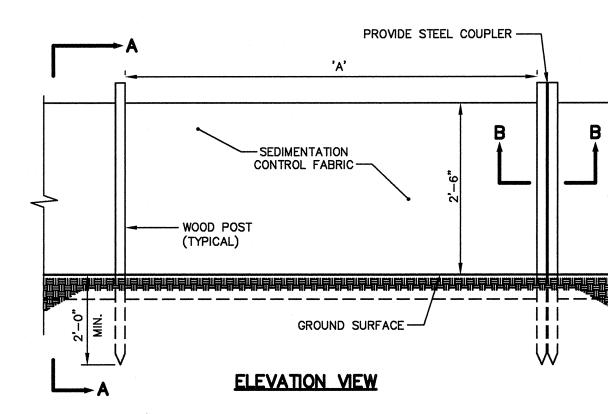

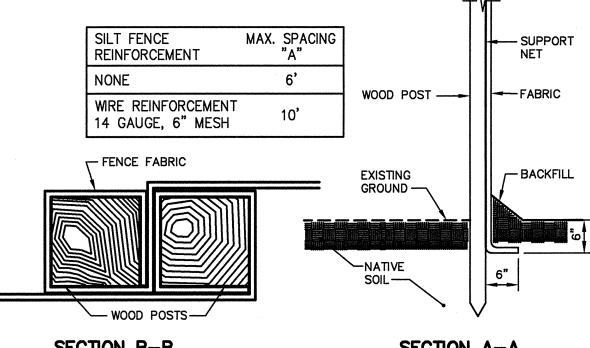

SILTATION FENCE DETAIL

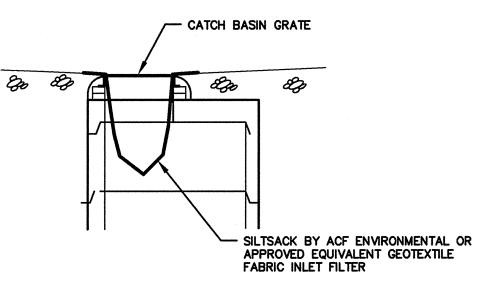

## CATCH BASIN INLET FILTER

- MOISTURE CONTENT 30-60%.
- C. SCREEN SIZE 100% LESS THAN 3", MAX. 70% LESS THAN 1".
- NO STONES LARGER THAN 2" IN DIAMETER. SILTS, CLAYS OR SUGAR SANDS ARE NOT ACCEPTABLE IN THE MIX.

CONTOUR.

VERY ROOTED FORESTED AREA OR AT THE EDGE OF GRAVEL PARKING AREAS.

FILL SLOPE--EXISTING GROUND RUNOFF <del>Varana arana kalana kalana</del>

WOOD WASTE COMPOST/BARK



DRAWINGS/SPECIFICATIONS BY:

X LANDLORD'S CONSULTANT


OTHERS.....□

ALL CONSTRUCTION WORK, UNLESS NOTED OTHERWISE, BY: □ WALGREENS' CONTRACTOR

X LANDLORD'S CONTRACTOR (TURNKEY CONSTRUCTION) BUILDING

NEW SHELL ONLY . . . □

. . . . . . . . . . . X REMODELING . . . EXISTING . . . . . . . . . RELOCATION . . . .

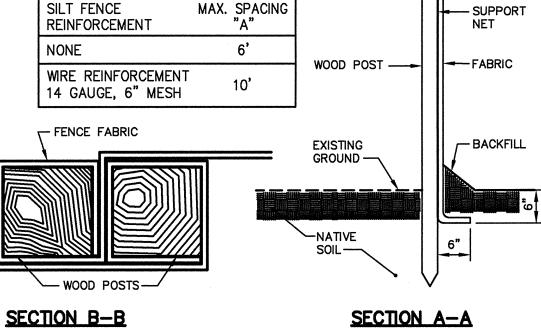


- THE WOOD WASTE COMPOST/BARK MIX SHALL CONFORM TO THE FOLLOWING
- B. pH 5.0 8.0. D. NO LESS THAN 40% ORGANIC MATERIAL (DRY WEIGHT) BY LOSS OF IGNITION.

2. THE COMPOST BERM SHALL BE PLACED, UNCOMPACTED, ALONG A RELATIVELY LEVEL

3. THE WOOD WASTE COMPOST/BARK FILTER BERM MAY BE USED IN LIEU OF SILTATION FENCE, AT THE TOE OF SHALLOW SLOPES, ON FROZEN GROUND, LEDGE OUT CROPS,

4. BERMS SHALL REMAIN IN PLACE UNTIL UPSTREAM AREA IS COMPLETED OR 70% CATCH OF VEGETATION IS ATTAINED. BERMS SHALL BE REMOVED BY SPREADING SUCH THAT NATIVE EARTH CAN BE SEEN BELOW.

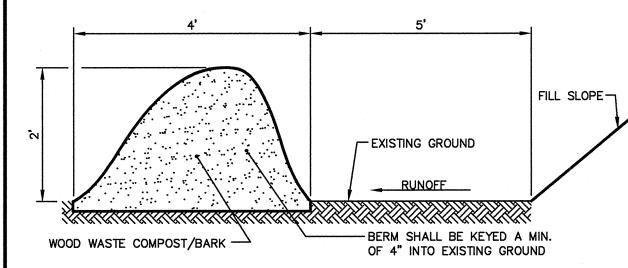

STORE NUMBER 12326 **PROJECT NAME** 

03/12/09 MPM ISSUED FOR CONSTRUCTION

10/15/08 MPM

DATE BY

HEREBY CERTIFY THAT THIS

PLAN AND SPECIFICATION

WAS PREPARED BY ME OR

SUPERVISION AND THAT I AM

STATE OF MAINE AS SIGNIFIED

UNDER MY DIRECT

A DULY REGISTERED

ARCHITECT OR ENGINEER

UNDER THE LAWS OF THE

BY MY HAND AND SEAL.

12/22/08 MPM RESPONSE TO CITY COMMENTS

09/22/08 MPM RESPONSE TO CITY COMMENTS

REVISIONS

CERTIFICATION AND SEAL

PER MDEP COMMENTS

**DESCRIPTION** 

WALGREENS - STORE #12326 (NWC) WASHINGTON AND ALLEN PORTLAND, MAINE

DRAWING TITLE **EROSION CONTROL NOTES AND DETAILS** CADD PLOT: DRAWING NO. \_ DRAWN BY: JBC VOID PLOT:

SUPERSEDES **REVIEWED BY:** PLAN DATED:

MPM

NOTE: THIS PLAN SET IS ISSUED FOR CONSTRUCTION.
