Form # P 04

DISPLAY THIS CARD ON PRINCIPAL FRONTAGE OF WORK

CITY OF PORTLAND

Please Read Application And Notes, If Any, Attached

BUILDING INSPECTION

PERM.

Permit Number: 061425

e of buildings and structures, and of the application on file in

This is to certify that KING CONSTRUCTION Compared by King Construction Corp

has permission to New Single Family HomeNew Single Family HomeNew Single Family HomeCar gar

AT 0 STEPPING STONE LN #2

provided that the person or persons from or person

of the provisions of the Statutes of the construction, maintenance and this department.

Apply to Public Works for street line and grade if nature of work requires such information.

ification of inspection must be an and writen permission product depretation by ilding or part there is need or atterwise cosed-in 4 UR NO HEQUIRED.

A certificate of occupancy must be procured by owner before this building or part thereof is occupied.

nspection Service

01/12/07

OTHER REQUIRED APPROVALS

Department Name


Fire Dept.

Health Dept.

Appeal Board

Other

PENALTY FOR REMOVING THIS CARD



E UNCAL

CITY OF PORTLAND, MAINE Department of Building Inspection

Certificate of Occupancy

LOCATION

9 STEPPING STONE LN #2

CBL 406 F052001

Issued to

KING CONSTRUCTION CORP /King Construction Corp Date of Issue

08/11/2008

This is to certify that the building, premises, or part thereof, at the above location, built — altered

— changed as to use under Building Permit No. 06-1425 has had final inspection, has been found to conform substantially to requirements of Zoning Ordinance and Building Code of the City, and is hereby approved for occupancy or use, limited or otherwise, as indicated below.

PORTION OF BUILDING OR PREMISES

Entire

APPROVED OCCUPANCY

Single Family
Use Group R3 Type 5B

IRC 2003

Limiting Conditions:

This CO is temporary, and is contingent upon fulfilling #4 of the conditions of approval (engineering

certification of lot grading) for the Autum Glenn Subdivision Site Plan Approval.

This condition must be fulfilled no later than September 30, 2008.

This certificate supersedes certificate issued

Approved:

(Date)

Inspector

Inspector of Buildings

Notice: This certificate identifies lawful use of building or premises, and ought to be transferred from owner to owner when property changes hands. Copy will be furnished to owner or lessee for one dollar.

TO:

Inspections Department

FROM:

Philip DiPierro, Development Review Coordinator

DATE:

August 12, 2008

RE:

C. of O. for #9 Stepping Stone Lane, Lot 2 Autum Glenn

Subdiv

(Id#2006-0190)(CBL 406 F 052001)

After visiting the site, I have the following comments:

Site work incomplete:

1. Miscellaneous site work,

This CO is temporary, and is contingent upon fulfilling #4 of the conditions of approval for the Autum Glenn Subdivision Site Plan Approval,

I anticipate this work can be completed by **September 30, 2008**. At this time, **I recommend issuing a temporary Certificate of Occupancy.**

Cc: Barbara Barhydt, Development Review Services Manager

Jeanie Bourke, Inspection Services Manager

File: Urban Insight


| | _ | | t Application | i | | CBL: | | |
|--|--|--|---|--|--|---|--|--|
| 389 Congress Street, 04101 | Tel: (207) 874-8703 | B, Fax: | (207) 874-871 | 6 06-1425 | national de la Company de la C | 406 FC | | |
| ocation of Construction: Owner Name: | | | Owner Address: | Phone: | | | | |
| STEPPING STONE LN #2 KING CONSTRUCTION COL | | | ION CORP | 198 SACO AV | Library Control of the Control of th | | | |
| Business Name: Contractor Name | | | | Contractor Addres | s: | Phone | | |
| King Construc | | | rp | 198 Saco OOB | . A 300 | 20793476 | | |
| Lessee/Buyer's Name | Phone: | the state of the s | | Permit Type: | | | | |
| | | |] | Single Family | Commence and processing the commence of the co | | | |
| Past Use: | Proposed Use: | | | Permit Fee: | Cost of Work: | CEO District: | | |
| Vacant Land | | ly Home/ New Single | | \$1,515.00 | \$142,000.0 | 00 4 | | |
| Family Home- | | - w/ 2 Car garage | | Approved | | SPECTION: Ise Group: R-3 To IRC 24 | | |
| Proposed Project Description: | | | | \sim | - AL | | | |
| New Single Family Home- w/ | 2 Car garage | | | Signature: S | | ignature: | | |
| | | | | PEDESTRIAN AC | TIVITIES DISTRI | CT (P.A.D.) | | |
| | | | | Action: App | roved Approx | ved w/Conditions | | |
| | | | | Signature: | Date: | | | |
| Permit Taken By: | Date Applied For: | | | Zoning Approval | | | | |
| ldobson | 09/27/2006 | | | 8-11 | | | | |
| This permit application does not preclude the Applicant(s) from meeting applicable State and | | | cial Zone or Revie | al Zone or Reviews Zoning Appeal | | Historic Preservati Not in District A Landon | | |
| Federal Rules. | J 11 | Shoretand y v v v | | , | | | | |
| 2. Building permits do not include plumbing, septic or electrical work. | | | ☐ Wetland NA ☐ Miscellaneous | | Does Not Require Revie | | | |
| 3. Building permits are void if work is not started within six (6) months of the date of issuance. | | | ood Zone and 7 - Zone | Conditional Use | | Requires Review | | |
| False information may inv permit and stop all work | alidate a building | ☐ Su | bdivision | Interp | retation | Approved | | |
| | - (| | te Plan Jool _ O190 | Appro | oved | Approved w/Conditions | | |
| gamena cheshe resolution i contributor i sonta di altra castato en material, contributo e e e e e e e e e e e | Menoral variable to the control of t | Maj [| ☐ Minor ☐ MM | ₩ Denie | d | Denied | | |
| PERMIT ISSI | ED | 1 - | Kwlcord. hor | | | Date: | | |
| JAN 1 2 20 CITY OF PORT | | | CERTIFICATION | g | | | | |
| I hereby certify that I am the ow I have been authorized by the o jurisdiction. In addition, if a peshall have the authority to enter such permit. | wner to make this applermit for work describe | med pro ication a d in the | operty, or that the as his authorized application is is | e proposed work agent and I agre sued, I certify the | e to conform to at the code offici | all applicable laws of this al's authorized representativ | | |
| SIGNATURE OF APPLICANT | | | ADDRESS | | DATE | PHONE | | |

Muse use plans stamped "Approved by the City".
Thanks T print out for insp. 5. fresenisdore 74x24 O.K namey O.K. Aunding - Drain - tested 5# O.K. water - Not tested CK Next insp. Julot- all plumBing tests on +OLE-6-18:08 - Final Insp. - Need to correct the Collowing Elect front & ven shirs - vise too high on front Weads 9/2" on rear - Exlisposed velds to be on plug & hole in foundation wall pueds to be scaled Bleak in plumbing, pipe in bsmot & bulkhead spirs need to be chosed in of bulkhad needs to be scaled on ext. Panel covers over heaters in buthrooms need to be fixed Drywall needs be finished in george near stairs in ell. Off & MAM. House find OK, punch list on house done! METry 7-17-08

Department of Health and Human Services

| | | APPLICATI | ON | | | Division of Environmental Health | | |
|--|--|--|------------------------|--|--|--|--|--|
| Town | | TY ADDRESS | | | | | | |
| Town or Plantation PORTLAND | | | | PORTLAN | 1.77 | 21166 | | |
| Street Subdivision Lot # 9 STEPPING STONE LANE | | | | Date Permit Co 20 | | | | |
| K III | PROPERTY ORFALT | OWNERS NAME | | Issued: LO 70 (| 2/] | \$ FEE Charged | | |
| Last: | | First: | | Local Plumbing Inspector Si | gnature | L.P.I.# 0, 1, 4,4 | | |
| Applica Name | | W+WAITZ | | | | | | |
| Mailing Add Owner/App (If Differ | dress of 321 4 | WOUN ST. | D MI | - 106 | 7 | 50 | | |
| knowle | that the information s | oplicant Statement ubmitted is correct to the nat any falsification is reas a Permit. | best of my | I have inspected the i | nstallation auth | ction Required orized above and found it to be in Rules. | | |
| 7// | Signature of Own | er/Applicant | Dat | e Local Plumbing Insp | pector Signatur | e Date Approv | | |
| | | | PERM | IT INFORMATION | | | | |
| This A | pplication is for | Тур | pe of Struct | ure To Be Served: | ING 1. ☑ MASTER PLUMBER 2. ☐ OIL BURNERMAN 3. ☐ MEC'D HOUSING DEALER/MECHANIC | | | |
| 1. ⊠, NE | W PLUMBING | 1. ⊠ SINGLE | FAMILY DW | | | | | |
| | LOCATED | 2. 🗆 MO | ODULAR OF | ' MODIEE HOME | | | | |
| | UMBING | the state of the state of the state of | LE FAMILY D | WELLING | | | | |
| | | 4. □ OTHER - | - SPECIFY | | | OPERTY OWNER | | |
| | | | | | LICENSI | =# <u>11526</u> | | |
| 1000 | Hook-Up & Piping | Relocation | | Column 2 | | Column1 | | |
| | Maximum of 1 Ho | | Number | Type of Fixture | Number | Type of Fixture | | |
| HOOK-UP: to public sewer in those cases where the connection is not regulated and inspected by | | 12 | Hosebib / Sillcock | 12 | Bathtub (and Shower) | | | |
| | the local Sanitary | | | Floor Drain | | Shower (Separate) | | |
| | OR | | | Urinal | 17 | Sink | | |
| | HOOK-UP: to an wastewater dispo | existing subsurface sal system. | | Drinking Fountain Indirect Waste | | Wash Basin | | |
| | | | | | | Water Closet (Toilet) | | |
| . | PIPING RELOCA lines, drains, and new fixtures. | TION: of sanitary piping without | | Water Treatment Softener, Filter, etc. | 1 | Clothes Washer | | |
| 7 | | | | Grease / Oil Separator | / | Dish Washer | | |
| | ************************************** | | | Roof Drain | 1.7 | Garbage Disposal | | |
| Y | C | \mathbf{R} | | Bidet | | Laundry Tub | | |
| TRANSFER FEE | | | Other: | | Water Heater | | | |
| | | [\$6.00] | ,2 | Fixtures (Subtotal) Column 2 | /3 | Fixtures (Subtotal) Column 1 | | |
| | | | | | 12 | Fixtures (Subtotal) Column 2 | | |
| SEE PERMIT FEE SCHED FOR CALCULATING FE | | | | 15 | Total Fixtures | | | |
| | | | G FEE | | Fixture Fee | | | |
| 1000 mm 4 4000 d | · · | | | | | Transfer Fee | | |
| | | | | | | Hook-Up & Relocation Fee | | |
| | e 1 of 1 | | martine e e l'implique | TOWN COPY | 7/- | Permit Fee (Total) | | |

Page 1 of 1 HHE-211 Rev. 08/05





Strengthening a Remarkable City, Building a Community for Life

www.portlandmaine.gov

Planning and Development Department Lee D. Urban, Director

Planning Division Alexander Jaegerman, Director

September 14, 2007

Mr. King Weinstein King Construction Corp. P.O.Box W Old Orchard Beach, Maine 04064

| 1/06 F | 51 |
|--------|----------|
| 406 F | S9 |
| 406 F | 53 |
| 406 F | 59 |
| 406 F | SE |
| 406 F | 57 |
| 406 | <u> </u> |

RE: Autumn Glen, aka Newcomb Glen/Stepping Stone Lane Job No. 2002-0178/ City # 710-0000-233.63-00

Dear Mr. Weinstein:

The City of Portland is informing you that it is calling the performance guarantee in the full amount of \$85, 424.50 for the above development which the City maintains in an escrow account. This call on the funds results from the "developer's failure to satisfactorily complete by October 15, 2005 the work in the improvements contained within the Autumn Glen Subdivision approval, dated April 8, 2003."

Thank you for your attention to this matter.

Sincerely

Director of Planning and Urban Development

406-F55 406-F56 406-F060 406-F52

Cc:

Penny Littell Barbara Barhydt Alex Jaegerman Nathan Smith

David Hirshon
Matthew Chamberlain
Jeanie Bourke
Phil DiPierro
Todd Merkle
Michael Bobinsky
Mr. George Denney



BUILDING PERMIT INSPECTION PROCEDURES Please call 874-8703 or 874-8693 to schedule your inspections as agreed upon

Permits expire in 6 months, if the project is not started or ceases for 6 months.

The Owner or their designee is required to notify the inspections office for the following inspections and provide adequate notice. Notice must be called in 48-72 hours in advance in order to schedule an inspection:

By initializing at each inspection time, you are agreeing that you understand the inspection procedure and additional fees from a "Stop Work Order" and "Stop Work Order Release" will be incurred if the procedure is not followed as stated below.

| A Pre-construction Meeting will take pla | ce upon receipt of your building permit. |
|--|--|
| Footing/Building Location Inspec | etion: Prior to pouring concrete |
| Re-Bar Schedule Inspection: | Prior to pouring concrete |
| Foundation Inspection: | Prior to placing ANY backfill |
| Framing/Rough Plumbing/Electri | ical: Prior to any insulating or drywalling |
| Final/Certificate of Occupancy: | Prior to any occupancy of the structure or use. NOTE: There is a \$75.00 fee per inspection at this point. |
| phase, REGARDLESS OF THE NOTICE | Occupancy. All projects DO require a final cur, the project cannot go on to the next E OR CIRCUMSTANCES. ES MUST BE ISSUED AND PAID FOR, PIED |

City of Portland, Maine Inspections Division Inspection Schedule

Appointment Date Between 1/1/2006 And 6/29/2007

| Dist.# Fire Insp. | Sch. Date: ParcelNo: . Contact: | Appl. Type Inspector | Schedule Type Comments | Appl #: | Location | |
|----------------------|---|------------------------------|---|---------|---------------------------------|--|
| 4 | 05/02/2007 406 F052001 KING CONSTRUCTION | Building Permit Tammy Munson | Footings/Setbacks | 06-1425 | 9 STEPPING STONE LN | |
| | | Tom Markley | 423-4742 Gary - met w/Gary on site - no lines strung out, missing pins, footing forms not in place. Told him we wanted a staement from a surveyor the footing placement is compliant and to return and verify the wall placement is compliant and the elevation. Told Gary not to pour. | | | |
| ļ | 05/11/2007 406 F052001 | Building Permit | Footings/Setbacks | 07-0473 | 9 STEPPING STONE LN | |
| | KING CONSTRUCTION | Tammy Munson Tom Markley | Call Gary @ 423-4742 - footings wall placement and send letter | | er from surveyor - will recheck | |
| 4 | 05/31/2007 406 F052001 | Building Permit | Foundation/Backfill | 06-1425 | 9 STEPPING STONE LN | |
| | KING CONSTRUCTION | Tammy Munson | Gary @ 423-4742 - ok to backfil | I | | |

Total Listed: 3



Facsimile Cover Sheet

| Project No. | 01259 | | | | |
|--|----------------------------|--|--|--|--|
| To: | Amy Munson | | | | |
| Company: | Portland Inspectors Office | | | | |
| Phone: | | | | | |
| Fax: | 874-8716 | | | | |
| From: | Matthew Ek | | | | |
| Date: | 6/5/07 | | | | |
| Pages including this | 3 | | | | |
| cover page: | | | | | |
| Comments: Here is the as-built letter requested on Lots 2&3 of Autumn Glen Subdivision, Stepping Stone Lane. Let me know if you have any questions. | | | | | |
| Thanks, Matt | | | | | |
| Reply Requested: |] Yes 🔲 No | | | | |
| Original to go out in mail: |] Yes 🔲 No | | | | |
| | | | | | |

If you have any problems receiving this FAX, please contact Julie at: (207) 856-0277 (207) 856-2206 FAX Number

One Chabot Street P.O. Box 1339 Westbrook, Maine 04098-1339 207-856-0277 Fax 207-856-2206



Facsimile Cover Sheet

| Project No. | 01259 | | | | |
|---|---------------------------------------|--|--|--|--|
| To: | GARY | | | | |
| Company: | Windsor Construction Company | | | | |
| Phone: | 423-4742 | | | | |
| Fax: | 934-1566 | | | | |
| From: | Matthew Ek | | | | |
| Date: | 6/5/07 | | | | |
| Pages including this | 3 | | | | |
| cover page: | | | | | |
| Comments: Here is the Letter going to questions. | the city. Let me know if you have any | | | | |
| Thanks, Matt | | | | | |
| | | | | | |
| Reply Requested: | Yes 🖾 No | | | | |
| Original to go out in mail: |] Yes 🗵 No | | | | |

If you have any problems receiving this FAX, please contact Julie at: (207) 856-0277 (207) 856-2206 FAX Number

Sebago Technics

Engineering Expertise You Can Build On

sebagotechnics.com

One Chabot Street P.O. Box 1339 Westbrook, Maine O4098:1339 Ph. 207-856-0277 Fax 856-2206

June 4, 2007 01259

Ms. Amy Munson Code Enforcement Office City of Portland 389 Congress Street Portland, ME 04101

Via Facsimile: 207-874-8716

Lots 2 and 3, Autumn Glen Subdivision

Dear Amy:

This letter is to inform you that Sebago Technics, Inc. has survey located the constructed foundations on Lots 2 and 3 in the Autumn Glen Subdivision. Under my supervision, one of our survey crews completed this as-built location on June 1, 2007. The proposed house met all of the setbacks as shown on the Subdivision Plan of Autumn Glen as shown on the attached sketch.

If you have any further questions, please feel free to contact me.

Sincerely,

SEBAGO TECHNICS, INC.


Pattle W. Et

Matthew W. Ek, PLS Project Surveyor

MWE:mwe/jc Enc.





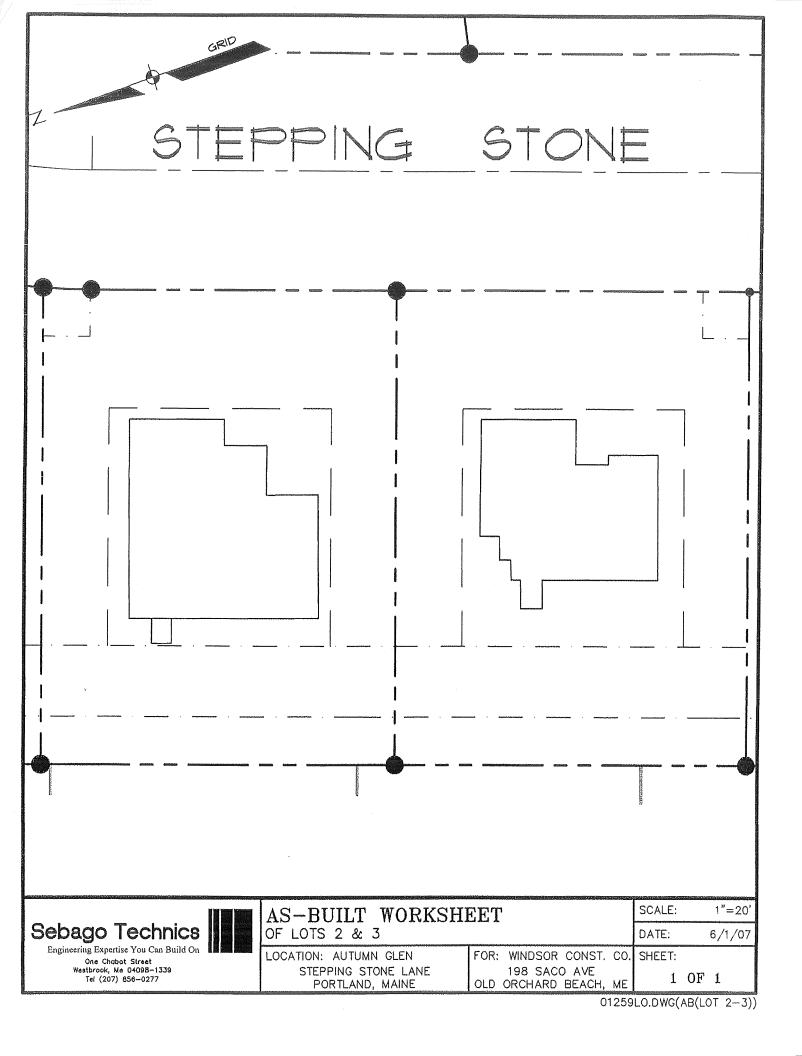

| <i>a</i> :1 | wof Davidand Maine Dui | ldina an Han Danii | 4 | | Permit No: | Date Applied For: | CBL: | |
|----------------------------|--|-------------------------|------------------------|--------|------------------------------------|--|-----------------|--|
| | ty of Portland, Maine - Bui O Congress Street, 04101 Tel: (| 0 | | 8716 | 06 1425 | 09/27/2006 | 406 F052001 | |
| Loca | ation of Construction: | Owner Name: | ` / | | Owner Address: | | Phone: | |
| 9 S | TEPPING STONE LN #2 | KING CONSTRUCT | ION CORP | | 198 SACO AVE | | | |
| Busi | ness Name: | Contractor Name: | | | Contractor Address: | *************************************** | Phone | |
| | | King Construction Co. | King Construction Corp | | 198 Saco OOB | | (207) 934-7622 | |
| Lessee/Buyer's Name Phone: | | | | 1 | Permit Type: | PP-100-10-10-10-10-10-10-10-10-10-10-10-10 | | |
| | | | | | Single Family | | | |
| Prop | posed Use: | | Pr | opose | d Project Description: | | | |
| Sin | ngle Family Home/ New Single Fa | mily Home- w/ 2 Car ga | rage N | Iew S | ingle Family Home | e- w/ 2 Car garage | | |
| N | ote: This property shall be a single far | Approved with Condition | | | Ann Machado quire a separate pe | Approval D | Ok to Issue: 🗹 | |
| 2) | approval. 2) This permit is being approved on the basis of plans submitted. Any deviations shall require a separate approval before starting that work. | | | | | | | |
| 3) | 3) As discussed during the review process, the property must be clearly identified prior to pouring concrete and compliance with the required setbacks must be established. Due to the proximity of the setbacks of the proposed addition, it may be required to be located by a surveyor. | | | | | | | |
| D | ept: Building Status: A | Approved with Condition | ns Revie | ewer: | Tammy Munson | Approval D | ate: 01/12/2007 | |
| | ote: | | | | · | ** | Ok to Issue: | |
| | A copy of the enclosed chimney of Certificate of Occupancy. | disclosure must be subm | itted to this | office | e upon completion | of the permitted wor | | |
| 2) | The basement is NOT approved as habitable space. A code compliant 2nd means of egress must be installed in order to change the use of this space. | | | | | | | |
| 3) | The design load spec sheets for any engineered beam(s) must be submitted to this office. | | | | | | | |
| 4) | Permit approved based on the plans submitted and reviewed w/owner/contractor, with additional information as agreed on and as noted on plans. | | | | | | | |
| 5) | As discussed, the rafters must be 2" x 10"s. | | | | | | | |
| 6) | 5) The attic scuttle opening must be 22" x 30". | | | | | | | |
| 7) | 7) Hardwired interconnected battery backup smoke detectors shall be installed in all bedrooms, protecting the bedrooms, and on every level. | | | | | | | |
| 8) | 3) There must be a 2" clearance maintained between the chimney and any combustible material, with draft stopping per code at each level | | | | | | | |
| 9) | Separate permits are required for any electrical, plumbing, or HVAC systems. Separate plans may need to be submitted for approval as a part of this process. | | | | | | | |

1) The Development Review Coordinator reserves the right to require additional lot grading or other drainage improvements as necessary due to field conditions.

Status: Approved with Conditions

Dept: DRC

Note:

- 2) A sewer permit is required for your project. Please contact Carol Merritt at 874-8300, ext. 8822. The Wastewater and Drainage section of Public Works must be notified five (5) working days prior to sewer connection to schedule an inspector for your site.
- 13) Two (2) City of Portland approved species and size trees must be planted on your street frontage prior to issuance of a Certificate of Occupancy.

Reviewer: drc

10/31/2006

Ok to Issue:

Approval Date:

