

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G _____ WJE _____ Sheet 1 of 1

Room Number on Plan: 1096 Building Room Number: ALUMNI HALL

Repair Designation/Description: Wall penetration TASK 1

Engineering Sketches / Calculations Reference: _____

Contractor: C. M. CIMINO

INSPECTION RECORD

Repair Start Date: _____ / _____ / _____ By: _____

Intermediate Inspections:

Date	Time	By	Comment/Photos

JAN 30 1995

Repair Completion Date: unknown / _____ By: _____

Final Sign Off: DP 1-21-95 / CP 01-29-95 [Signature]
P&G WJE City of Portland

MJE 942506
WJE 1410

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G _____ WJE _____ Sheet 1 of 1

Room Number on Plan: 2034 Building Room Number: _____

Repair Designation/Description: REPAIR & WATER PENETRATIONS TASKS
THRU 4

Engineering Sketches / Calculations Reference: _____

Contractor: CNC

INSPECTION RECORD

Repair Start Date: ____/____/____ By: _____

Intermediate Inspections:

Date	Time	By	Comment/Photos

JAN 30 1995

Repair Completion Date: 1 / 29 / 95 By: DVP

Final Sign off: DVP 1-29-95 / CP 01/29/95 / [Signature] 01-28-95
P&G WJE City of Portland

WJE 942566
WJE 1912

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G WJE Sheet 1 of

Room Number on Plan: 2035 Building Room Number: BATHROOM

Repair Designation/Description: W2 + W7, CHASE PENET. (TYP.)
CLAY TILE AREA

Engineering Sketches / Calculations Reference:

Contractor: CM CIMINO

INSPECTION RECORD

Repair Start Date: 1 / 3 / 95 By: MWC

Intermediate Inspections:

Date	Time	By	Comment/Photos
<u>1/3/95</u>	<u>2:30 PM</u>	<u>MWC</u>	<u>MASONRY INFILL DONE AT WALL</u>
			<u>ABOVE FIXTURES, STARTING WORK</u>
			<u>AT OPENINGS ADJACENT TO ENTRANCE DOORS</u>
			<u>SIGN OFF CONTINGENT ON REPAIR OF</u>
			<u>CLAY TILE AREA. PENET. BEING COMPLETE</u>
			<u>FEB. VACA.</u>

JAN 30 1995

Repair Completion Date: unknown By:

Final Sign Off: DWP 1-29-95 / CP 01-29-95 By:
P&G WJE City of Portland

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G _____ WJE _____ Sheet 1 of 1

Room Number on Plan: 2040 Building Room Number: STORAGE

Repair Designation/Description: PIPE HANGERS, PATCH CEILING

Engineering Sketches / Calculations Reference: _____

Contractor: C. M. Cimino

INSPECTION RECORD

Repair Start Date: 12 / 9 / 94 By: MWC

Intermediate Inspections:

Date	Time	By	Comment/Photos
<u>12/7/94</u>	<u>unknown</u>	<u>MWC</u>	<u>Small holes patched</u> <u>(PIPE HANGERS, DAMAGED BY STATE FIRE</u> <u>MARSHAL, REPAIRS MAY BE DELAYED)</u>

JAN 30 1995

Repair Completion Date: unknown By: _____

Final Sign Off: HP 1-29-95, CP 01-29-95, [Signature] 1-29-95
P&G WJE City of Portland

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G _____ WJE _____ Sheet 1 of 1

Room Number on Plan: 2057 Building Room Number: STORAGE

Repair Designation/Description: RAISE CEILING W/GWB, LOWER

SPRINKLER HEAD

Engineering Sketches / Calculations Reference: _____

Contractor: _____

INSPECTION RECORD

Repair Start Date: _____ / _____ / _____ By: _____

Intermediate Inspections:

Date	Time	By	Comment/Photos
1-10-95	unknown	DVP	GWB COMPLETE, LOWER SPRINK. HEAD

JAN 30 1995

Repair Completion Date: unknown / _____ / _____ By: _____

Final Sign Off: DVP 1-29-95 / CP 01-29-95 / [Signature] 1-29-95
P&G WJE City of Portland

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G WJE _____ Sheet 1 of 1

Room Number on Plan: 2092 Building Room Number: TELLER

Repair Designation/Description: TASK 1 WALL PENETRATION

Engineering Sketches / Calculations Reference: _____

Contractor: CMC

INSPECTION RECORD

Repair Start Date: 1 / 25 / 95 By: DUP

Intermediate Inspections:

Date	Time	By	Comment/Photos

JAN 30 1995

Repair Completion Date: 1 / 25 / 95 By: DUP

Final Sign Off: DUP 1-29-95 / CP 29 JAN 95 / [Signature] 1-29-95
P&G WJE City of Portland

WJE 942566
WJE 1/16

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G _____ WJE _____ Sheet 1 of 1

Room Number on Plan: 2095 Building Room Number: 209

Repair Designation/Description: WALL OPENING TASK #1

Engineering Sketches / Calculations Reference: W2, W7

Contractor: C.M. SIMONS

INSPECTION RECORD

Repair Start Date: 12 / 7 / 94 By: RBJ

Intermediate Inspections:

Date	Time	By	Comment/Photos
12/7/94	unknown	RBJ	FIRE STOP old DUCT OPENING w/mortar Down

JAN 30 1995

Repair Completion Date: 1 / 28 / 95 By: [Signature]

Final Sign Off: [Signature] P&G 1-29-95 / [Signature] WJE 01-29-95 / [Signature] City of Portland 1-29-95

WJE 942566
WJE 1416

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G _____ WJE _____ Sheet 1 of 1

Room Number on Plan: 2096 Building Room Number: _____

Repair Designation/Description: NEW STEEL OLD STEEL WELDS
TILE ARCH PENETRATION

Engineering Sketches / Calculations Reference: _____

Contractor: _____

INSPECTION RECORD

Repair Start Date: ____/____/____ By: _____

Intermediate Inspections:

Date	Time	By	Comment/Photos

JAN 30 1995

Repair Completion Date: 1 / 28 / 95 By: [Signature]

Final Sign Off: DGP 1-29-95 / CP 01-29-95 / [Signature] 1-29-95
 P&G WJE City of Portland

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G _____ WJE _____ Sheet 1 of 1

Room Number on Plan: 2102 Building Room Number: 207

Repair Designation/Description: GAP AND TILE AREA

PENETRATIONS

Engineering Sketches / Calculations Reference: S+W3, W1W3

Contractor: CEMENTUMS. KNOWLTON

INSPECTION RECORD

Repair Start Date: 12 / 7 / 94 By: RBJ

Intermediate Inspections:

Date	Time	By	Comment/Photos
12/7/94	UNKNOWN	RBJ	Filled solid 6" opening TASK#5
1-28-95	UNKNOWN	JPS	OBSERVED G. TEL

JAN 30 1995

Repair Completion Date: 1 / 28 / 95 By: JPS

Final Sign Off: OKP 1-29-95, CP 01/29/95 / (Signature) 1-29-95
P&G WJE City of Portland

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G _____ WJE _____ sheet 1 of _____

Room Number on Plan: 2119 Building Room Number: hallway near

Repair Designation/Description: Bridge Repair 2019 etc

Engineering Sketches / Calculations Reference: _____

Contractor: _____

INSPECTION RECORD

Repair Start Date: 1/17/95 By: O. Rowe

Intermediate Inspections:

Date	Time	By	Comment/Photos
1/17/95	8:55 am	AL	work progresses
1/17/95	9:30 am	KL/AR	NO PLAN MOVING HAND GRIPPER INTO PLACE DON
1/17/95	11:05 am	AL	work continues
1/17/95	1:10 pm	AL	" "
1/17/95	2:55 pm	AL	" "
1/17/95	1:30 p	LFV	Increased installation of new WIG; verbally described construction sequence
1-18-95	2:15	JJ	Final plan of work in progress

JAN 30 1995

Repair Completion Date: unknown By: _____

Final Sign Off: WJP 1-29-95 / CP 01-29-95 [Signature] 1-29-95
 P&G WJE City of Portland

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G _____ WJE _____ Sheet _____ of _____

Room Number on Plan: 3017 Building Room Number: VIEWING ROOM

Repair Designation/Description: _____

Engineering Sketches / Calculations Reference: _____

Contractor: _____

INSPECTION RECORD

Repair Start Date: _____ / _____ / _____ : _____

Intermediate Inspections:

Date	Time	By	Comment/Photos

JAN 30 1995

Repair Completion Date: _____ / _____ / _____ By: _____

Final Sign Off: DUP 1-29-95 / CP 01/29/95 / [Signature] 1-29-95
P&G WJE City of Portland

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G _____ WJE _____ Sheet 1 of 1

Room Number on Plans: 3035 Building Room Number: 324

Repair Designation/Description: SKYLIGHT, CEILING AND
WALL PENETRATIONS, LOOSE JOINT FALL HAZARD

Engineering Sketches / Calculations Reference: _____

Contractor: C.P. SUMINU

INSPECTION RECORD

Repair Start Date: 12 / 13 / 94 By: MWC

Intermediate Inspections:

Date	Time	By	Comment/Photos
<u>12/13/94</u>	<u>4:00 PM</u>	<u>MWC</u>	<u>Area Inspected and Taped. Note - plaster ceiling skylight needs repair.</u>

JAN 30 1995

Repair Completed: UNKNOWN By: _____

Final Signatures: P&G / CP / 01-28-95 / [Signature] / 01-28-95
P&G WJE City of Portland

MPI 94254d
1-12-94

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G _____ WJE _____ Sheet 1 of 1

Room Number on Plan: 3054 Building Room Number: 337

Repair Designation/Description: TASKS 1-2 WALL PENETRATIONS;

CEILING PENETRATIONS TASKS 3, 4, 6; ALARM BOX TASK 5

Engineering Sketches / Calculations Reference: _____

Contractor: CNC

INSPECTION RECORD

Repair Start Date: _____ / _____ / _____ By: _____

Intermediate Inspections:

Date	Time	By	Comment/Photos
<u>1-18-95</u>	<u>9:30</u>	<u>DVP</u>	<u>TASKS 1 & 2 COMPLETE</u>
<u>1-29-95</u>	<u>unknown</u>	<u>DVP</u>	<u>TASKS 3, 4, 6, 7 COMPLETE</u>

JAN 30 1995

Repair Completion Date: unknown By: _____
Final Sign Off: DVP 1-29-95 / OP 01/24/95 / WJE 1-29-95
P&G WJE City of Portland

WJE 0-2566
WJE 191A

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G _____ WJE _____ Sheet 1 of 1

Room Number on Plan: 3056 Building Room Number: 338

Repair Designation/Description: NO WORK REQUIRED

Engineering Sketches / Calculations Reference: _____

Contractor: _____

INSPECTION RECORD

Repair Start Date: _____ / _____ / _____ By: _____

Intermediate Inspections:

Date	Time	By	Comment/Photos

JAN 30 1995

Repair Completion Date: _____ / _____ / _____ By: _____

Final Sign off: WJP 1-24-95 / CP 01/24/95 [Signature]
P&G WJE City of Portland

WJE 542566
WJE 1410

SAM H.

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G _____ WJE _____ Sheet 1 of 1

Room Number on Plan: 3005 Building Room Number: _____

Repair Designation/Description: TASK 1

Engineering Sketches / Calculations Reference: _____

Contractor: _____

INSPECTION RECORD

Repair Start Date: _____ / _____ / _____ By: _____

Intermediate Inspections:

Date	Time	By	Comment/Photos

JAN 30 1995

Repair Completion Date: 1 / 29 / 95 By: [Signature]

Final Sign Off: [Signature] P&G 1-29-95 CP 01/29/95, [Signature] WJE 29/01/95
City of Portland

WJE 942566
WJE 1410

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G _____ WJE _____ Sheet 1 of 1

Room Number on Plan: 3014 Building Room Number: HALL

Repair Designation/Description: _____

Engineering Sketches / Calculations Reference: _____

Contractor: _____

INSPECTION RECORD

Repair Start Date: _____ / _____ / _____ By: _____

Intermediate Inspections:

Date	Time	By	Comment/Photos

JAN 30 1995

Repair Completion Date: _____ / _____ / _____ By: _____

Final Sign Off: DWP 1-19-95 / CP 1/29/95 / [Signature]
P&G WJE City of Portland

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G _____ WJE _____ Sheet _____ of _____

Room Number on Plan: 306 Building Room Number: 1404

Repair Designation/Description: _____

Engineering Sketches / Calculations Reference: _____

Contractor: _____

INSPECTION RECORD

Repair Start Date: _____ / _____ / _____ By: _____

Intermediate Inspections:

Date	Time	By	Comment/Photos

JAN 30 1995

Repair Completion Date: _____ / _____ / _____ By: _____

Final Sign Off: P&G 1-29-95, CP 01/29/95, [Signature] 21 Jan 95
P&G WJE City of Portland

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G _____ WJE _____ Sheet 1 of 1

Room Number on Plan: 3018 Building Room Number: HALL

Repair Designation/Description: NO WORK

Engineering Sketches / Calculations Reference: _____

Contractor: _____

INSPECTION RECORD

Repair Start Date: _____ / _____ / _____ By: _____

Intermediate Inspections:

Date	Time	By	Comment/Photos

JAN 30 1995

Repair Completion Date: 1 / 1 / _____ By: _____

Final Sign Off: OKP 1-29-95 P&G ICE 01/29/95 WJE [Signature] City of Portland

WJE 942566
WJE 141A

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G _____ WJE _____ Sheet 1 of 1

Room Number on Plan: 3038 Building Room Number: HALL

Repair Designation/Description: NO WORK REQUIRED

Engineering Sketches / Calculations Reference: _____

Contractor: _____

INSPECTION RECORD

Repair Start Date: _____ / _____ / _____ By: _____

Intermediate Inspections:

Date	Time	By	Comment/Photos

JAN 30 1995

Repair Completion Date: _____ By: _____

Final Sign Off: P&G 1-29-95 / WJE 01/29/95 City of Portland

WJE 940566
WJE 1916

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G _____ WJE _____ Sheet 1 of 1

Room Number on Plan: 3057 Building Room Number: HALL

Repair Designation/Description: NO WORK REQUIRED

Engineering Sketches / Calculations Reference: _____

Contractor: _____

INSPECTION RECORD

Repair Start Date: _____ / _____ / _____ By: _____

Intermediate Inspections:

Date	Time	By	Comment/Photos

JAN 30 1995

Repair Completion Date: _____ / _____ / _____ By: _____

Final Sign Off: DWP 1/29/95 / CP 01/24/95 [Signature]
P&G WJE City of Portland

WJE 242566
WJE 1410

SAM-H

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G _____ WJE _____ Sheet 1 of 1

Room Number or Plan: 200L Building Room Number: STORAGE

Repair Information/Description: FIRE STOP GWB NOLE TAKI

Engineering Sketches / Calculations Reference: _____

Contractor: Coastal

INSPECTION RECORD

Repair Start Date: 1 / 28 / 95 By: RB1

Intermediate Inspections:

Date	Time	By	Comment/Photos
1-28-95	3:30	DVP	GWB COMPLETE

JAN 30 1995

Repair Completion Date: 1 / 28 / 95 By: DVP

Final Sign off: DVP 1-28-95 / CP 01/28/95 [Signature] 01/28/95
P&G WJE City of Portland

WJE 942566
WJE1416

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G WJE Sheet 1 of 2

Room Number on Plan: 2003 Building Room Number: 204

Repair Designation/Description: _____

Engineering Sketches / Calculations Reference: _____

Contractor: _____

INSPECTION RECORD

Repair Start Date: ____/____/____ By: _____

Intermediate Inspections:

Date	Time	By	Comment/Photos
12/30/94	12:45	WJE	KNICKING OUT MASONRY TO ALLOW FOR CLEAN EDGES TO BRICK TO
1-28-95	PM UNK.	DWP	WORK COMPLETE

JAN 30 1995

Repair Completion Date: 1/28/95 By: DWP

Final Sign Off: DWP 1-28-95 P&G WJE City of Portland

WJE 942566 WJE1410

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G _____ WJE _____ Sheet 2 of 2

Room Number on Plan: 2003 Building Room Number: 204

Repair Designation/Description: Wall Penetrations Tasks 1-4

Engineering Sketches / Calculations Reference: W7/W4, W7/W2, W2

Contractor: C.M. CIMINO

INSPECTION RECORD

Repair Start Date: 12 / 30 / 94 By: RBJ

Intermediate Inspections:

Date	Time	By	Comment/Photos
<u>12/30/94</u>	<u>0730</u>	<u>RBJ</u>	<u>PREP For Repair BRICKS Being Removed.</u>
	<u>0830</u>	<u>RBJ</u>	<u>BRICKING @ SIDE TASK #2</u>
	<u>0946</u>	<u>RBJ</u>	<u>@ SIDE COMPLETE @ SIDE 1/2 BRICKED. TASK 2</u>
	<u>10 47</u>	<u>RBJ</u>	<u>TASK 2 complete</u>
	<u>1428</u>	<u>RBJ</u>	<u>Down ...</u>
			<u>TASK3 Laid 3 courses full depth (W/penetration)</u>
<u>1/3/95</u>	<u>0945</u>	<u>RBJ</u>	<u>TASK 4 REPAIR FULL & Misc. Notes</u>

JAN 30 1995

Repair Completion Date: UNKNOWN By: _____

Final Sign Off: WJP 1-28-95 ICP 01/28/95 [Signature] 1-28-95
 P&G WJE City of Portland

WJE 942566
WJE 1/1/95

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G _____ WJE _____ Sheet 1 of 6

Room Number on Plan: 3004 Building Room Number: _____

Repair Designation/Description: CEILING PROTECTION

Engineering Sketches / Calculations Reference: _____

Contractor: _____

INSPECTION RECORD

Repair Start Date: ____ / ____ / ____ By: _____

Intermediate Inspections:

Date	Time	By	Comment/Photos
<u>1-28-95</u>	<u>3:15</u>	<u>DWP</u>	<u>FIRESTOP COMPLETE</u>

REPAIR INSPECTION
JAN 30 1995

Repair Completion Date: 1 / 28 / 95 By: _____

Final Sign Off: DWP 1-28-95, CP 01/28/95, _____
P&G WJE City of Portland

WJE 942566
WJE 1/1/95

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G _____ WJE _____ Sheet 1 of 3

Room Number on Plan: 3006 Building Room Number: 302

Repair Designation/Description: Screw dry wall to ceiling

Engineering Sketches / Calculations Reference: _____

Contractor: _____

INSPECTION RECORD

Repair Start Date: 1/13/95 By: A. Rowe

Intermediate Inspections:

Date	Time	By	Comment/Photos
<u>1/13/95</u>	<u>9:55 AM</u>	<u>AR</u>	<u>work progressing - separate permit - not a Cimino job.</u>
<u>1-13-95</u>	<u>9:10 AM</u>	<u>T.M.</u>	<u>HANGING DRYWALL -</u>
<u>1-13-95</u>	<u>10:00 AM</u>	<u>T.M.</u>	<u>" " ONLY 1 LAYER RIGHT NOW. - CHECK ON HOW THEY ARE SECURING GYP. BD. TO BRICK WALL ON CORRIDOR SIDE.</u>

JAN 30 1995

Repair Completion Date: 1/28/95 By: T.M.

Final Sign Off: DVP 1-28-95 P&G ICP 01/28/95 WJE [Signature] City of Portland

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G _____ WJE _____ Sheet 2 of 3

Rcom Number on Plan: 3006 Building Room Number: 302

Repair Designation/Description: drywalling ceiling

Engineering Sketches / Calculations Reference: _____

Contractor: _____

INSPECTION RECORD

Repair Start Date: 1 / 17 / 95 By: A. Rowe

Intermediate Inspections:

Date	Time	By	Comment/Photos
<u>1/17/95</u>	<u>10:05 AM</u>	<u>AR</u>	<u>work nearly done</u>
<u>1/17/95</u>	<u>12:45 PM</u>	<u>AR</u>	<u>work goes on</u>
<u>1/17/95</u>	<u>1:50 PM</u>	<u>AR</u>	<u>work goes on</u>
<u>1/17/95</u>	<u>2:20 PM</u>	<u>AR</u>	<u>" " "</u>

Repair Completion Date: 1 / 28 / 95 By: T.M.M.

Final Sign Off: DVP 1-28-95 / CP 01/28/95 [Signature]
P&G WJE City of Portland

WJE 942544
V42 1416

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G _____ WJE _____ Sheet 3 of 3

Room Number on Plan: 3006 Building Room Number: 302

Repair Designation/Description: RM 302 CEILING REPAIR PROJECT -
PORTLAND HIGH SCHOOL

Engineering Sketches / Calculations Reference: _____

Contractor: COASTAL MECHANIC INC. / COASTAL DEVELOPMENT

INSPECTION RECORD

Repair Start Date: 1 / 18 / 95 By: _____

Intermediate Inspections:

Date	Time	By	Comment/Photos
1-18-95	7:30AM	T.M.	CHECK SEAL OF DRYWALL THAT ABUTTS TO BECK WORK.
1/18/95	9:25 am	AR	OK - framing work started
1/18/95	1:10 pm	KK	Framing Complete, duct work going in
1-18-95	2:11pm	DJ	Ductwork + 3/8" x Tape work complete
1/19/95			ductwork
1/19/95	1:12 pm		Step 2 - V. Sprinklers
1-19-95	2:00	DJ	sprinkler installation in progress
1-20-95	1:50 pm	DJ	Suggested ceiling gridwork installation
1-22-95	12:25 pm	GM	Painting + finish work IN wall

Repair Completion Date: 1 / 28 / 95 By: T.M.

Final Sign Off: P&G 1-28-95 / WJE 01/28/95 / City of Portland 1-28-95

WJE 942544
WJE 1410

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G _____ WJE _____ Sheet 1 of 1

Room Number on Plan: 3013 Building Room Number: _____

Repair Designation/Description: _____ (7. 1. 1. 2. Notes)

Engineering Sketches / Calculations Reference: _____

Contractor: _____

INSPECTION RECORD

Repair Start Date: _____ / _____ / _____ By: _____

Intermediate Inspections:

Date	Time	By	Comment/Photos

JAN 30 1995

Repair Completion Date: 1 / 28 / 95 By: DVP

Final Sign Off: 1-28-95 / CP 01/28/95 / [Signature] 01-28-95
P&G WJE City of Portland

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G _____ WJE _____ Sheet 1 of 1

Room Number on Plan: 3015 Building Room Number: MENP

Repair Designation/Description: TANK, USE W/274751

Engineering Sketches, Calculations Reference: _____

Contractor: _____

INSPECTION RECORD

Repair Start Date: _____ / _____ / _____ By: _____

Intermediate Inspections:

Date	Time	By	Comment/Photos
1-29-95	2:50	DKP	FIRETOP COMPL.

JAN 30 1995

Repair Completion Date: 1 / 29 / 95 By: DKP

Final Sign Off: DKP 1-26-95, CP 6/28/95, [Signature]
P&G WJE City of Portland

WJE 942566
WJE 1416

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G _____ WJE _____ Sheet 1 of 1

Room Number on Plan: 3065 Building Room Number: OFFICE

Repair Designation/Description: NO MORE WORK

Engineering Sketches / Calculations Reference: _____

Contractor: _____

INSPECTION RECORD

Repair Start Date: _____ / _____ / _____ By: _____

Intermediate Inspections:

Date	Time	By	Comment/Photos

JAN 30

Repair Completion Date: _____ / _____ / _____ By: _____

Final Sign Off: P&G 1-28-95 / WJE 1/28/95 / [Signature] 1-28-95
P&G WJE City of Portland

USE 942566
WJE 942566

Copyright 1995 by City of Portland, Oregon. All Rights Reserved. Printed in the USA. 95-001-01

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G _____ WJE _____ Sheet 1 of 10

Room Number on Plan: 3001 Building Room Number: _____

Repair Designation/Description: WALL PENETRATION PATCH

Engineering Sketches / Calculations Reference: _____

Contractor: _____

INSPECTION RECORD

Repair Start Date: _____ / _____ / _____ By: _____

Intermediate Inspections:

Date	Time	By	Comment/Photos
<u>1-28-95</u>	<u>1:50</u>	<u>DVP</u>	<u>Wall patch finished</u>

Repair Completion Date: 1 / 28 / 95 By: DVP

Final Sign Off: DVP 1/28/95 / CP 01/29/95 / [Signature] 1-28-95
P&G WJE City of Portland

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G _____ WJE _____ Sheet 1 of 1

Room Number on Plan: 3002 Building Room Number: 2250

Repair Designation/Description: NBL GIB/SI/ST JOIST CEILING ADDED AS A RESULT OF DAMAGE BY WORKMEN ABOVE. NOT NOTED ON 2ND FD. BOOK

Engineering Sketches / Calculations Reference: _____

Contractor: _____

INSPECTION RECORD

Repair Start Date: _____ / _____ / _____ By: _____

Intermediate Inspections:

Date	Time	By	Comment/Photos

JAN 30 1995

Repair Completion Date: _____ / _____ / _____ By: _____

Final Sign Off: 01/28/95 / 01/28/95 / 1-25-95
P&G WJE City of Portland

WJE #2566
WJE 1/16

SAM H.

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G _____ WJE ✓ _____ Sheet 1 of _____

Room Number on Plan: 2119 Building Room Number: BRIDGE - 2nd FLOOR

Repair Designation/Description: _____

Engineering Sketches / Calculations Reference: _____

Contractor: CIMINO

INSPECTION RECORD

Repair Start Date: _____ / _____ / _____ By: _____

FEB 21 1995

Intermediate Inspections:

Date	Time	By	Comment/Photos
1-18-95	8:10AM	T.M.	BRICKING UP WEST SIDE OF WALL - PREPING FOR 12"x24" PLATE - DID NOT FEEL ANY MORTAR IN GAP BEHIND NEW BRICK
1/18/95	9 ⁰⁰ AM	AR	work continues
1/18/95	10 ⁰⁰ AM	AR	work continues
1/18/95	11 ⁰⁰ AM	DR/KS/ML	work continues
1/18/95	12 ⁴⁰	KC	Work Continues
1-18-95	2:03	DS	Detail work in (Detail 1) states bolt's to use torque wrench @ 110 ft. lb cannot confirm
1-19-95	8:15 AM	T.M.	WEST SIDE APPEARS COMPLETE - CAN'T CONFIRM GAP BEHIND NEW BRICK WAS PACKED WITH MORTAR. QUESTIONS: VERIFY ADEQUATE BEARING OF 12x24 PLATE ON NEW BRICK @ VERIFY NEW BRICK HAS PROPER BRNG ON STEEL BEAMS.
1/19/95	11 ⁴⁵	KE/MW	NO WORK GOING ON

Repair Completion Date: 1 / 30 / 95 By: RGT

Final Sign Off: OKP 2-8-95 / CP 2-8-95 City of Portland

WJE 442546
WZ1110

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G _____ WJE Sheet 2 of _____
 Room Number on Plan: 2119 Building Room Number: Blinker 2nd fl
 Repair Designation/Description: @ 1-24-95 CL3.3
1-12-95 NVK (2nd Fl. F&D Bldg: connecting link) (Mason's Detail sheet)
 Engineering Sketches / Calculations Reference: _____
 Contractor: MINNO -

INSPECTION RECORD

Repair Start Date: 1, 19, 95 By: DT FEB 21 1995

Intermediate Inspections:

Date	Time	By	Comment/Photos
<u>1/19/95</u>	<u>1:30</u>	<u>VO/DJ</u>	<u>No work going on</u>
<u>1-19-95</u>	<u>3:20</u>	<u>DT</u>	<u>Bracing still in place / work drying</u>
<u>1-24-95</u>	<u>1:15</u>	<u>DT</u>	<u>3/4" threaded rod set into screen sleeve</u>
			<u>w/Epoxy HiTi Hit-C20 @ 16" OC</u>
<u>1-24-95</u>	<u>3:05 pm</u>	<u>DT</u>	<u>threaded rods installed (all 6) Epoxy setting up</u>
<u>1-25-95</u>	<u>7:10 A.M.</u>	<u>T.M.</u>	<u>11 RODS INSTALLED OVER DOOR ON WEST SIDE - PREPING TO LAY TILE.</u>
<u>1-25-95</u>	<u>8:20 AM.</u>	<u>T.M.</u>	<u>LAYING TILE</u>
<u>1/25/95</u>	<u>9:30 am</u>	<u>AR</u>	<u>work ceased for now</u>
<u>1/25/95</u>	<u>10:15 am</u>	<u>AR</u>	<u>" " " "</u>
<u>1/25/95</u>	<u>10:55 am</u>	<u>AR/MAJ</u>	<u>grouting Floor tiles</u>
<u>1/25/95</u>	<u>11:44</u>	<u>GRUN</u>	<u>" " " " still</u>
<u>1-25-95</u>	<u>12:45</u>	<u>GRUN</u>	<u>letting set up NOT working here now</u>

Repair Completion Date: 1, 30, 95 By: RAJ
 Final Sign Off: OP 2-8-95 / CP 2-8-95 / 02-08-95
 P&G WJE City of Portland

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G _____ WJE _____ Sheet 3 of 3

Room Number on Plan: 2119 Building Room Number: CORRIDOR 2nd Fl.

Repair Designation/Description: C.A.S.3

Engineering Sketches / Calculations Reference: _____

Contractor: MINO

INSPECTION RECORD

Repair Start Date: 1/18/95 By: TM

Intermediate Inspections:

Date	Time	By	Comment/Photos
1-25-95	2:00	WJE	Floor tiles down / no plates on $\frac{3}{4}$ " threaded rod.
1-26-95	8:15 AM.	T.M.	PLATES INSTALLED ON $\frac{3}{4}$ " THREADED RODS - NO PLATES INSTALLED ON RODS ABOVE DOORS.
1-26-95	3:21 pm	WJE	(Same) @ this time
1-27-95	3:00 pm	WJE	(Same)
1/28/95	12:55 pm	AR	Sheet rock being installed
1-4-95	UNK	DKY	SEE DLP INSP NOTES

Repair Completion Date: 1/30/95 By: RBJ

Final Sign Off: DKP 2-8-95 / CP 2-8-95 / 02-08-95 AR
P&G WJE City of Portland

WJE 942566
WJE 1110

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G _____ WJE _____ Sheet 2 of 2
Room Number on Plan: 6066 Building Room Number: Auto Shop (S-26)
Repair Designation/Description: Repair above door 2x6 + Brick + conduit

Engineering Sketches / Calculations Reference: _____

Contractor: _____

INSPECTION RECORD

Repair Start Date: 1 / 10 / 94 By: K. Cassell

Intermediate Inspections:

Date	Time	By	Reframing Door Comment/Photos
<u>1/10/95</u>	<u>11:30</u>	<u>KC</u>	<u>Inspected w/ E channels, 6x6 & 2x6 no spec sheet avail - No working right now</u>
<u>"</u>	<u>12:40</u>	<u>KC</u>	<u>Same</u>
<u>1-10-95</u>	<u>2:00</u>	<u>DS</u>	<u>(no work)</u>
<u>1-11-95</u>	<u>12:10</u>	<u>KC</u>	<u>MASONRY WORK IN PROGRESS ABOVE HEADERS SOME VOIDS NOTED</u>
<u>1-11-95</u>	<u>1:30</u>	<u>KC</u>	<u>NOBODY WORKING - REMAINS AS ABOVE</u>
<u>1-11-95</u>	<u>3:30</u>	<u>DS</u>	<u>(no work)</u>
<u>1/12/95</u>	<u>7:25 AM</u>	<u>ARL</u>	<u>Work Resumed</u>
<u>1-12-95</u>	<u>9:15</u>	<u>KC</u>	<u>WORK CLOSED IN ON CORRIDOR SIDE</u>
<u>1-12-95</u>	<u>12:00 PM</u>	<u>T.M.</u>	<u>WORK CLOSED IN - SHEETROCKED AND TAPED</u>

FEB 21 1995

Repair Completion Date: UNKNOWN / _____ By: _____
Final Sign Off: DUP 1-28-95 / OC 01-28-95
P&G WJE City of Portland

WJE 942586
WJENID

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G WJE Sheet 1 of 2

Room Number on Plan: E-066-1 Building Room Number: Auto shop

Repair Designation/Description: W-5 WALL Penetrations

Engineering Sketches / Calculations Reference: W5

Contractor: C.M. Cimino

INSPECTION RECORD

Repair Start Date: 12 / 23 / 94 By: J.F.M.

Intermediate Inspections:

Date	Time	By	Comment/Photos
12/24/94	6:10	J.F.M.	REMOVING OLD BRICKS HAVE TO REMOVE MORE BRICKS TO GET FULL WIDTH BEARING ON TOP OF PLATE.
12/24/94	9:05	J.F.M.	1 PIER DONE
12/27/94	3:10	J.F.M.	REMOVING MORE OLD BRICK
12/28/94	7:22	J.F.M.	2 nd PIER DONE PLATE going in
1-5-95	10:00	DJP	NEED TO CHECK EXHAUST GUST FOR FIRE DAMPER

FEB 21 1995
RECEIVED

Repair Completion Date: UNKNOWN By: [Signature]
 Final Sign Off: DJP 1-13-95 / J.F.M. 1/13/95 City of Portland

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G WJE _____ Sheet 2 of 2

Room Number on Plan: G066 Building Room Number: AUTO SHOP

Repair Designation/Description: NEW ENLARGED DOOR OPENING
TASK #2

Engineering Sketches / Calculations Reference: SPECIAL DESIGN

Contractor: C. M. CIMINO

INSPECTION RECORD

Repair Start Date: 12 / 9 / 94 By: MWC

Intermediate Inspections:

Date	Time	By	Comment/Photos
12/9/94	UNKNOWN	MWC	TWO CHANNELS INSTALLED CORRIDOR SIDE
12/12/94	0830	MWC	ONE WYTH OF BRICK REMOVED AUTO SHOP SIDE
12/13/94	UNKNOWN	MWC	SHOP SIDE TWO CHANNELS INSTALLED SMACERS BEING INSTALLED ON CORRIDOR SIDE.
12/13/94	UNKNOWN	RJS	LINTELS COMPLETE. TASK #2.

FEB 21 1995
MTCB

Repair Completion Date: UNKNOWN / _____ By: _____

Final Sign Off: DLP 1-13-95, DFM 1/13/95  1-13-95
P&G WJE City of Portland

WJE 942566
WJE 1416

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G _____ WJE _____ Sheet 1 of _____
 Room Number on Plan: 1033 Building Room Number: MENS ROOM
 Repair Designation/Description: WALL PENETRATION TASK #1, #2

Engineering Sketches / Calculations Reference: W4/W3
 Contractor: C.M. CIMINO

INSPECTION RECORD

Repair Start Date: 12 / 16 / 94 By: RBJ

Intermediate Inspections:

Date	Time	By	Comment/Photos
<u>12/16/94</u>	<u>UNKNOWN</u>	<u>RBJ</u>	<u>MOL DUCT W/ PIPES FILLED SOLID. IN DR</u>
<u>1-6-95</u>	<u>UNKNOWN</u>	<u>DVP</u>	<u>N WALL PENET. FILLED TASK #2</u>

FEB 21 1995
 RECEIVED

Repair Completion Date: 1 / 5 / 95 By: RBJ
 Final Sign Off: DVP 1-6-95 / OP 06 JAN 95 [Signature] 1-6-95
 P&G WJE City of Portland

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G _____ WJE _____ Sheet _____ of _____

Room Number on Plan: 1033 Building Room Number: MENS RM

Repair Designation/Description: WINDOW INFILL Full DEPTH (4) wythes

congrated TIES @ SIDE REBAR @ SIDE EVERY 16" O.C. VERTICALLY

Engineering Sketches / Calculations Reference: _____

Contractor: C. M. CIMINO

INSPECTION RECORD

Repair Start Date: _____ / _____ / _____ By: _____

Intermediate Inspections:

Date	Time	By	Comment/Photos
<u>12/30/94</u>	<u>1300</u>	<u>RBJ</u>	<u>DISCUSS TIES AND JOINT SIZE AS PER TO USE "2" JOINT. THIS IS SMALLEST POSSIBLE BASED ON SIZE OF BRICK.</u>
	<u>1450</u>	<u>RBJ</u>	<u>Laid (8) COURSES OF BRICK</u>
<u>12/31/94</u>	<u>0730</u>	<u>RBJ</u>	<u>TIE BRICK AND REINFORCING TIES INSTALLED 32"</u>
	<u>0850</u>	<u>RBJ</u>	<u>TIE BRICK AND REINFORCING TIES INSTALLED 48"</u>
	<u>1055</u>	<u>RBJ</u>	<u>TIE BRICK AND REINFORCING TIES INSTALLED 60"</u>
<u>1/3/95</u>	<u>0815</u>	<u>RBJ</u>	<u>PREP FOR LAYING BRICK INSTALLED CONGRATED TIES</u>

FEB 21 1995
RECEIVED

Repair Completion Date: UNKNOWN / _____ / _____ By: _____

Final Sign Off: DLP 1-6-95 / CP 01-06-95 (Signature) 1-6-95
P&G WJE City of Portland

WJE 942566
WJE1416

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G _____ WJE _____ Sheet 1 of 1

Room Number on Plan: 1084 Building Room Number: 132

Repair Designation/Description: TASKS 1-3 WALL PENETRATIONS

Engineering Sketches / Calculations Reference: W7, S

Contractor: C. McMINO

INSPECTION RECORD

Repair Start Date: 12 / 8 / 94 By: RBJ

Intermediate Inspections:

Date	Time	By	Comment/Photos
<u>12/8/94</u>	<u>0930</u>	<u>RBJ</u>	<u>PLACING SIEEVES. TOLD MASON TO RELOCATE ELECTRICAL BOX TO ALLOW FOR PROPER INSTALLATION</u>
<u>1-6-95</u>	<u>UNKNOWN</u>	<u>DVP</u>	<u>CEILING HOLES NOT FIRE STOPPED</u>
<u>1-9-95</u>	<u>UNKNOWN</u>	<u>DVP</u>	<u>FIRE STOPPING INSTALLED</u>

FEB 21 1995
ELECTRICAL

Repair Completion Date: 1 / 9 / 95 By: DVP

Final Sign Off: DVP 1-9-95 / CP 09 JAN 95
P&G WJE City of Portland

WJE 942566
WJE141a

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G ¹⁰⁸⁴ WJE Sheet 1 of 3

Room Number on Plan: ~~132~~ Building Room Number: 132 / 133

Repair Designation/Description: 1-11-95 - NO DESIGN SUBMITTED 8:00 a.m.

Engineering Sketches / Calculations Reference:

Contractor: C.M. CIMINO

INSPECTION RECORD

Repair Start Date: 1 / 11 / 95 By: T.M.

Intermediate Inspections:

Date	Time	By	Comment/Photos
1-11-95	7:55 a.m.	T.M.	KNOCKING OUT BRICK OVER CORRIDOR SIDE DOOR
1-11-95	9:00 am	AR	same activity as above
1-11-95	10:10 AM	AR	same activity as above
1-11-95	11:30 AM	KC	SAME WIP
1/11/95	12:15 pm	KC	ALL work out - Lintel Being Installed - Still Laying Ledge While Workers @ Lunch
1/11/95	1:30 PM	KC	Lintel in place over - Brick in - NEVER SAW Lintel BEARING
1-11-95	3:20	DJ	Hallway side looks completed may need finish work / class rm side looks to need lintel / will check w/engin.
1-11-95	3:40	DJ	Yes lintel class rm side FEB 2 1 1995
1-12-95	9:15	KC	Closed in on corridor side - NO work going on - FEB 2 1 1995
1/13/95	8:00	AR	OK. TRIM being removed

Repair Completion Date: UNKNOWN 1 By:

Final Sign Off: P&G WJE City of Portland 1-27-95 / CR 28 JAN 95 / P.L. Hoffer 28 JAN 95

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G _____ WJE _____ Sheet 2 of 3

Room Number on Plan: _____ Building Room Number: 33/132

Repair Designation/Description: NO Design yet

1-13-95 Worker states Design is in / see R-Jones / Design is 1884A-Rm 132

Engineering Sketches / Calculations Reference: _____

Contractor: VIMINO

INSPECTION RECORD

Repair Start Date: 1/11/95 By: T.M.

Intermediate Inspections:

Date	Time	By	Comment/Photos
1-13-95	10:30 AM	T.M.	KNOCKING OUT BRICK ON INSIDE WALL OF CLASS ROOM.
1-13-95	11:25	A.S.	" "
1-13-95	1:05	A.S.	REMOVING 1 MORE COURSE TO ACCOMMODATE 6" LINTELS (ROSKETUI) 3 LINTELS @ 4" x 4"
1-13-95	1:50	DJ	Brick removal in progress
1-13-95	2:05 pm	DJ	1st lintel set in place. (bearing OK)
1-13-95	3:15 pm	DJ	2nd lintel in place " "
1-13-95	3:30 pm	DJ	3rd lintel in place all brick work completed
1-16-95	0915	RBJ	Installing GWB AROUND STAIR opening
1-16-95	1035	RBJ	AGREED TO USE GWB STR OVER DOOR TO STAIR opening.
1-16-95	1525	RBJ	OPENING CLOSED ONLY (2 LAYERS 5/8" GWB ON WALL) NO opening for light switch.

Repair Completion Date: 1/13/95 By: DJ

Final Sign Off: WJE 1-27-95 / CP 20 JAN 95 / [Signature] / 1/28/95
 P&G WJE City of Portland

WJE 942566
 WJE 110

FEB 21 1995

4

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G _____ WJE _____ Sheet 3 of 3

Room Number on Plan: 133 Building Room Number: 133/132

Repair Designation/Description: Re-installing trim
(elec. trouble shooting)

Engineering Sketches / Calculations Reference: replacing trim

Contractor: _____

INSPECTION RECORD

Repair Start Date: 1 / 23 / 95 By: A Rowe

Intermediate Inspections:

Date	Time	By	Comment/Photos
1/23/95	8 ⁰⁰ Am	AA	work started
1/23/95	9 ¹⁵ Am	AA	work goes on
1/23/95	10 ⁰⁰ Am	AA	" " "
1-23-95	11:05	DJ	Finish trim repair in progress
1-23-95	1:30	DJ	OK Trim Finished / electrician in rm

Repair Completion Date: 1 / 23 / 95 By: _____

Final Sign Off: wp 1-21-95 / d 28 5/19/95 A. Rowe 28 Jan/95
P&G WJE City of Portland

WJE 942566
WJE/INL

FEB 21 1995

RECEIVED

P.H.S. LINTEL DESIGN
DOOR 1084 A - RM 132
1ST FLR WEST

JAM/DKP 1/13/95

DOOR 3'-4" W x 7'-0" H:

A. CORRIDOR SIDE:

WALL THICKNESS = 8"

LINTEL LENGTH = 5'-0" (MIN.)

LINTEL SIZE = (2) L4x3 1/2"x 5/16"




B. CLASSROOM SIDE:

WALL THICKNESS = 12"

LINTEL LENGTH = 8'-10" (MIN.)

LINTEL SIZE = (3) L6x3 1/2"x 3/8"



RECEIVED BY EXTON

FEB 21 1995

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G _____ WJE _____ Sheet 1 of 1

Room Number on Plan: 3003-1 Building Room Number: 302

Repair Designation/Description: W34W7

Masonry 1 layer

Engineering Sketches / Calculations Reference: _____

Contractor: C.M. Cimino

INSPECTION RECORD

Repair Start Date: 12 / 21 / 94 By: TFM

Intermediate Inspections:

Date	Time	By	Comment/Photos
<u>12/21/94</u>	<u>8:37</u>	<u>T.M.</u>	<u>Mason Dropped Flashlight DOWN chase</u>
<u>12/21/94</u>	<u>9:34</u>	<u>T.M.</u>	<u>Finishing up Pointing</u>
<u>12/21/94</u>	<u>10:55</u>	<u>TM</u>	<u>Masonry Pointed conduit Fire STOPPED.</u>

Repair Completion Date: 12 / 21 / 94 By: [Signature]

Final Sign Off: [Signature] 1-28-95 1-28-95 P&G WJE City of Portland

WJE 942566

FEB 21 1995

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G _____ WJE _____ Sheet 1 of 1
Room Number on Plan: 3061 Building Room Number: 305
Repair Designation/Description: TASKS 1-3 WALL & CEILING
PENETRATIONS
Engineering Sketches / Calculations Reference: W2, W7
Contractor: C. M. Cimino

INSPECTION RECORD

Repair Start Date: 11 / 29 / 94 By: RAJ


Intermediate Inspections:

Date	Time	By	Comment/Photos
<u>11/29/94</u>	<u>unknown</u>	<u>RAJ</u>	<u>1ST COAT of PLASTER on wire MESH Applied FROM TOP</u>
<u>11/30/94</u>	<u>unknown</u>	<u>RAJ</u>	<u>2ND COAT FROM TOP SMALL HOLES PATCHED</u>
<u>1-26-95</u>	<u>10:00</u>	<u>DWP</u>	<u>FINAL REPAIR OK</u>

FEB 21 1995

Repair Completion Date: unknown / _____ By: _____
Final Sign Off: DWP 1-26-95 / CP 01-26-95 / [Signature] Feb-95
P&G WJE City of Portland 95

WJE 942566
WJE 1410

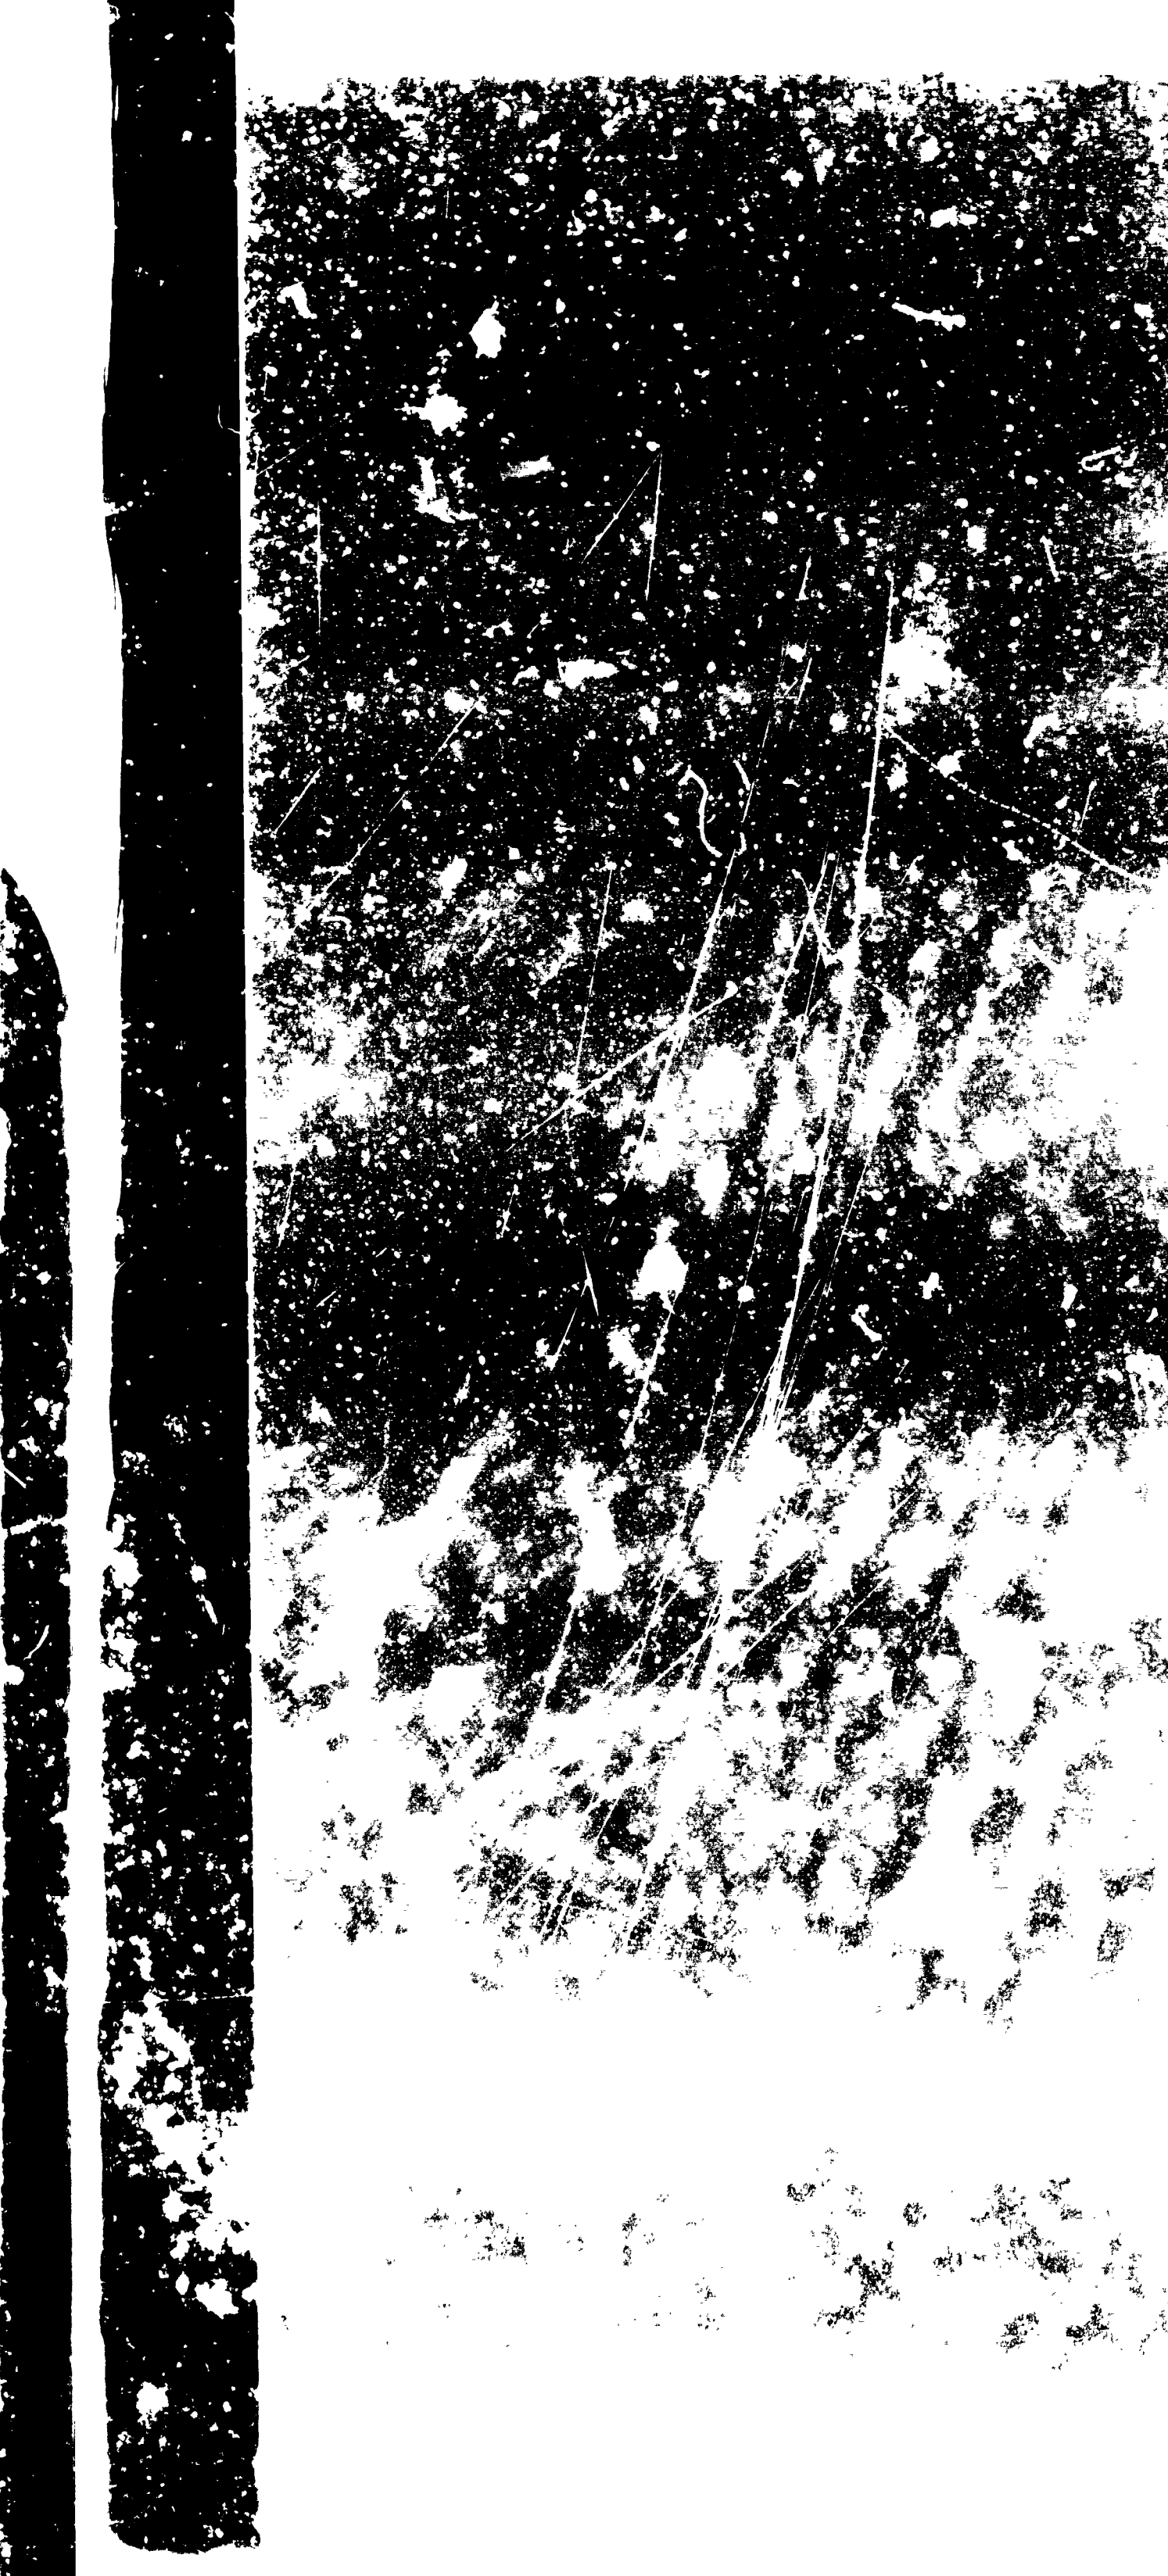

SAM 11

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G WJE Sheet 1 of 1

Room Number on Plan: 6025 Building Room Number: VAULT

Repair Designation/Description: CEL. PENETS. FIRESTOP

Engineering Sketches / Calculations Reference:

Contractor:

INSPECTION RECORD

Repair Start Date: 2 / 8 / 95 By: DUP

Intermediate Inspections:

Date	Time	By	Comment/Photos
2-8-95	11:10	DUP	FIRESTOP comp.

FEB 21 1995

Repair Completion Date: 2 / 8 / 95 By: DUP

Final Sign Off: DUP 2-8-95 / OP 2-8-95 / [Signature] 02-08-95
P&G WJE City of Portland

WJE 942566
WJE1416

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G / WJE Sheet 1 of 1

Room Number on Plan: G-2-B Building Room Number: STORAGE

Repair Designation/Description: FIRESTOP-LEAK, PENETS.

Engineering Sketches / Calculations Reference: —

Contractor: CHAIND

INSPECTION RECORD

Repair Start Date: 2 / 8 / 95 By: DYP

Intermediate Inspections:

Date	Time	By	Comment/Photos

FEB 21 1995

Repair Completion Date: 2 / 8 / 95 By: DYP

Final Sign Off: DYP 2-8-95 / OP 2-8-95 / [Signature] 02-08-95
 P&G WJE City of Portland

WJE 942566
 WJE 1414

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G _____ WJE _____ Sheet / of /

Room Number on Plan: G-031 Building Room Number: _____

Repair Designation/Description: NO WORK REQUIRED

Engineering Sketches / Calculations Reference: _____

Contractor: _____

INSPECTION RECORD

Repair Start Date: ____/____/____ By: _____

Intermediate Inspections:

Date	Time	By	Comment/Photos

FEB 21 1995
RECEIVED

Repair Completion Date: ____/____/____ By: _____

Final Sign Off: DVP 2-8-95 / CP 2-8-95 / 02-08-95 [Signature]
 P&G WJE City of Portland

WJE 942566
WJE 1410

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G WJE Sheet 1 of 1

Room Number on Plan: G032 Building Room Number: HALL @ BOOK STORAGE

Repair Designation/Description: BAR JOIST, PIPE HANGERS, CEILING WALL PENETRATIONS TASKS 1-6

Engineering Sketches / Calculations Reference: _____

Contractor: C.M. CLINE

INSPECTION RECORD

Repair Start Date: _____ / _____ / _____ By: _____

Intermediate Inspections:

Date	Time	By	Comment/Photos
2-8-95	10:10	DJP	ONE JOIST NOT GROUDED; TASKS 3, 4, 5, 6
2-8-95	10:42	DJP	JOIST GROUDED
2-8-95	10:45	CP	FIRST BRIDGING TIE-OFF COMPLETED

FEB 21 1995

Repair Completion Date: 2 / 8 / 95 By: DJP

Final Sign off: DJP 2-9-95 / CP 2-8-95 / [Signature] 2-08-95
 P&G WJE City of Portland

WJE 942566
WJE 1416

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G _____ WJE _____ Sheet 1 of _____

Room Number on Plan: G038 Building Room Number: Old Electric Room

Repair Designation/Description: Repair holes in walls
2 holes

Engineering Sketches / Calculations Reference: _____

Contractor: _____

INSPECTION RECORD

Repair Start Date: 1 / 13 / 95 By: Alowe

Intermediate Inspections:

Date	Time	By	Comment/Photos
<u>1/13/95</u>	<u>8⁰⁰ AM</u>	<u>AR</u>	<u>1st hole nearly bricked up</u>

FEB 21 1995

Repair Completion Date: UNKNOWN / _____ By: _____

Final Sign Off: DKP 2-8-95 / CP 2-8-95 / 02-08-95 / [Signature]
P&G WJE City of Portland

WJE 942566
WJE 191a

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G / WJE / Sheet 1 of 3
 Room Number on Plan: 6038 Building Room Number: _____
 Repair Designation/Description: 6038-2 (WJTE)

Engineering Sketches / Calculations Reference: W3
 Contractor: CIMINO

INSPECTION RECORD

Repair Start Date: 1, 13, 95 By: A.S.

Intermediate Inspections:

Date	Time	By	Comment/Photos
<u>1.13.95</u>	<u>1:00</u>	<u>A.S.</u>	<u>COMPLETED ✓</u>

RECEIVED
 FEB 21 1996

Repair Completion Date: 1, 13, 95 By: A.S.
 Final Sign Off: WJP 2-8-95 , CP 2-8-95 [Signature] 2-8-95
 P&G WJE City of Portland

WJE 942566
 WJE1416

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G / WJE / Sheet 1 of 3

Room Number on Plan: 6030 Building Room Number: _____

Repair Designation/Description: 6030-1 (WATER)

Engineering Sketches / Calculations Reference: 43

Contractor: CIMINO

INSPECTION RECORD

Repair Start Date: 1 / 13 / 95 By: A.S.

Intermediate Inspections:

Date	Time	By	Comment/Photos
1-13-95	12:55	A.S.	COMPLETED ✓

FEB 21 1995
RECEIVED

Repair Completion Date: 1 / 13 / 95 By: A.S.

Final Sign Off: P&G 2-8-95 / WJE 2-8-95 / [Signature] 02-08-95
City of Portland

WJE 942566
WJE 1414

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G ✓ WJE ✓ Sheet 1 of 1
Room Number on Plan: 1001 Building Room Number: Cafeteria other side of 1001^B
Repair Designation/Description: W6 Per Jim Stewardless -
no design designated (1001-B other side)
Engineering Sketches / Calculations Reference: 1001-B W6 (OTHER
SIDE IN CAF.)
Contractor: Limino

INSPECTION RECORD

Repair Start Date: ____/____/____ By: _____

Intermediate Inspections:

Date	Time	By	Comment/Photos
1-9-95	11:20 a.m.	TN./KC	old brick work removed - Preping for new brick work & repair
1-9-95	1:30	KC/DJ	unchanged
1/10/95	8:10 AM	Glowe	cleaning out - preparing for brickwork
1-10-95	10:05 AM	T.M.	PLATE NOT INSTALLED YET - STILL PREPING
1-10-95	11:35 AM	KC	" " " " " "
1-10-95	3:10 pm	DJ	plate installation in progress (check 1-11-AM)
1/11/95	12:05 pm	KC	Room locked - DARK - Could NOT check
1-11-95	3:10	DJ	Room locked -
1-12-95	9:30	JLC	Locked

FEB 21 1995

Repair Completion Date: unknown / ____ / ____ By: _____

Final Sign Off: WJP 1-29-95 / CP 01-29-95 / [Signature] 1-29-95
P&G WJE City of Portland

FINAL SIGN OFF IS CONTINGENT ON REPAIR OF OLD VENT OPENING, (COVER W/ 2 LAYERS GIBB) BY FEB. VACATION

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G _____ WJE _____ Sheet / of _____

Room Number on Plan: 1001 Building Room Number: CAFETERIA

Repair Designation/Description: TASK 1-8 WALL PENETRATIONS

Engineering Sketches / Calculations Reference: _____

Contractor: CMC

INSPECTION RECORD

Repair Start Date: 1 / 5 / 95 By: JPS

Intermediate Inspections:

Date	Time	By	Comment/Photos
1/5/95	1030	JPS	#1001-4 Right half complete chipping and level SDR. REMOVING DUCT.
1/5/95	1300	JPS	#1001-4 COMPLETE, 1001-7 chipped out old BECK STANDED building @ duct pipes RE-INSTALLING DUCT
1/5/95	1500	JPS	1001-7 complete building pier till margin to fill in 4" shaft web. Reinstalling ductwork.
1/9/95	0900	JPS	1001-8 Told contractor that for installation was unacceptable and must be redone so R is level
1/9/95	0930	JPS	Told THAT W6 Repair could BE USED on South Side of #1001-7 and 8.
1/6/95	1545	JPS	1001-7 DUCT REMOVED. R 15 IN. NOTCH TO ALLOW CONDUIT WAS APPROVED THERE IS 4" OF BEARING 1001-8 LATER LIKE PLATE IS NOT ADEQUATELY SUPPORTED. Need to check proper installation.

FEB 21 1995

Repair Completion Date: UNKNOWN _____ By: _____

Final Sign off: DKP 1-29-95 P&G ICP 01-29-95 WJE [Signature] City of Portland

WJE 942566
WJE 1416

REPAIR INSPECTION FORM

Portland High School Repair Project

Project Team Member: P&G WJE ✓ Sheet 1 of 3

Room Number on Plan: _____ Building Room Number: 100.1 DINING HALL

Repair Designation/Description: E1-1 & SECTION (1)

Engineering Sketches / Calculations Reference: (10M)

Contractor: KSC KNOWLES

INSPECTION RECORD

Repair Start Date: 1, 24, 95 By: A.S.

Intermediate Inspections:

Date	Time	By	Comment/Photos
1.26.95	12:47	A.S.	INSTALLING BEARINGS A1 @ 2ND FLOOR (A1 = 1" x 3" x 3/8") A325 IS, FLAT WASHER, LOCK WASHER NO TORQUE, METAL TO METAL.

FEB 21 1995

Repair Completion Date: UNKNOWN By: _____

Final Sign Off: DKP 1-29-95 / CP 01-29-95 / [Signature] 01-29-95
P&G WJE City of Portland
