

September 06, 2016

City of Portland 389 Congress St Suite 208 Portland, ME 04101

RE: Asylum Sports Bar - Business & Construction Interaction

It is Consigli Construction's intention to turn over the sports bar, kitchen and basement bathrooms (hence forth know an Phase 1A) to Asylum to open for business on Thursday 9/8/16. All required life safety and food service requirements will have been met and a final inspection scheduled.

Upon completion of Phase 1A, Consigli will still be required to install other materials with long lead times or construction durations that were not able to be completed in Phase 1A that will continue until the end of this year. These items will be installed/completed during off hours on Mondays and Tuesdays as well as mornings Wednesday through Friday. These items include:

- 1. New doors and hardware for openings 156, 102, and 102A
- 2. New windows (R) looking into Stair 155 with new solid surface backsplash
- 3. New bar/lobby glass door with sidelights 101A
- 4. New entry canopy's over entrances 101 and 105
- 5. Walk-in cooler addition (103, 104 and 104A)
- Lower kitchen storage area finishes and existing cooler demolition in room 039
- 7. Fitout of basement office room 029 adjacent the bathrooms
- 8. Access control, CCTV and intrusion alarms
- 9. New gas fired hot water heaters in the basement
- 10. Gas service upgrade
- 11. New lighting inverter
- 12. Replacement RFU 1 for the sports bar

The construction of the cooler area outside the kitchen is ongoing and, as a result, the existing opening 103 going into the cooler vestibule has been closed off with plywood until its completion later this year. Asylum kitchen staff will continue to use the existing cooler in basement kitchen storage 039. Upon completion of the new cooler/freezer the old one will be demolished off hours and new finishes (flooring and wall FRP) will be installed in 039.

The new steel canopies over entrances 101 and 105 will be constructed one at a time so there will be one primary entrance/exit at all times. The sports Bar entrance will be completed first allowing public access to the sports bar through entrance 105. The Sports bar door will only be used for emergency egress.

Upon completion of the sports bar entrance 101, we will begin the canopy at the lobby entrance 105. This door will only be used as an emergency exit as will the rear lobby door going out to the back alley.

Completely separated from the occupied sports bar and kitchen is the renovation of the dance floors in the basement and the first floor as well as the new addition henceforth known as Phase 3. This work will be

ongoing Monday through Friday until April 2017. The addition construction will be accessed from outside the existing building and will not interact directly with the occupied space. However, there will be required utility outages for swapovers and tie-ins.

The existing building renovation between the sports bar and the new addition in currently ongoing in the basement and the first floor. This construction will also be ongoing Monday through Friday and will be completed with the Phase 3 addition with the exception of the basement dance floor which is listed as Phase 2 and will be completed by the end of this year. These areas will be isolated from the occupied areas via temporary partitions and construction doors that will be locked after 5:00 when construction ends for the day. Consigli will access these spaces vial the lobby entrance to access the 1st and second floor.

Throughout all construction in all phases, the existing fire suppression and fire alarm system will be active. The main panel will be temporarily relocated within the construction space until the new permanent walls are constructed in Phase 3. All fire hydrants will be fully accessible from outside the fence lines.

Please see the attached plan for the logistics of the construction operation.


Regards,

Consigli Construction Co., Inc.


Chris Brown

Senior Project Manager

cc: Rob Frank – WBRC, Dave Thomas – Consigli Tedlum Associates 1ST FOOR

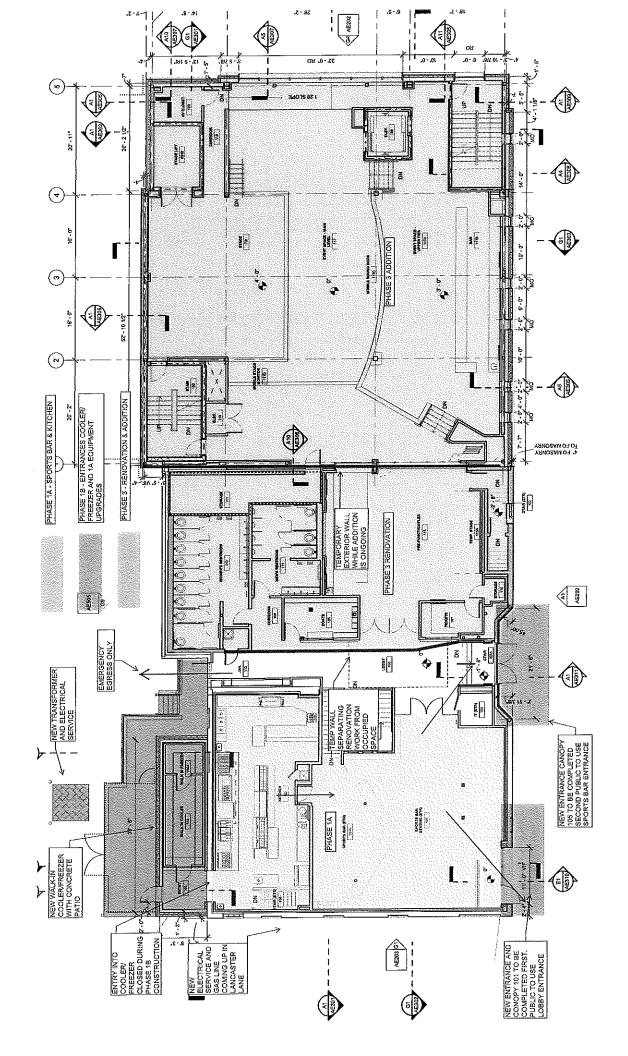

MASEMENT

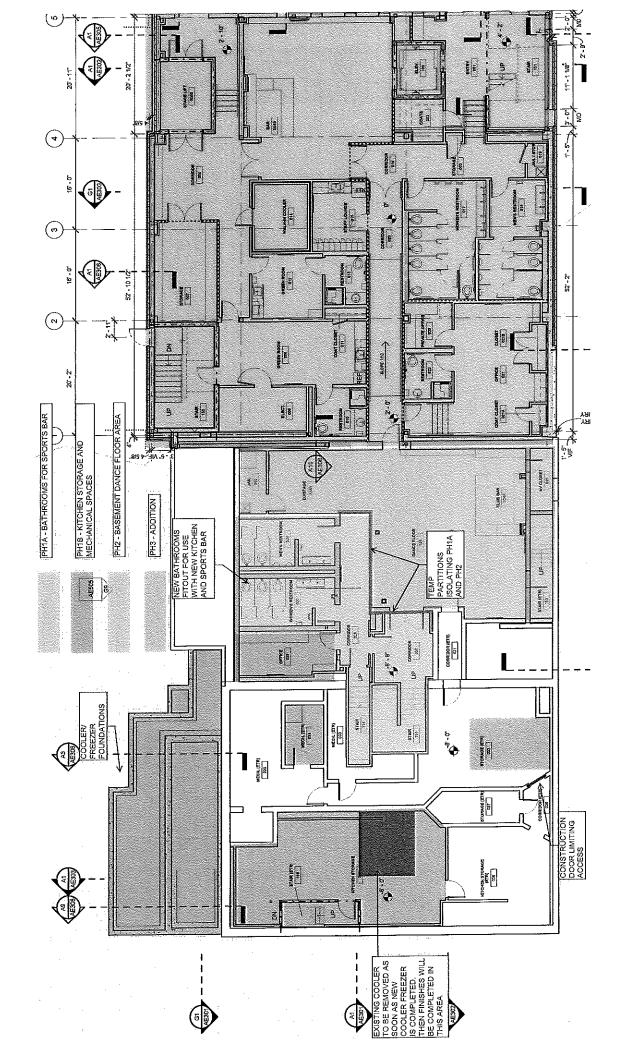



September 2, 2016

Attn: Consigli Contractors C/o Asylum 121 Center Street Portland, ME 04101

Dear Consigli Contractors,

This letter is to inform you that on September 2, 2016, we completed **partial** installation, programming and testing of the new fire alarm devices added in the Asylum Building located at 121 Center Street Portland, Maine. Partial is defined as Phase 1A, which included the sports bar, sports bar kitchen (Ansul & Hood), basement bathrooms, main entry hall and the full building sprinkler system (flow, pressure & tamper). These new fire alarm devices were tied into the new fire alarm control panel. These new devices were installed, programmed and tested to NFPA 72 & NFPA 2009 standards with signals sent to and received at our central monitoring station. All these devices were found to be fully functional at that time.

Should you have any questions or comments regarding this matter, please feel free to contact me at (207) 846-3350.

Sincerely,

Steven L Hayden General Manager

cc: Acct. File

Affordable Fire Protection 277 Spears Corner Road West Gardiner, Me. 04234 207-512-4464



*Portable Fire Extinguishers Service
*Restaurant Suppression Systems
*Fuel Island Suppression Systems
*Entergency & Exit Lighting
*39 Hour Emergency Service

	The state of the s
Date	
tra	(A) 1. /a /

Kitchen Range Hood Report

Customer Name:	<u> </u>	. × 1/4	
- Site Address:			
	180 Steve 1808 (24) 18	j i j Bernaria kana k ana kana kana kana kana	
	ordance w/mfg ut listing	Yes (No(if not UL 300, see Other)	
Manufactures, quantity & size of each cylinder bottle?		Contable & March Later Care	
Manufacturer date: Hydrostatic test date		200 State St	
Location of each cylinder pottle? Any visible rust or physical damage on each bottle?		Valle A Land	
Any visible rust or phy	steat damage on each votes.	Yes / (No.) - (<u>(if yes, see othec)</u> - (Yés / No	
 Cylinder & bracker securely mounted & cleaned? Pressure gauge on cylinder bottle in proper operating range 		The state of the s	
Pressure gauge on cyul	nder oome in proper operating rang ? Amerex curicidge in operating rang		
Ansur carmoge weight	KRS or XV: data Co2 actuator carte	Adra nantanado - An N. A	
Type of Auto Shut Dos		15åsV Electric / Both	
Type of Auto Stratton	sus He an automatic ges shus-off velve?	and the second s	
it gas appliantes, is un	no en amonano gas ameros vaces. Estado do amonostio electricai vietro		
If electric appliances, is there an automatic electrical start of is system hooked up to building fire alarm system?		₹ 8 87 No	
Does system have a manual pull station?		Yes ANO (II) No. See Other)	
Pull station tested, sealed, tagged		Yoskino / N / A	
Total tength of excess cable at manual pull release?			
FMT conduit and link	tiae free of grease build up?	Yes/ No (If No. See Other)	
Are all comer quiley or	aps in place on all EMT. (C/V. P/S &		
Piping and Nozzles its	e of grease build up f/or removed &	eteaned (Yesy No	
All nozzles checked, ar	id cleaned and have proper caps / se	els? (Yes/140	
All piping, ENT & nozzles properly brookered, senure & fig		ght? (Yésyi No	
Oues hood, thick & plenum have proper type & quantity of nozzies? Yes/ No (If No. See Other)			
Total number of pozzle	c? Daul=∅ Plenum=+/	Applianes	
Total number of fusible links changed? 360 K/A/MR. 7450 K/A/MC 500 K/A/MIL			
Fan Weming Sign on Hood?		1987 No.	
System reset for proper operation & safety removed?		1/03/No	
System bottle properly tagged & punched?		(Yes# No	
Does site have a Class K. fire exchaguisher for each hood?		(Yes A No <u>(If Ixo. See Other)</u>	
Customer shown how to manually operate system?		MAN No	
Exhaust dan la working		72\$7 No	
Cooking appliance loc	ations: Lait to Right & Nozzie po	1108 11 14 1 4 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1	
Comments / Recomme	مانند که در		
	andanous. en Red Taged / out of Compliance/V	Ass:	
A FD regression	ade moradina non comuliant system	ro III. 300 Standards	
AFP recommends upgrading non compliant system to UL 300 Standards Appliances shown above need additional negates to be properly professed & up to Code			
2) Other			
427 Sec. (COV)	The second secon	The second secon	

Reviewed & Received By
