

## Schedule / Notes

All traffic singage and lane diversions to be done per direction of the Portland Traffic Department

Signage and lane diversions to be established the morning of the work


Road signs and diversions to be in place 24 hrs/day.

Two way traffic to be maintained on Congress St at all times.

Work is schedule to begin 9/8/20.

Work is scheduled to be completed 10/23/20

## Overall Work Areas

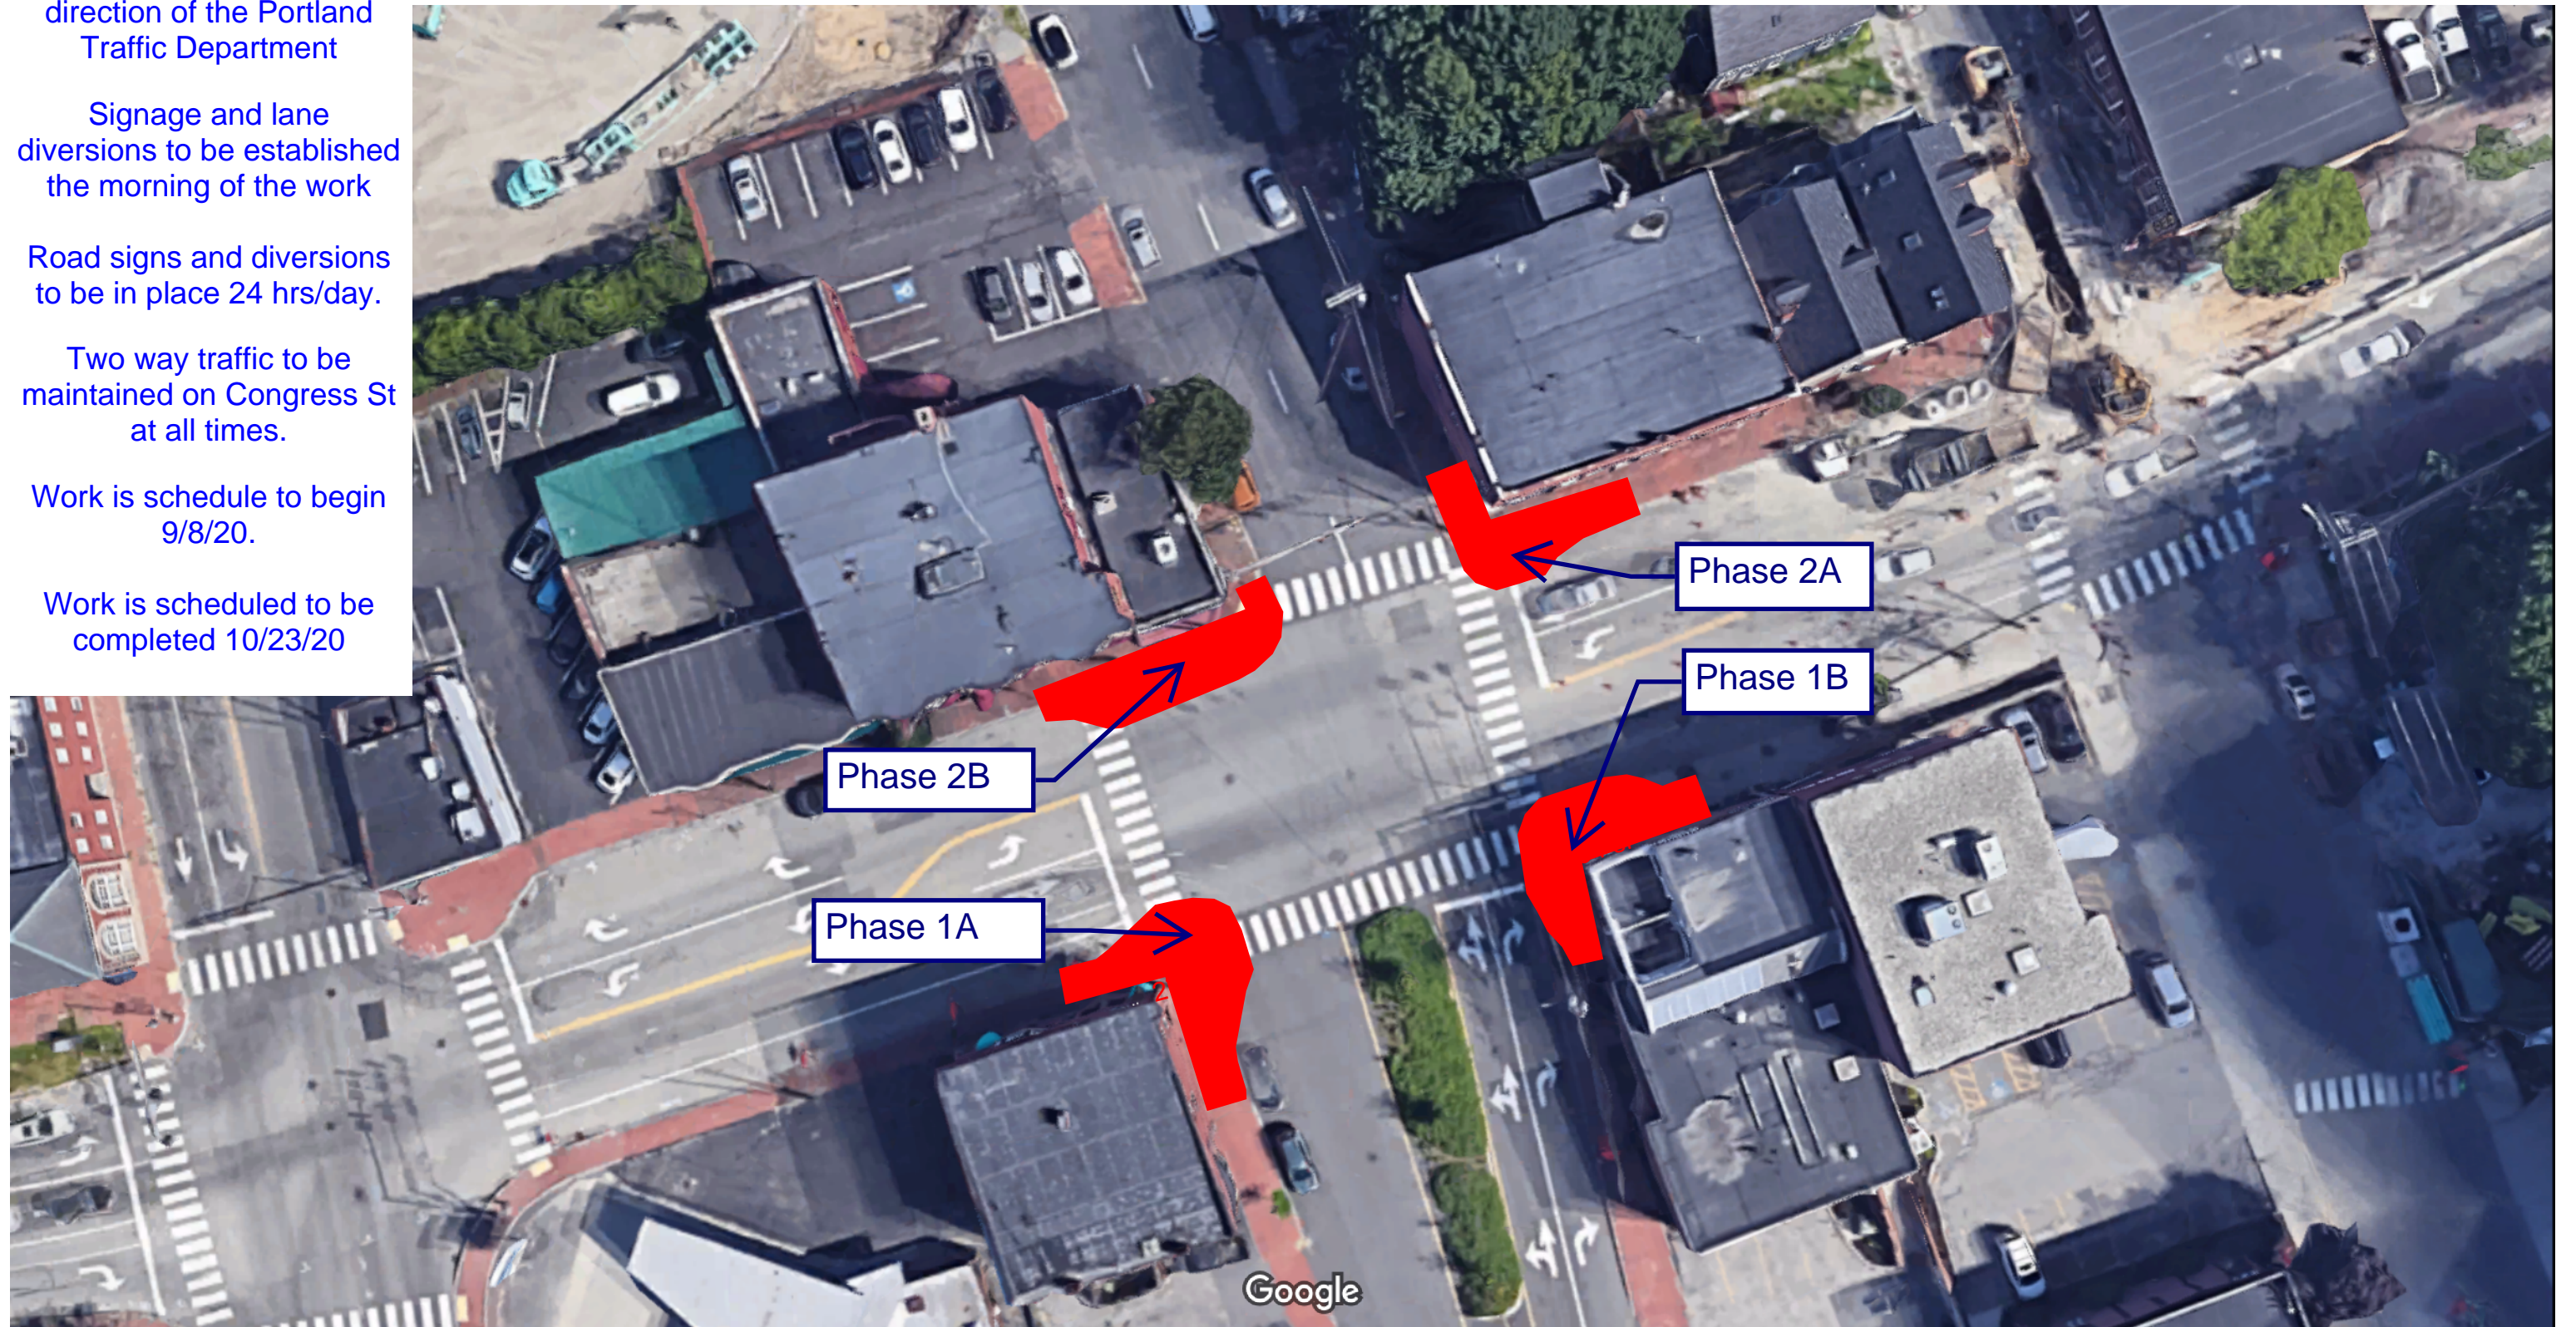

Imagery ©2020 Google, Map data ©2020 50 ft

## Valley/Congress Intersection Work

**Turner**

# Phase 1A - Congress St - Inbound 9/8/20-9/16/20

## Schedule / Notes

All traffic singage and lane diversions to be done per direction of the Portland Traffic Department

Signage and lane diversions to be established the morning of the work

Road signs and diversions to be in place 24 hrs/day.

Two way traffic to be maintained on Congress St at all times.



Pedestrian Route

Sidewalk Closed

## Valley/Congress Intersection Work

# Phase 1B - Congress St - Inbound 9/17/20-9/25/20


## Schedule / Notes



All traffic singage and lane diversions to be done per direction of the Portland Traffic Department

Signage and lane diversions to be established the morning of the work

Road signs and diversions to be in place 24 hrs/day.

Two way traffic to be maintained on Congress St at all times.

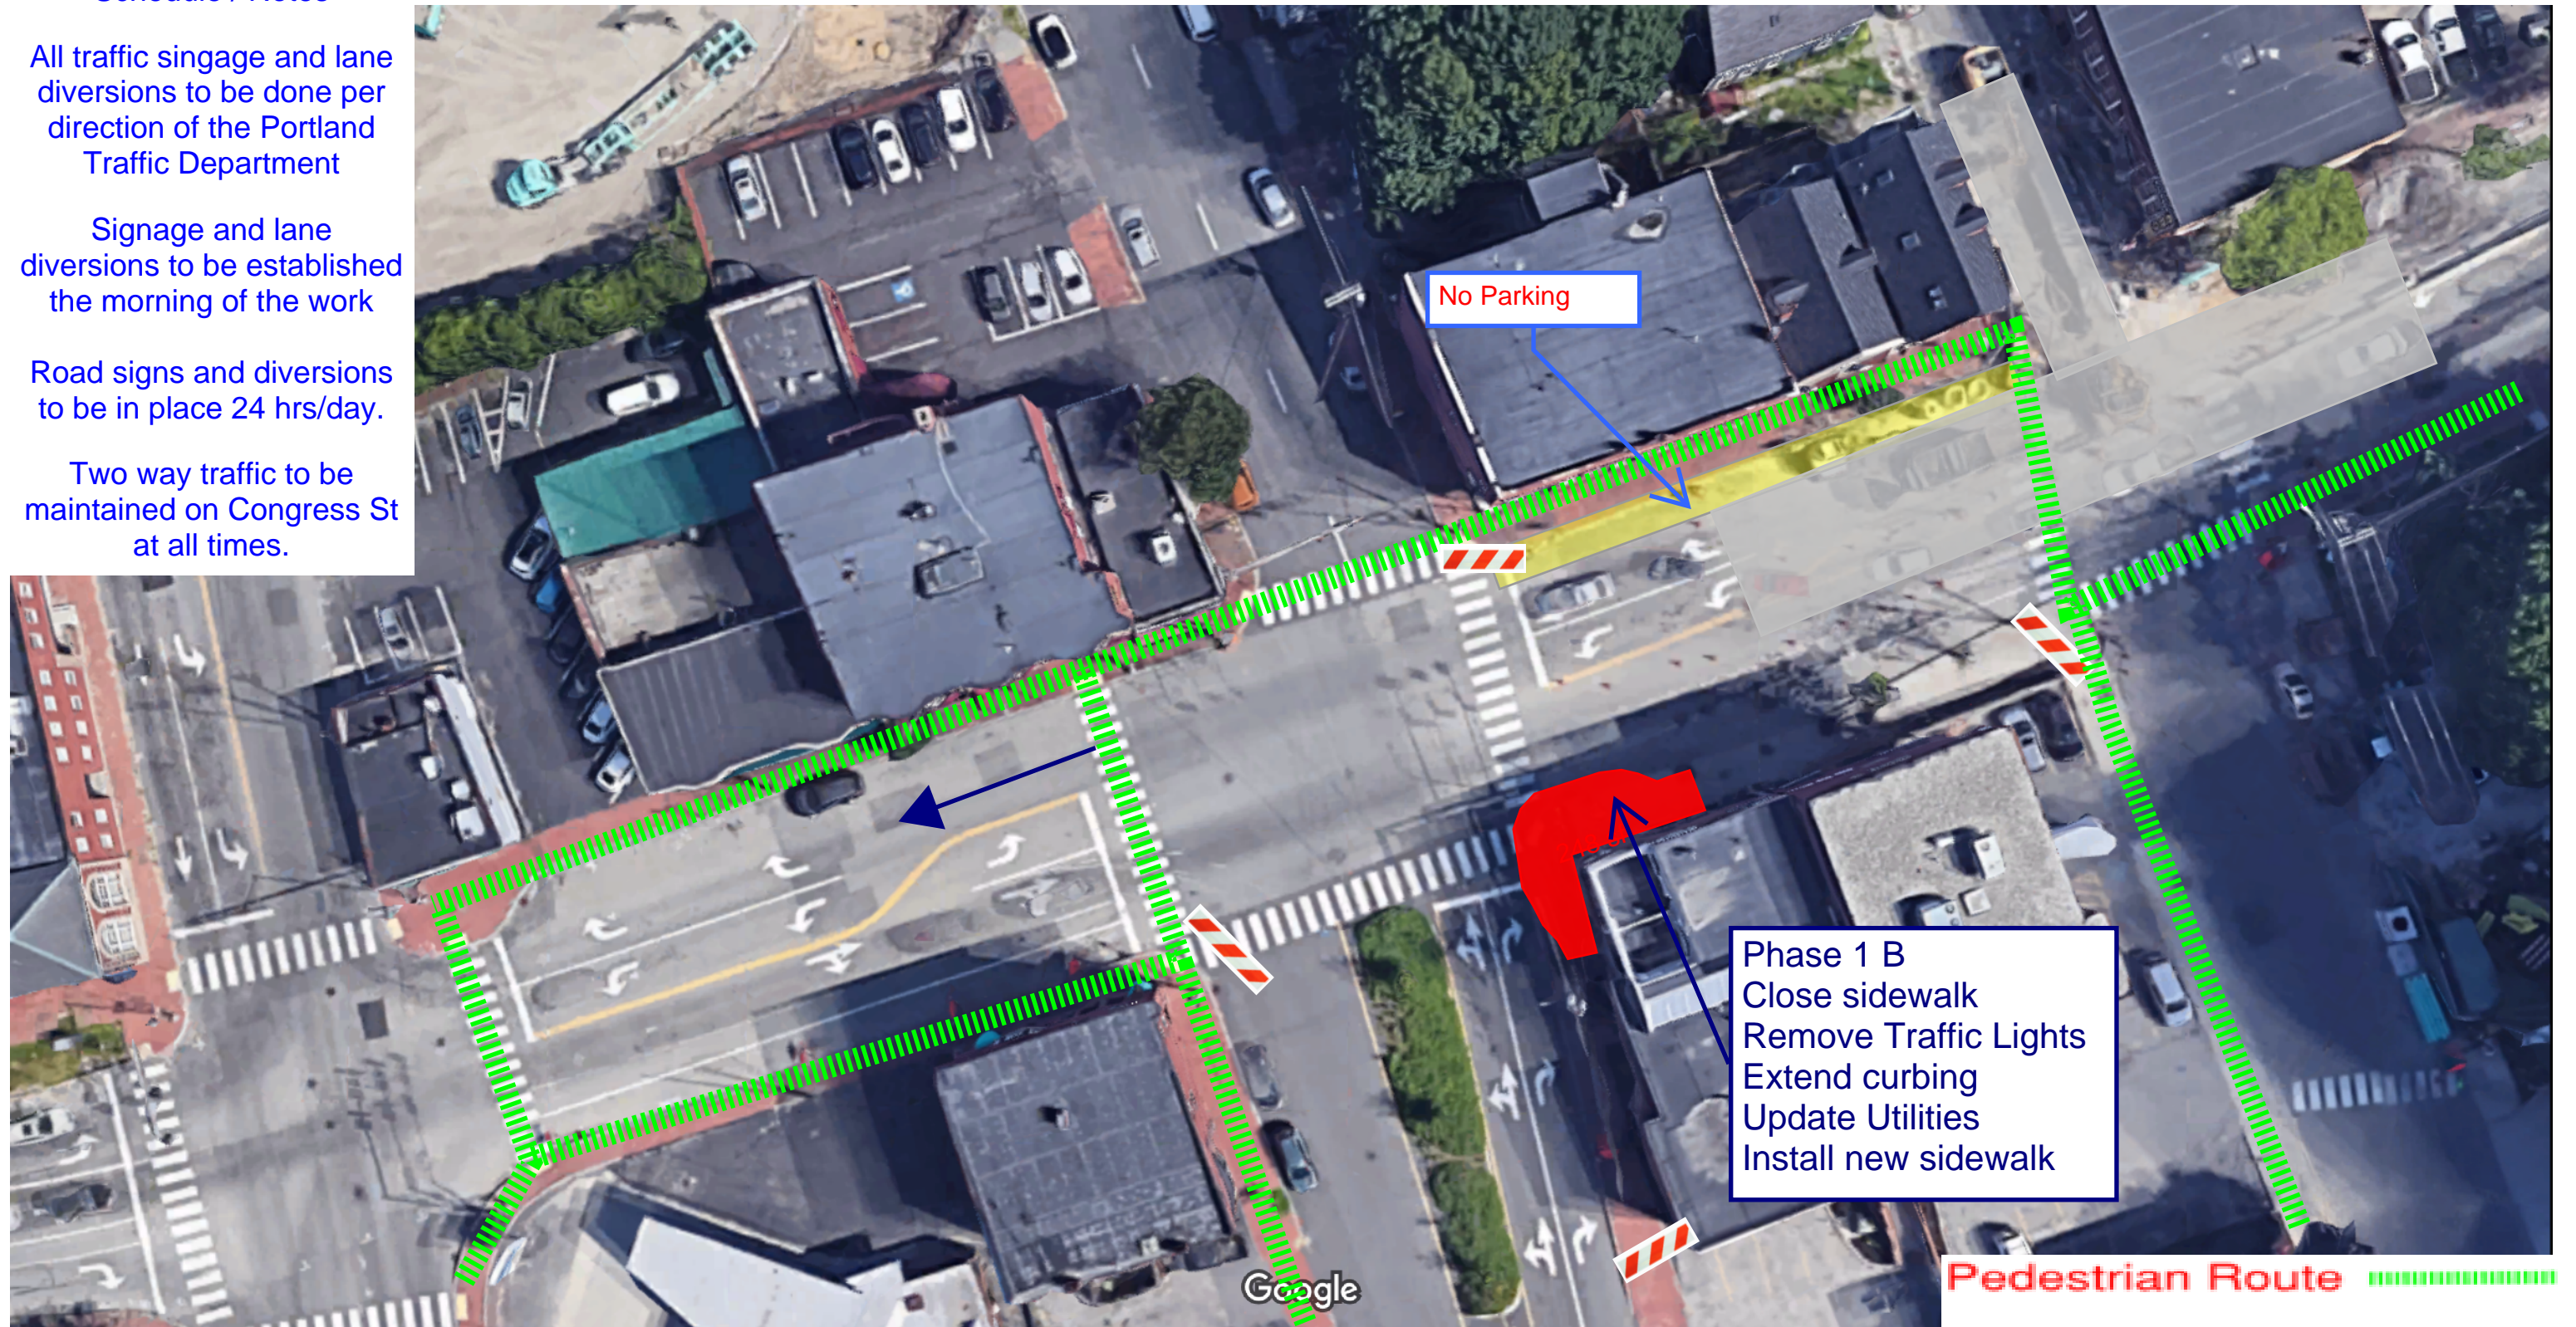

**Pedestrian Route**   
**Sidewalk Closed** 

Valley/Congress Intersection Work



# Phase 2A - Congress St - Outbound

9/28/20 - 10/7/20

### Schedule / Notes

All traffic singage and lane diversions to be done per direction of the Portland Traffic Department

Signage and lane diversions to be established the morning of the work

Road signs and diversions to be in place 24 hrs/day.

Two way traffic to be maintained on Congress St at all times.



Phase 2A  
Close sidewalk  
Remove Traffic Lights  
Extend curbing  
Update Utilities  
Install new sidewalk

Google

Pedestrian Route

Sidewalk Closed

# Phase 2B - Congress St - Outbound 10/8/20 - 10/14/20

### Schedule / Notes


All traffic singage and lane diversions to be done per direction of the Portland Traffic Department

Signage and lane diversions to be established the morning of the work

Road signs and diversions to be in place 24 hrs/day.

Two way traffic to be maintained on Congress St at all times.

Phase 2B  
Close sidewalk  
Remove Traffic Lights  
Extend curbing  
Update Utilities  
Install new sidewalk

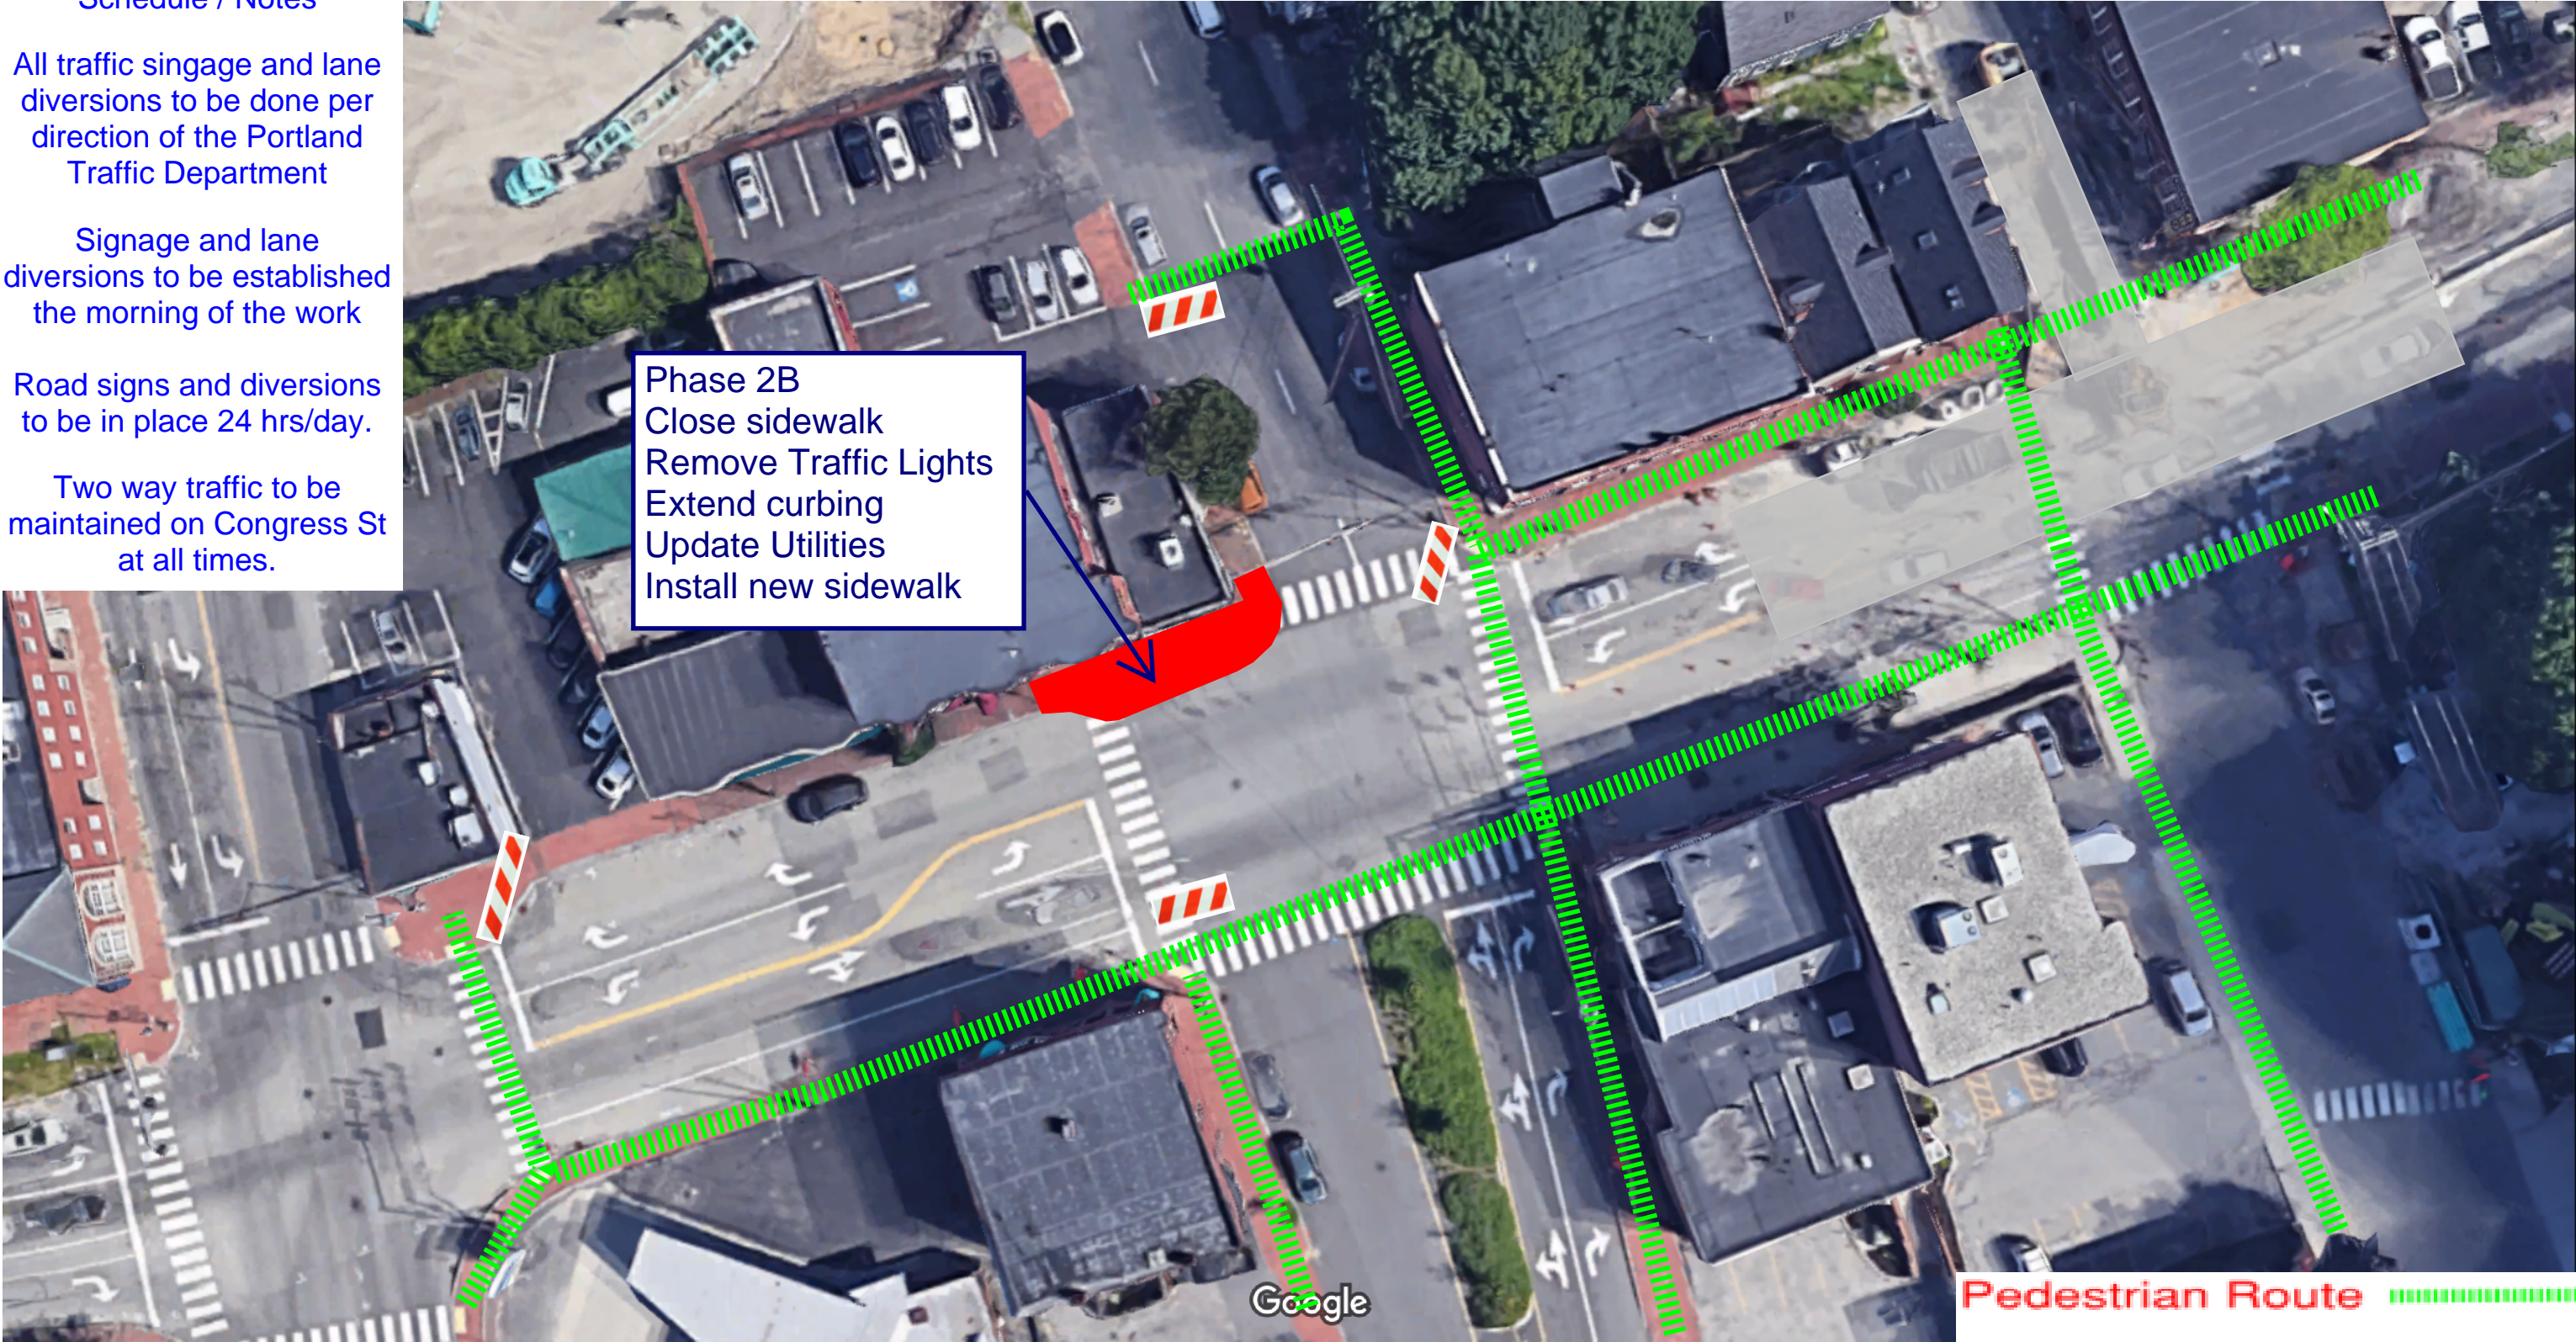

Pedestrian Route 

Sidewalk Closed 

# Phase 3 - Congress St/Valley Intersection 10/15/20-10/23/20

## Schedule / Notes

All traffic singage and lane diversions to be done per direction of the Portland Traffic Department

Signage and lane diversions to be established the morning of the work

Road signs and diversions to be in place 24 hrs/day.

Two way traffic to be maintained on Congress St at all times.



Complete new line striping work per plans this area. Utilize flagmen for traffic control during striping work.

Imagery ©2020 Google, Map data ©2020 50 ft

## Valley/Congress Intersection Work

