


Contact Name: Joe Petruska
 Company: Sprinkler Systems, Inc.
 Tel: (207) 689-9927
 Email: joe@sprinklersystemsinc.com

Flow Hydrant: POD-HYD00051
 Static: 110 psi
 Pitot: 48 psi
 Flow: 1162 GPM

Test Hydrant: POD-HYD11998
 Static: 110 psi
 Residual: 102 psi

DATE: 10/06/2015
 TIME: 6:35 AM
 TESTED BY: JL / JK
 SERV REQ #: 348543
 A-SPAS WO #: 869088
 HY-TEST WO#: 869978

TWO HYDRANT FLOW TEST

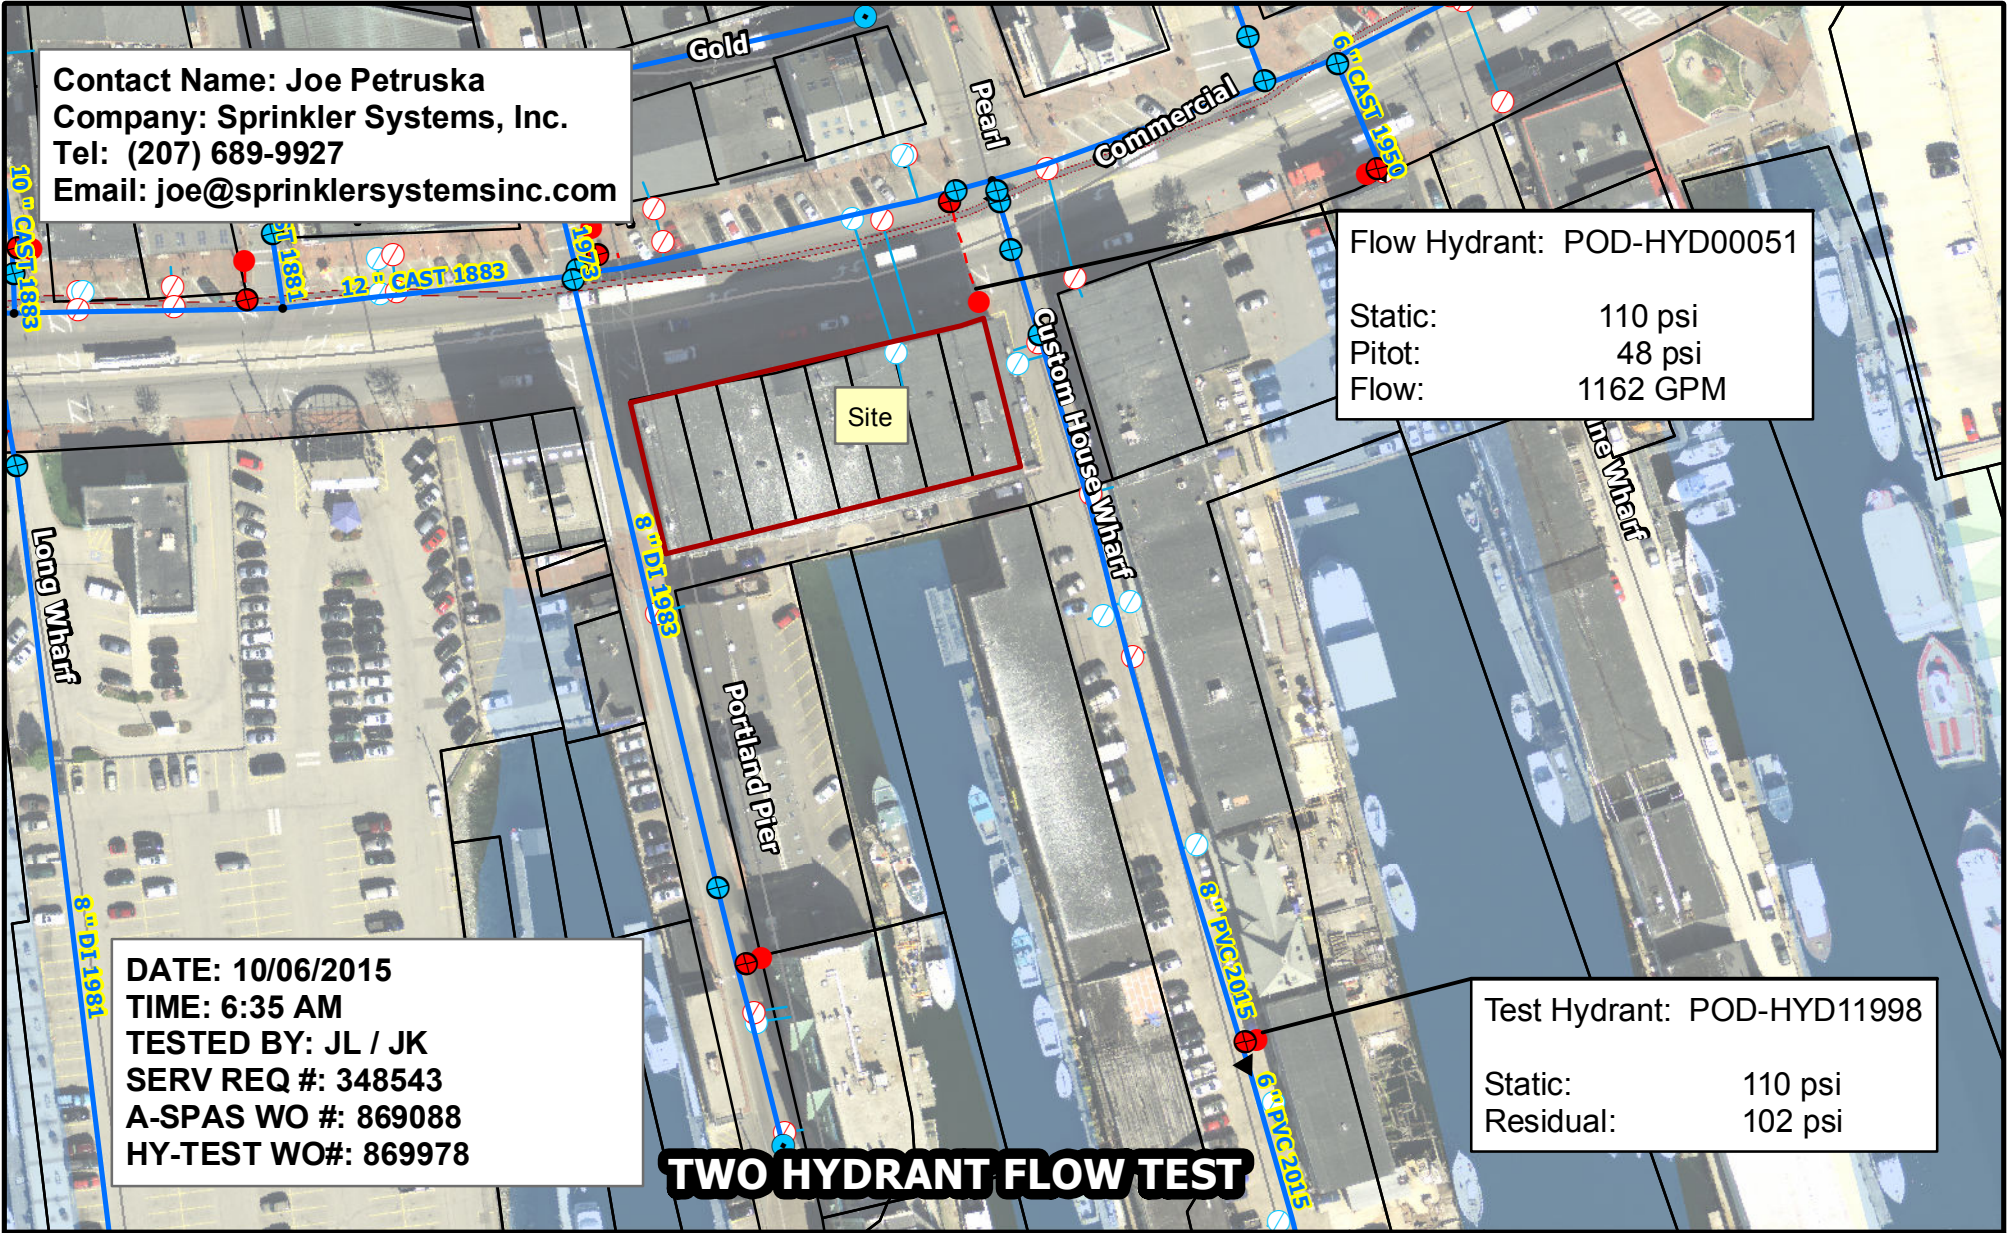

100 Commercial Street
 Portland

Scale 0 50 100 150 200 Feet 1 inch = 100 feet



Disclaimer: This map is suitable for preliminary study and analysis and is based on PWD record information. PWD is not liable for any damages whatsoever resulting from inaccurate data or from errors made in the location and marking of its infrastructure.



PORTLAND WATER DISTRICT
 225 Douglass Street
 PO Box 3553
 Portland, ME 04104
 Telephone: (207) 774-5961
 Fax: (207) 761-8307

Legend

- | | | | |
|----------------|--------------------|--------------------|-----------|
| ● Air Valve | ● Connection | ⊕ Combined Service | ● Manhole |
| ⊕ Blow Off | ● Attribute Change | ⊕ Domestic Service | ● CSO |
| ⊕ By Pass | ▲ Reducer | ⊕ Fire Service | → Gravity |
| ⊕ Distribution | ● Hydrant | ● Private Hydrants | → Force |
| ⊕ Transmission | ● Hydrant Control | ⊕ Meter Pits | |

Drawn By: HAS

Prepared for: Joe Petruska
 Sprinkler Systems, Inc.

Test Fee:

Date: October 6, 2015
