


Salvation Army Preble Street Construction Management Plan

Duration of Project

- Benchmark will maintain existing fencing highlighted in green through construction. This fence will be used with gates for access and egress to the work area.
- Benchmark will install temporary fencing for the duration of construction as shown in red. This fencing will encompass part of the sidewalk along Preble St.
- In order to maintain a safe walk path on Preble St., where pedestrians do not need to cross the road, Benchmark will install jersey barriers along side the fenced area to create a temporary sidewalk. This sidewalk will be a minimum of 5' wide and will have an ADA (1"/1' slope) tip down ramp constructed from wood or asphalt to address the elevation change from the sidewalk to the street level. The location of the barriers is shown with a pink line. Benchmark will leave both travel lanes open which head into town. Benchmark will pay to close the parking meters in this zone and will establish the sidewalk within the parking area. This will allow sidewalks to remain open throughout construction on both sides of the roadway.

Temporary Activities

- Benchmark will need to close part of Preble Street for utility ties ins and abandonments. It is anticipated the closure work last no more than 1 week.
- Benchmark will use traffic cones and signage along with police detail during this time frame.
- Preble Street will remain open and we will not close down the road.
- The orange line indicates the existing dashed white lane split where we will use traffic cones. Our work will take place on one side of the orange line at a time thus allowing the alternate side to remain open for traffic.
- The yellow line indicates how traffic cones will be laid out to shut off specific lanes. A Police detail will also be used. Only one side will have cones up at any given time to allow for the opposite side to remain open to traffic. We will complete work on one side and then move to the other side and re-open the lane which was shut down.
- When working on the side opposite the jobsite there is one parking meter Benchmark will need to purchase a meter bag for. This should be for no more than two days.

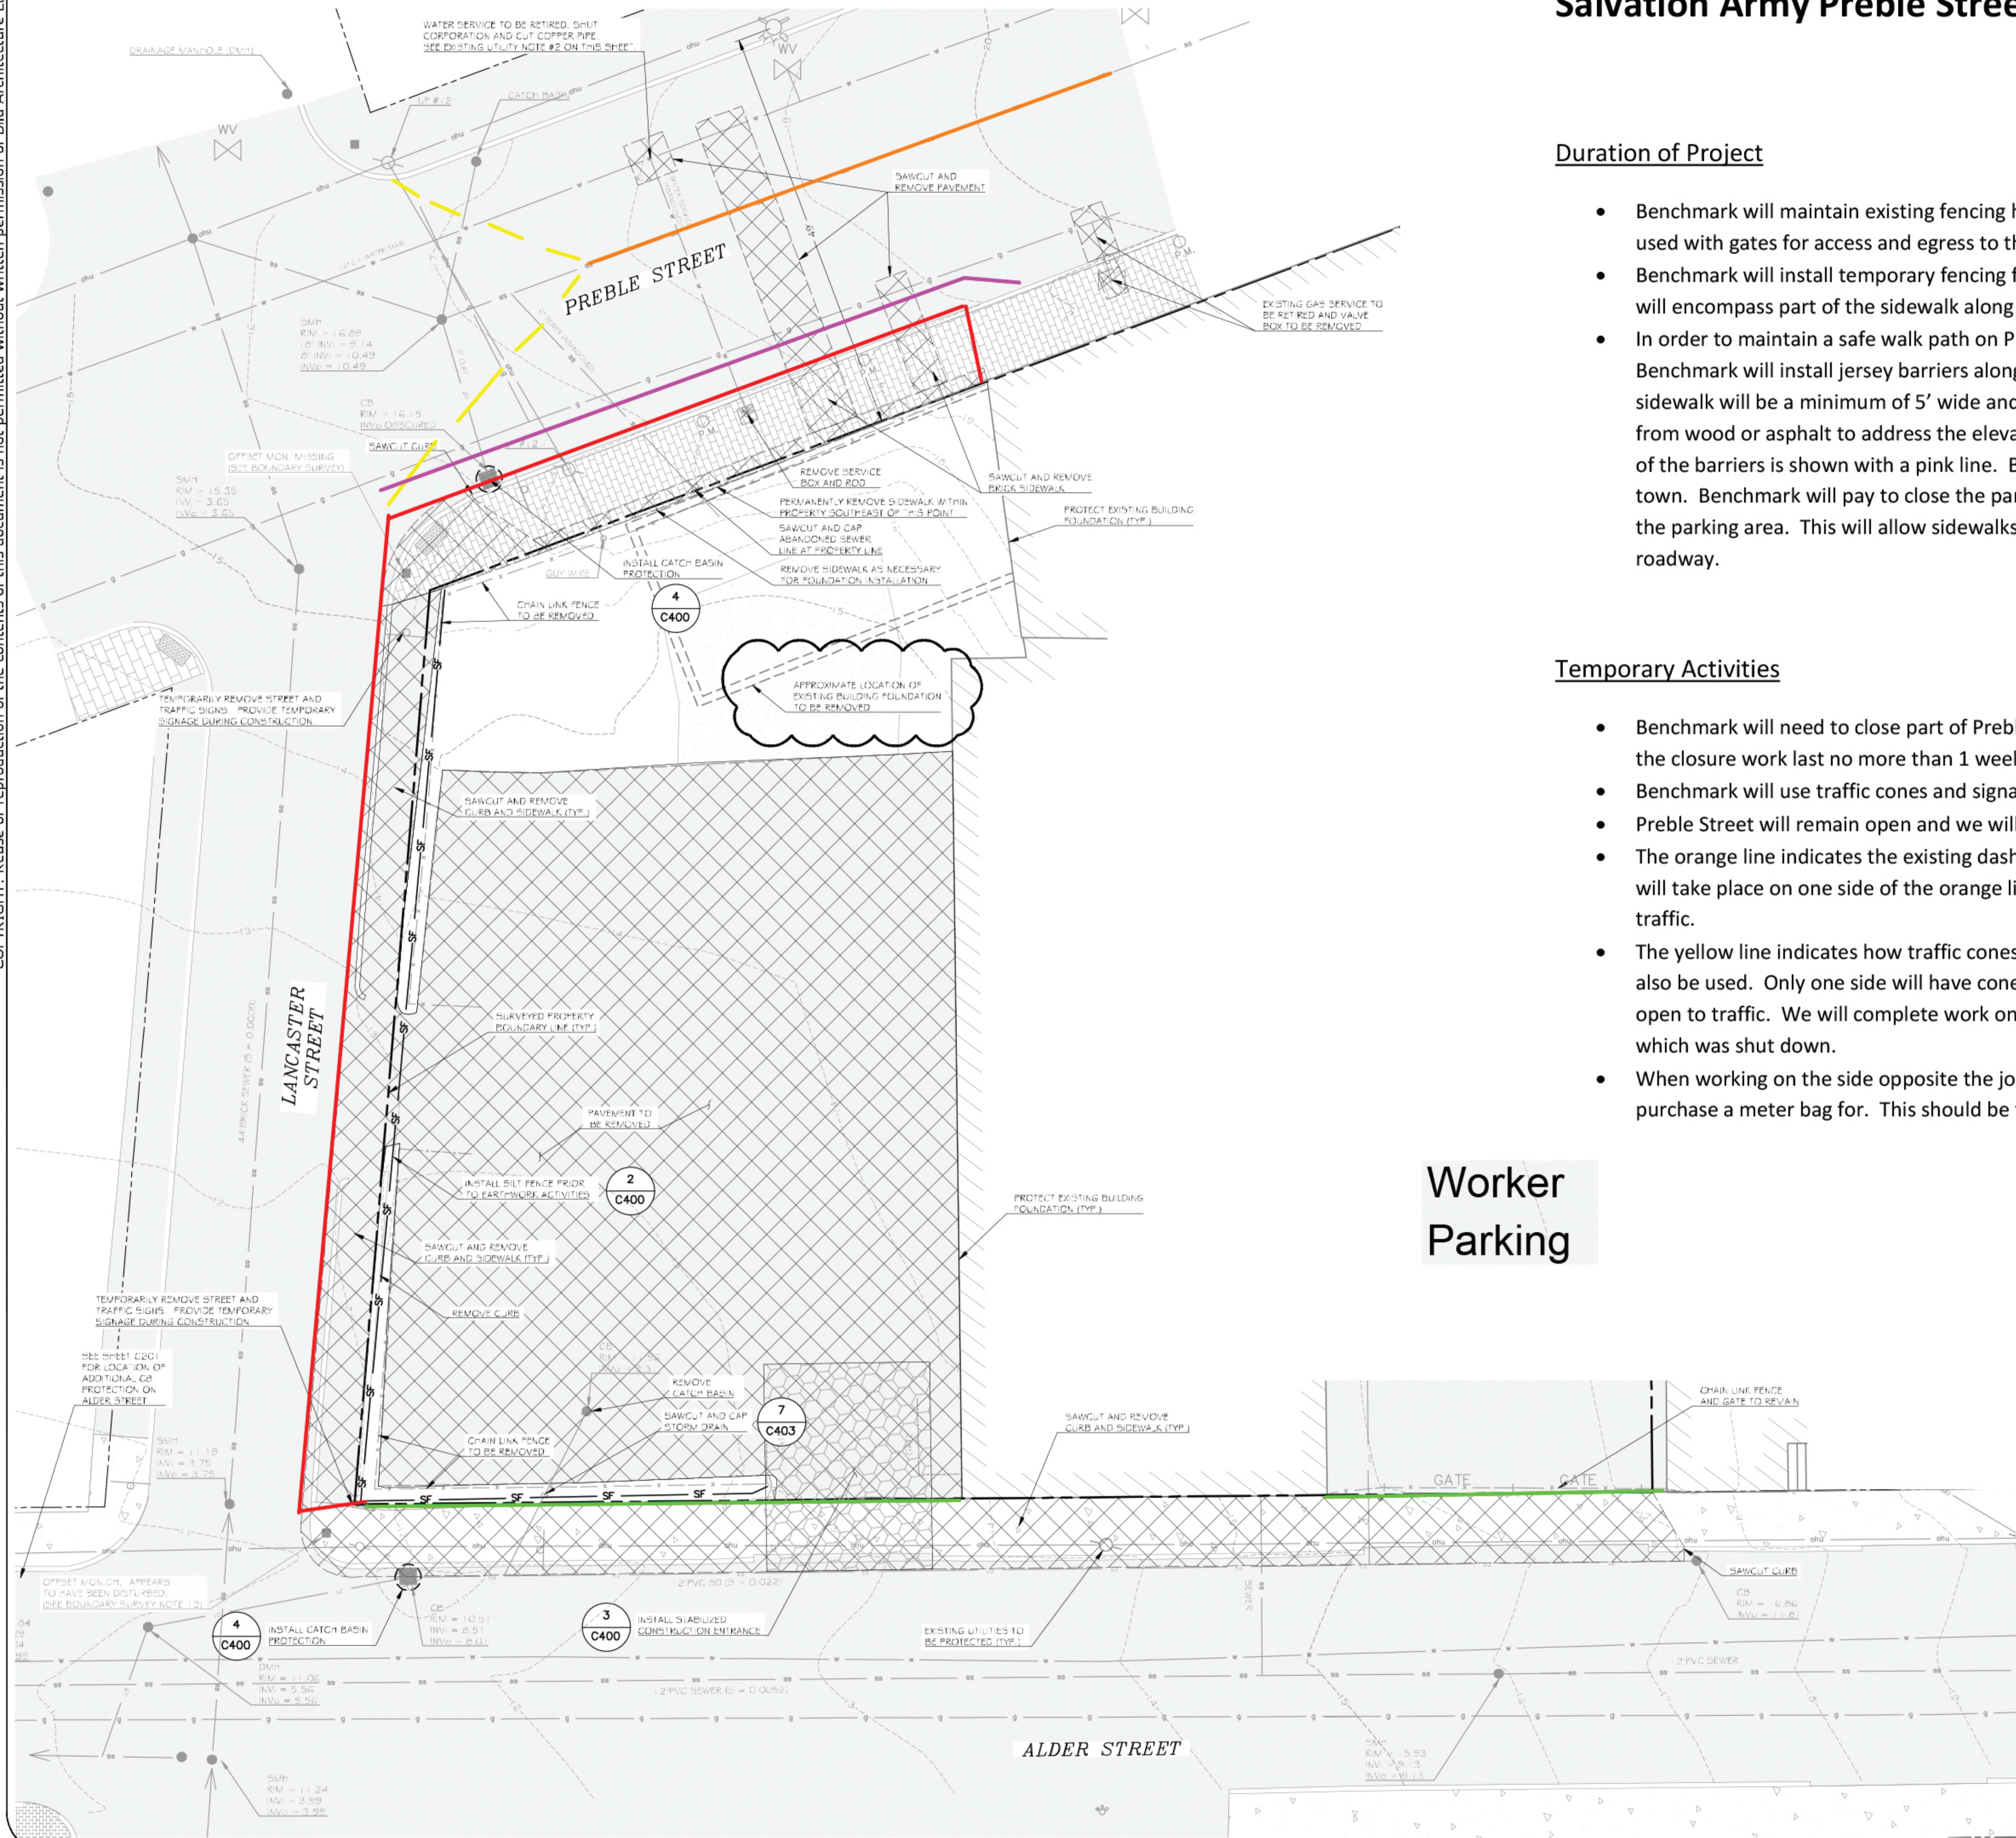

Worker
Parking
