


facsimile transmittal

To: Chris Briley **From:** Mike Nugent
Fax: 773-0194 **Date:** January 2, 2003
Phone: 775-6141 **Pages:** 1
Re: St. Dom's 044 H004

Urgent For Review Please Comment Please Reply Please Recycle

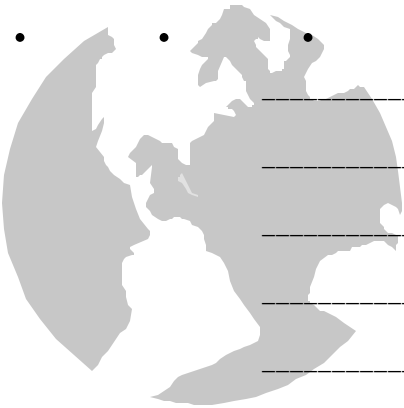

A statement on special inspections pursuant to Section 1705 of the Building Code is required for certain elements of this project. This statement must be filed for review prior to approval.

I have completed the initial review and have the following questions/comments:

- 1) The vertical shaft is required to have a 2-hour fire separation assembly (710.3 BOCA).
- 2) What is the Fire rating of column detail 1 on page A-1-12?
- 3) I assume fire dampers for the bathroom vents fire partition penetrations are omitted pursuant to Section 714.1.5.2.1.
- 4) Are there details or specs that accompany the fire assembly penetration language on the Floor/Ceiling assembly pages?
- 5) What type of fire suppressions system is to be used?
- 6) What are the sound transmission ratings of all tenant separation assemblies?
- 7) What is the access ladder for on page A-4-2
- 8) Does the Clothes dryer exhaust penetrate the fire separation assembly? Also, materials, cleanouts etc?
