

SUBSURFACE WASTEWATER DISPOSAL SYSTEM APPLICATION

Meine Department of Human Services
Division of Health Engineering, Station 10
(207) 287-5672 Fax: (207) 287-3165

Town, City, Plantation
Portland (Cliff Island)


Street, Road, Subdivision
37 Wharf Road

Owner or Applicant Name
Andrew McDonald

Existing Grade Elevations
-46" -57"
-46" -57"
FIELD CORNERS

SUBSURFACE WASTEWATER DISPOSAL PLAN

Scale: 1" = 20' ft

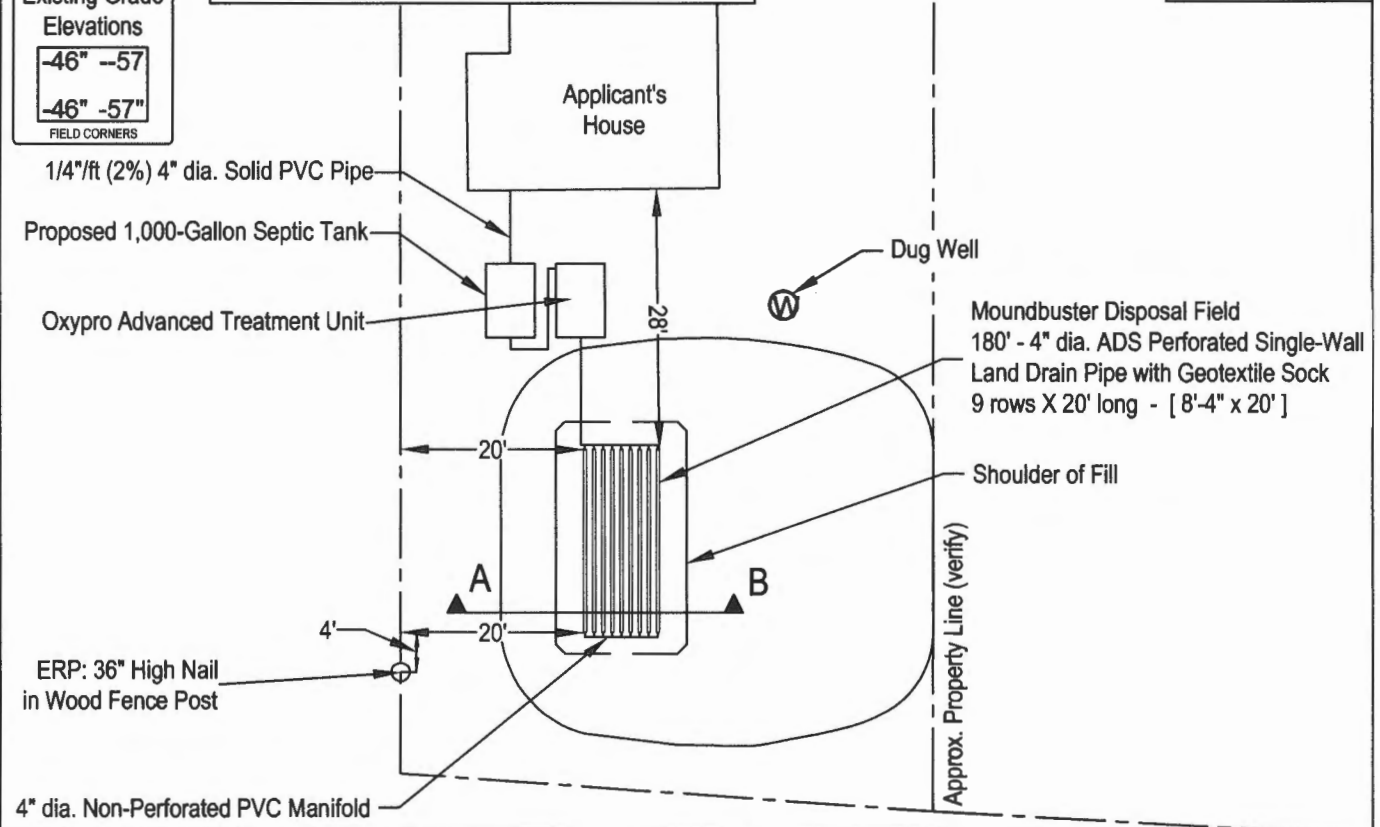

BACKFILL REQUIREMENTS

Depth of Backfill (upslope) 24-24"
Depth of Backfill (downslope) 35-35"

CONSTRUCTION ELEVATIONS

Finished Grade Elevation (at Row 1) -27"
Top of Proprietary Device (at Row 1) -35"
Bottom of Disposal Field (at Row 1) -39"

ELEVATION REFERENCE POINT

Location & Description: 36" High Nail in Wood Fence Post
Reference Elevation is 0.0" or: _____


NOTE: Backfill 3 feet beside and 6 inches below system must meet the following gradation portion of the Code.
Less than 80% passing the #10 sieve
Less than 30% passing the #40 sieve
Less than 4% passing the #200 sieve

DISPOSAL FIELD CROSS SECTION

ROW #1 to 9
TOP -35"
BOTTOM -39"

TOP OF ROW #1 INLET AT -30"

Scales:
Verticle: 1" = 5'
Horizontal: 1" = 5'

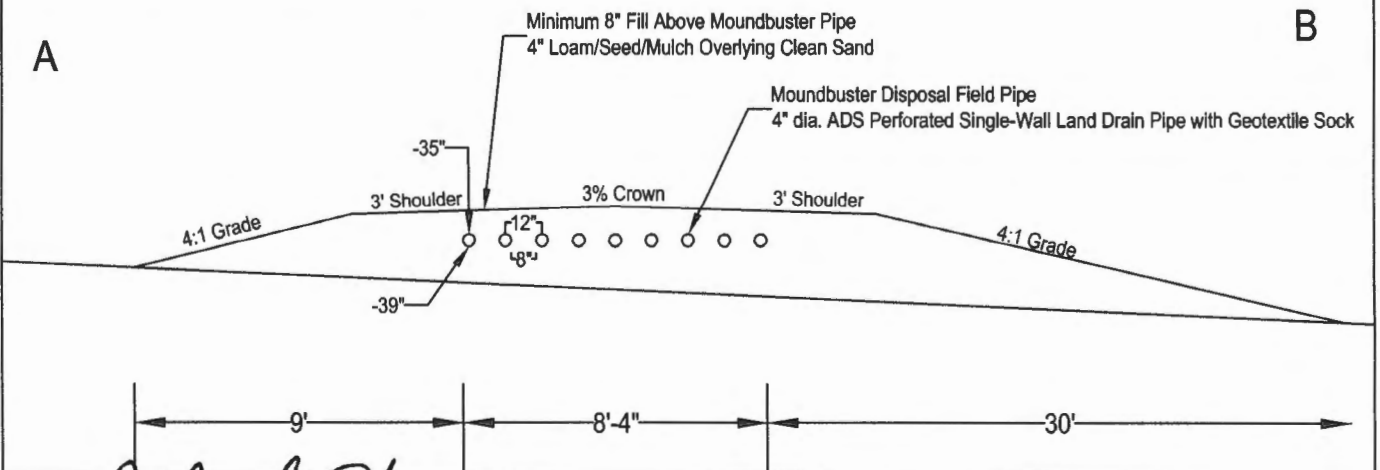

Richard Summit
Site Evaluator Signature

034
SE #

01/06/15
Date

Page 3 of 3
HHE-200 Rev. 2/11
