


Project Name PORTLAND - THE INN AT CEDARS - MATERIALS TESTING
 Client THE OSHER INN AT CEDARS
 Material Type STRUCTURAL FILL
 Material Source INPLACE/PORTLAND S&G DRAINAGE-STON

Project Number 07-0503
 Lab ID 7106G
 Date Received 7/13/2007
 Date Completed 7/17/2007
 Tested By JUSTIN BISSON

<u>STANDARD</u> <u>DESIGNATION (mm/um)</u>	<u>SIEVE SIZE</u>	<u>AMOUNT PASSING (%)</u>	<u>07-0503 COMPACTED STRUCTURAL FILL</u> <u>SPECIFICATIONS (%)</u>
150 mm	6"	100	
125 mm	5"	100	
100 mm	4"	100	
75 mm	3"	100	100
50 mm	2"	100	
38.1 mm	1-1/2"	100	
25.0 mm	1"	100	
19.0 mm	3/4"	100	
12.5 mm	1/2"	100	
6.3 mm	1/4"	90	
4.75 mm	No. 4	86	30 - 90
2.00 mm	No. 10	69	
850 um	No. 20	41	
425 um	No. 40	20	10 - 50
250 um	No. 60	11	
150 um	No. 100	6	
75 um	No. 200	3.7	0.0 - 8.0

SAMPLE MEETS SPECIFICATION

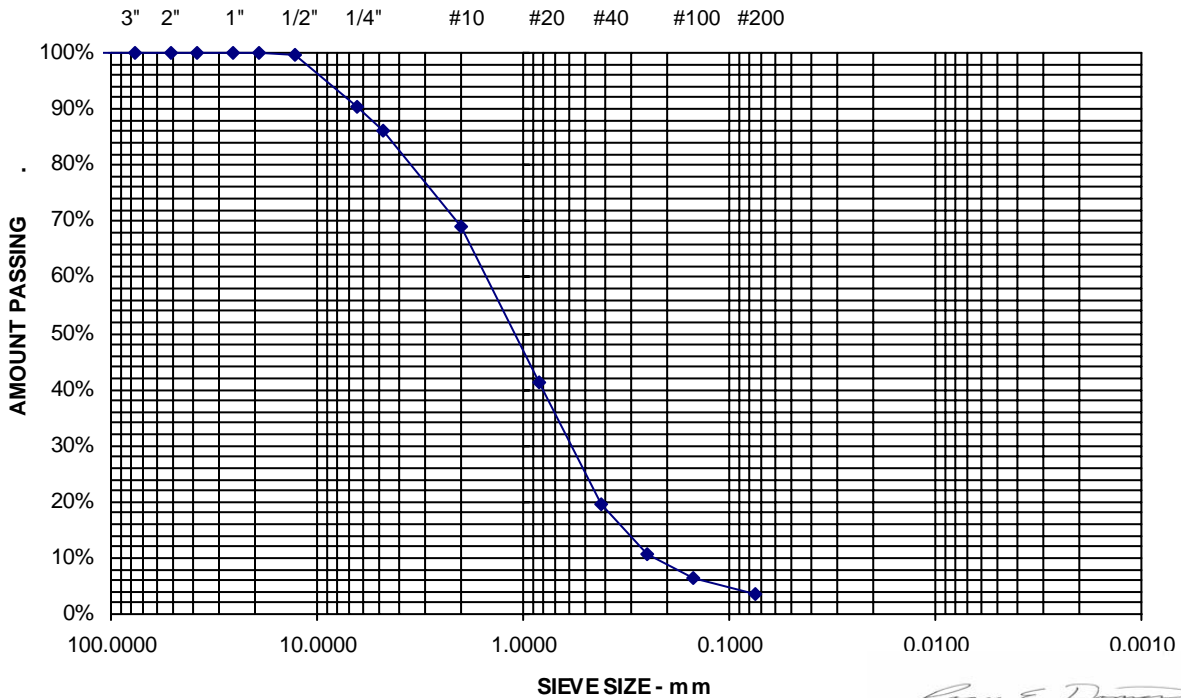

Roger E. Domingo

Comments

Roger E. Domingo
