


Hello Scott,

Following are comments on the Rammed Aggregate Pier (RAP) submittal for Seaside:


- 1) Add Grouted and Ungrouted RAPs at locations shown on attached plan
- 2) Add load tests at Grouted RAP 59 and Ungrouted RAP 203
- 3) Submit PL insurance certificate specific to the project
- 4) Submit lab test results for gradation and internal friction angle of aggregate for ungrouted RAPs
- 5) Submit mix design and batch method for grouted RAPs

Regards,



Tim Boyce, P.E. | Senior Geotechnical Engineer
S. W. Cole Engineering Inc.
286 Portland Road
Gray, Maine 04039
Phone: 207.657.2866



Lisa R. Caselli
12-7-12



John S. Linscott IV
12/7/12

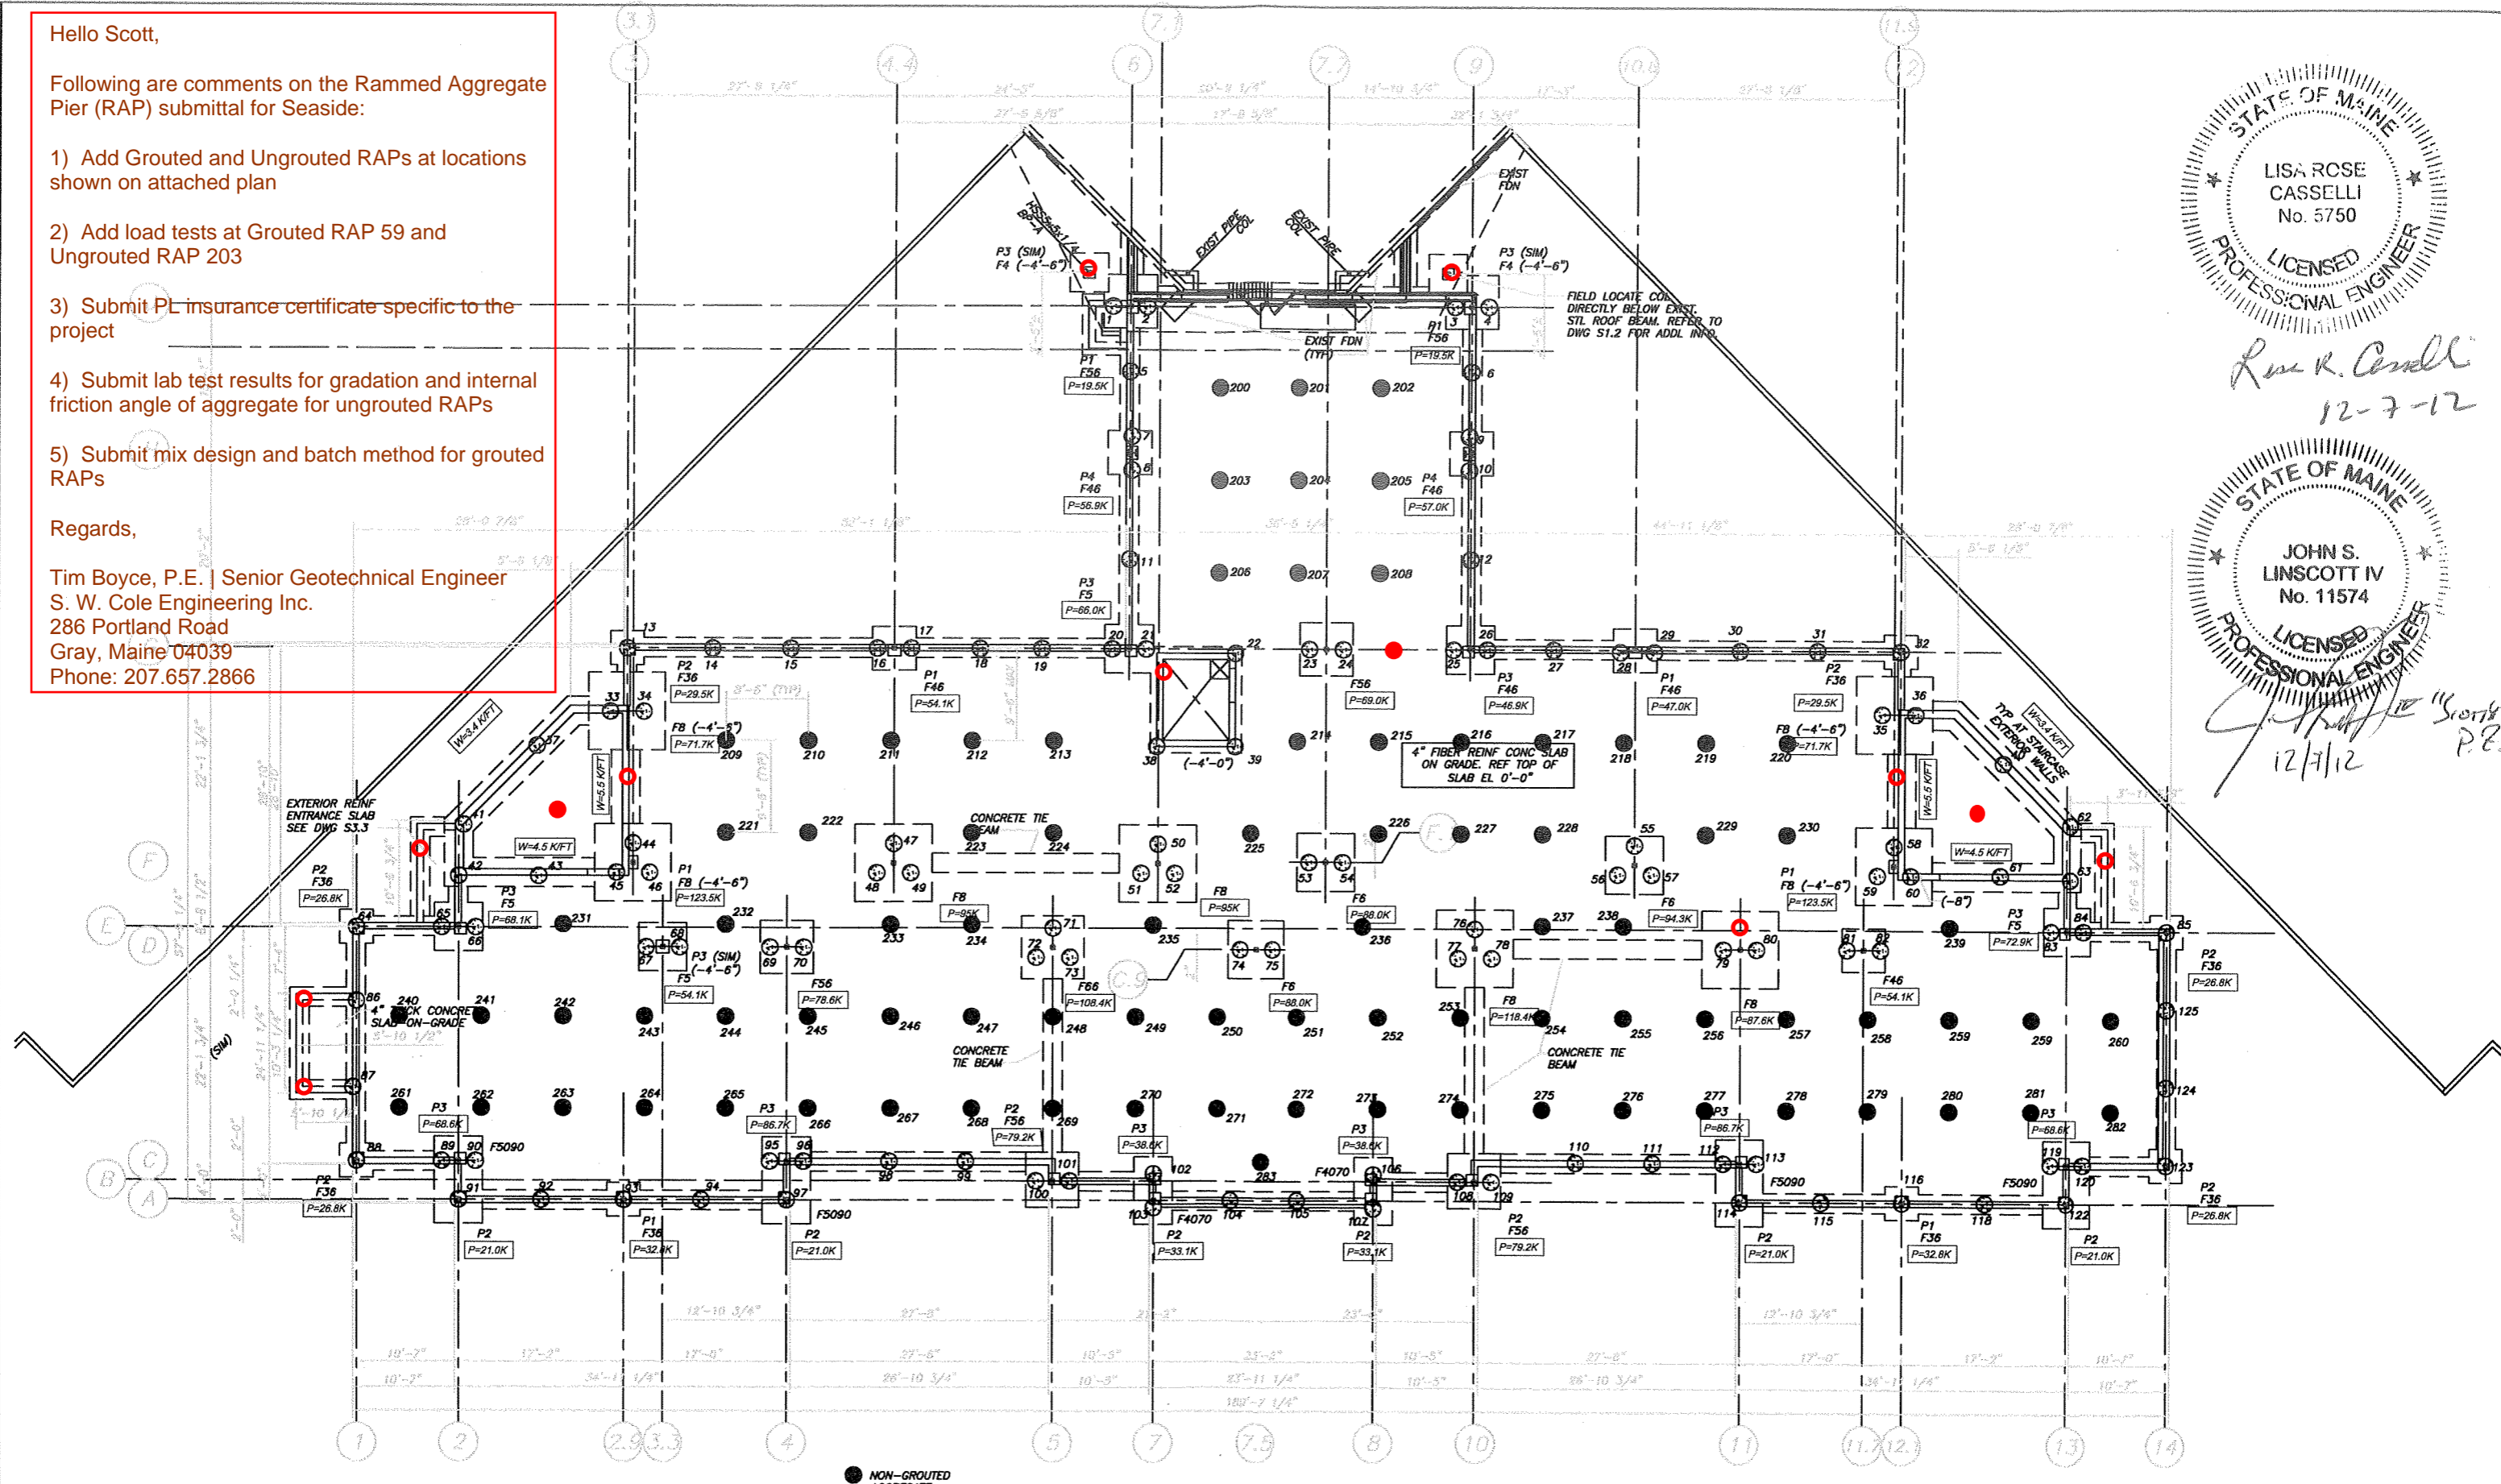

H.B. FLEMING
89 PLEASANT AVENUE
SO. PORTLAND, ME 04106
P: 207-799-8514 F: 207-799-8538
www.hbfleming.com

TITLE: AGGREGATE PIER PLAN
PROJECT: SEASIDE REHABILITATION
LOCATION: PORTLAND, ME
DATE: 12/7/2012
SCALE: AS NOTED
