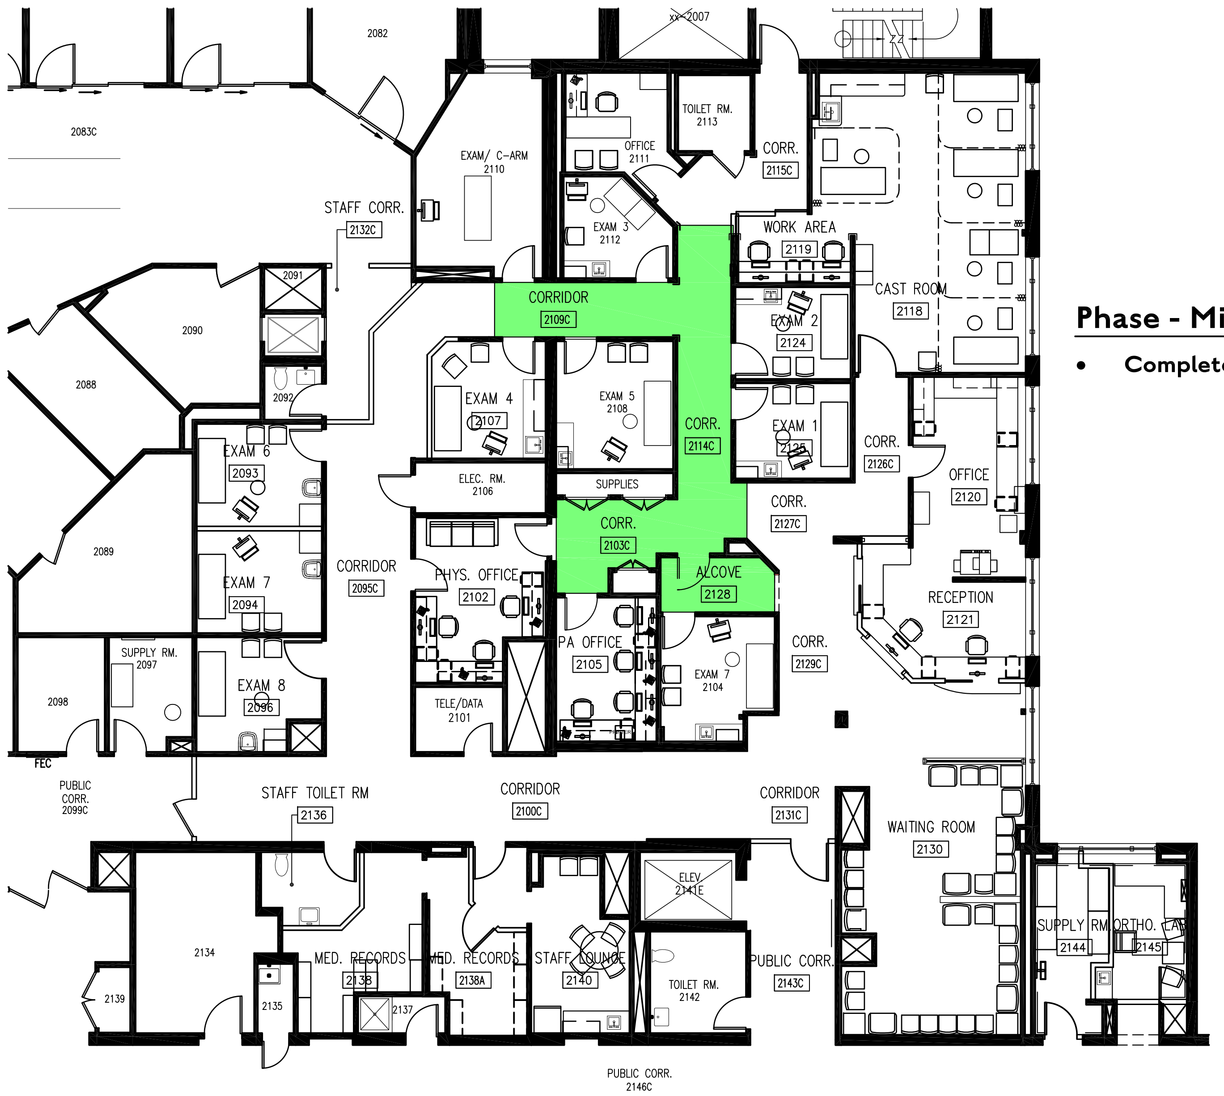

4 PHASE MISC. WORK
1/8" = 1'-0"

Phase - Misc.

- Complete Corridor finishes

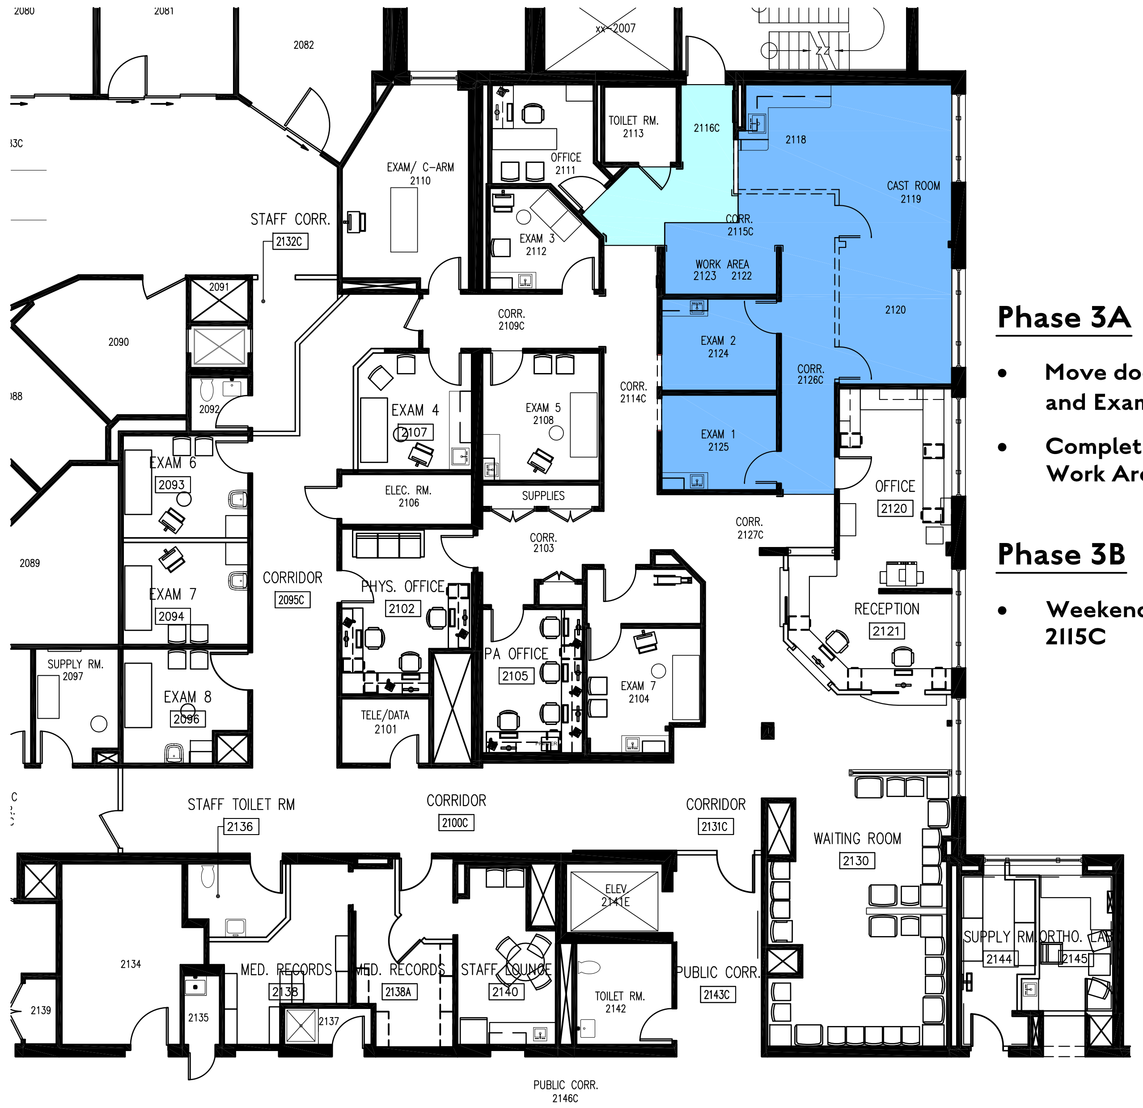

3 PHASE 3A & 3B
1/8" = 1'-0"

Phase 3A

- Move doors in Exam 1 (2125) and Exam 2 (2124)
- Complete Cast Room 2118 and Work Area 2119

Phase 3B

- Weekend work in Corridor 2115C

LEGEND:

- PHASE 1A
- PHASE 1B
- PHASE 2A
- PHASE 2B
- PHASE 3A
- PHASE 3B WEEKEND
- PHASE MISC. WORK

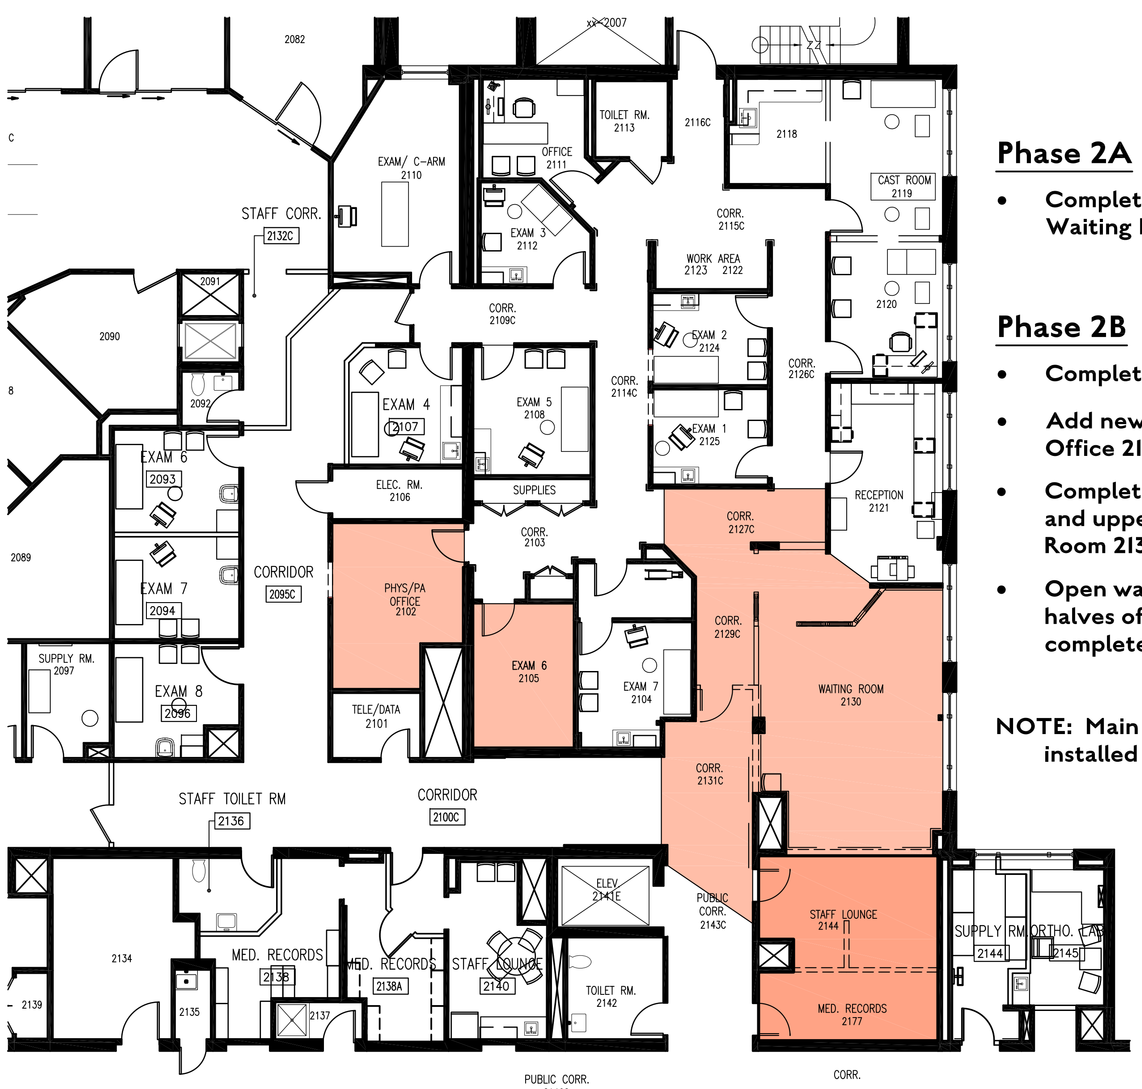

2 PHASE 2A & 2B
1/8" = 1'-0"

Phase 2A

- Complete lower half of Waiting Room 2130

Phase 2B

- Complete PA Office 2105
- Add new door at Physician Office 2102
- Complete Reception 2121 and upper half of Waiting Room 2130
- Open wall between two halves of Waiting Room and complete finishes

NOTE: Main entrance will be installed after hours.

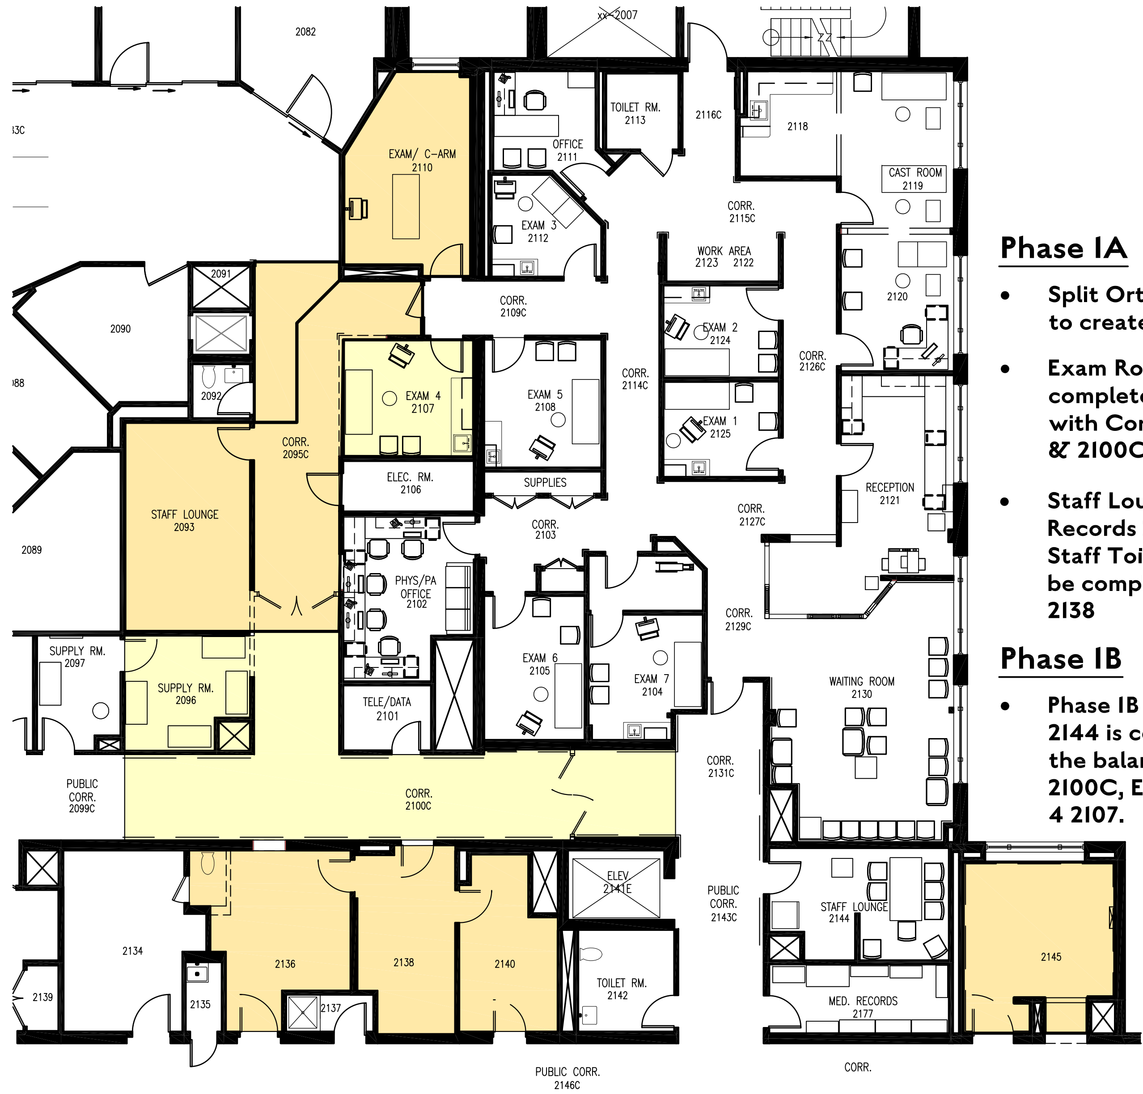

1 PHASE 1A & 1B
1/8" = 1'-0"

Phase 1A

- Split Orthotics № 2145 in half to create new Supply Room
- Exam Rooms 6 & 7 will be completed in conjunction with Corridors 2109C, 2095C & 2100C
- Staff Lounge 2140, Med. Records 2138-2138A and Staff Toilet Room 2136 will be completed from inside 2138

Phase 1B

- Phase 1B will start after Supply 2144 is complete and include the balance of Corridor 2100C, Exam 8 2096 and Exam 4 2107.

PLAN N

PDT ARCHITECTS
49 DARTMOUTH STREET
PORTLAND, MAINE 04101
207-775-1059
www.pdtarchs.com

COPYRIGHT 2012
PDT Architects
Reuse or reproduction of the contents of this document is not permitted without written permission of PDT Architects.

MMP - ORTHOPEDIC TRAUMA & FRACTURE CARE

BRIGHTON CAMPUS, PORTLAND, MAINE

JOB NO. 12-110

DRWN. CHK

SCALE: AS NOTED

ISSUE PROGRESS DECEMBER 6, 2012

TITLE PHASING PLAN

SHEET G1.0

Wednesday, December 12, 2012 10:36:37 AM BRIDGTON ANN
H:\MASTER PROJ FILES2\MMP - 12110 - ORTHO TRAUMA\12110 -WORKING FILES\CAD\CDS\12110-MMC-BMC SECOND-PHASING-.DWG
