Main Line Fence

Waiting on Permit

32

Work Order

Terri 773-8414

MATERIALS

USED	TAKE
	13 - Panels 8' stockade
	1 - 8' to 6' sloped panel
	14 - 12' round posts
	1 - end
	13 - lines
	1 - 10' round end post
	2" SS20 pipe 8' long
	3 - 2" Rail Bands
	1 - 2" Rail End

Date: 3/13/17

Project: Shirley Stewart
433 Capisic Street
Portland, Maine 04102

Subject: ~~112~~ 104' of 8' stockade

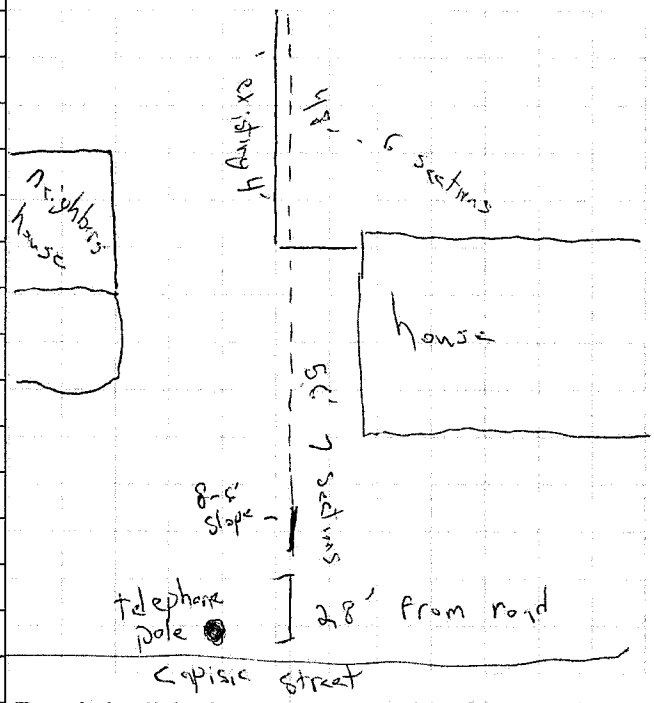

Don't build slope yet not 100% which way fence will face.

Fence will be placed right up against existing 4' chain link, they own it and want to leave it. It will also run through part of the chain link fence We will detach and drive new post for hook up to close off again.

She wants to run fence as close to road as possible needs to be 25' away

Salesman: ***Andrew Davenport***

Work Order Completed **Date:** _____

By: _____
